ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - **All Tasks**

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1	**5041 - ARC BOWDEN APARTMENTS PROJECT**	**52%**	**491 days**	**Mon 18/11/24**	**Tue 13/10/26**
2	**KEY MILESTONES**	**0%**	**449 days**	**Thu 23/01/25**	**Tue 13/10/26**
18	**OFF SITE WORKS**	**78%**	**427 days**	**Mon 18/11/24**	**Tue 21/07/26**
1023	**ON SITE WORKS**	**17%**	**459 days**	**Tue 19/11/24**	**Mon 31/08/26**
1024	**SITE ESTABLISHMENT**	**100%**	**54 days**	**Sat 15/01/25**	**Mon 31/03/25**
1025	**SITE CLEARANCE**	**100%**	**17 days**	**Fri 17/01/25**	**Sat 8/02/25**
1030	**CONSTRUCTION (EARLY WORKS)**	**100%**	**102 days**	**Mon 17/02/25**	**Sat 5/07/25**
1046	**SUPERSTRUCTURE**	**68%**	**185 days**	**Mon 14/07/25**	**Mon 13/04/26**
1047	**LEVEL 1 - 2,200m2 CARPARK**	**100%**	**30 days**	**Mon 14/07/25**	**Thu 28/08/25**
1048	**Zone A**	**100%**	**20 days**	**Mon 14/07/25**	**Thu 7/08/25**
1049	SA Water fire main installation	100%	1 day	Fri 18/07/25	Fri 18/07/25
1050	Precast Concrete install (A+B)	100%	6 days	Mon 14/07/25	Sat 19/07/25
1051	Ground floor column pour	100%	1 day	Tue 15/07/25	Tue 15/07/25
1052	Ground floor strip columns	100%	1 day	Wed 16/07/25	Wed 16/07/25
1053	Bubbledeck false work	100%	5 days	Tue 15/07/25	Sat 19/07/25
1054	Bubbledeck installation ZONE (A)	100%	6 days	Thu 24/07/25	Thu 31/07/25
1055	Install scaffold handrail to live deck (pm)	100%	**2 days**	Wed 30/07/25	Thu 31/07/25
1056	Open live deck (pm)	100%	1 day	Thu 31/07/25	Thu 31/07/25
1057	Install (BD) reo	100%	2 days	Fri 1/08/25	Sat 2/08/25
1058	Install screw in bars	100%	1 day	Fri 1/08/25	Fri 1/08/25
1059	Install services	100%	2 days	Fri 1/08/25	Sat 2/08/25
1060	Install setdowns	100%	1 day	Tue 5/08/25	Tue 5/08/25
1061	Concrete pour floor slab Zone [A] pour (1)	100%	1 day	Wed 6/08/25	Wed 6/08/25
1062	Concrete pour floor slab Zone [A] pour (2)	100%	1 day	Thu 7/08/25	Thu 7/08/25
1063	**Zone B**	**100%**	**22 days**	**Wed 23/07/25**	**Tue 19/08/25**
1064	Bubbledeck false work	100%	14 days	Wed 23/07/25	Sat 9/08/25
1065	Bubbledeck installation ZONE (B)	100%	2 days	Mon 11/08/25	Tue 12/08/25
1066	Install scaffold handrail to live deck (pm)	100%	2 days	Mon 11/08/25	Tue 12/08/25
1067	Open live deck (pm)	100%	1 day	Tue 12/08/25	Tue 12/08/25
1068	Install (BD) reo	100%	3 days	Wed 13/08/25	Fri 15/08/25
1069	Install screw in bars	100%	2 days	Wed 13/08/25	Thu 14/08/25
1070	Install services	100%	3 days	Wed 13/08/25	Fri 15/08/25
1071	Install setdowns	100%	1 day	Sat 16/08/25	Sat 16/08/25
1072	Concrete pour floor slab Zone [B] pour (1)	100%	1 day	Mon 18/08/25	Mon 18/08/25
1073	Concrete pour floor slab Zone [B] pour (2)	100%	1 day	Tue 19/08/25	Tue 19/08/25
1074	**LEVEL 2 - 2,200m2 CARPARK**	**100%**	**26 days**	**Thu 7/08/25**	**Thu 25/09/25**
1075	**Zone A**	**100%**	**23 days**	**Thu 7/08/25**	**Fri 5/09/25**
1076	Strip slab edge and set downs - tidy up	100%	1 day	Thu 7/08/25	Thu 7/08/25
1077	Survey - columns set out	100%	**1 day**	Thu 7/08/25	Thu 7/08/25
1078	Survey - as built slab	100%	**1 day**	Thu 7/08/25	Thu 7/08/25
1079	Survey - precast wall panels set out	100%	1 day	Thu 7/08/25	Thu 7/08/25
1080	Survey - Bubbledeck panels set out	100%	1 day	Thu 7/08/25	Thu 7/08/25
1081	Jump the stretcher stairs	100%	3 days	Thu 7/08/25	Sat 9/08/25
1082	Jump the Hoist	100%	1 day	Fri 8/08/25	Fri 8/08/25
1083	Lift column cages	100%	1 day	Thu 7/08/25	Thu 7/08/25
1084	Column cage reo inspection sign off	100%	1 day	Thu 7/08/25	Thu 7/08/25
1085	Lift column formwork	100%	1 day	Thu 7/08/25	Thu 7/08/25
1086	Column formwork install	100%	2 days	Thu 7/08/25	Fri 8/08/25
1087	Pour concrete columns	100%	2 days	Fri 8/08/25	Sat 9/08/25
1088	Strip and remove column form work	100%	1 day	Mon 11/08/25	Mon 11/08/25
1089	Install precast wall panels	100%	7 days	Fri 8/08/25	Fri 15/08/25
1090	Lift BD false work	100%	4 days	Thu 7/08/25	Mon 11/08/25
1091	Install BD false work	100%	9 days	Tue 12/08/25	Thu 21/08/25
1092	BD false work inspection and sign off	100%	1 day	Thu 21/08/25	Thu 21/08/25
1093	Install BD panels	100%	3 days	Fri 22/08/25	Mon 25/08/25
1094	Install scaffold handrail to live deck (pm)	100%	4 days	Fri 22/08/25	Tue 26/08/25
1095	Open Live deck (pm)	100%	1 day	Tue 26/08/25	Tue 26/08/25
1096	Lift BD reo	100%	1 day	Wed 27/08/25	Wed 27/08/25
1097	Install BD reo	100%	1 day	Wed 27/08/25	Wed 27/08/25
1098	Install services	100%	1 day	Wed 27/08/25	Thu 28/08/25
1099	Pre-pour engineer inspections inspections Zone [A]	100%	0 days	Thu 28/08/25	Thu 28/08/25
1100	Install set downs	100%	0 days	Thu 28/08/25	Thu 28/08/25
1101	Concrete pour floor slab Zone [A] pour (1)	100%	0 days	Fri 29/08/25	Fri 29/08/25
1102	Concrete Pour beam + ramp infill Zone [B]	100%	0 days	Fri 29/08/25	Fri 29/08/25
1103	Concrete pour floor slab Zone [A] pour (2)	100%	1 day	Fri 5/09/25	Fri 5/09/25
1104	**Zone B**	**100%**	**26 days**	**Tue 19/08/25**	**Thu 25/09/25**
1105	Strip slab edge and set downs - tidy up	100%	1 day	Tue 19/08/25	Tue 19/08/25
1106	Survey - columns set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1107	Survey - as built slab	100%	1 day	Tue 19/08/25	Tue 19/08/25
1108	Survey - precast wall panels set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1109	Survey - Bubbledeck panels set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1110	Jump the stretcher stairs	100%	1 day	Tue 19/08/25	Tue 19/08/25
1111	Lift column cages	100%	1 day	Tue 19/08/25	Tue 19/08/25
1112	Column cage reo inspection sign off	100%	1 day	Tue 19/08/25	Tue 19/08/25
1113	Lift column formwork	100%	1 day	Tue 19/08/25	Tue 19/08/25
1114	Column formwork install	100%	2 days	Tue 19/08/25	Wed 20/08/25
1115	Pour concrete columns	100%	1 day	Wed 20/08/25	Wed 20/08/25
1116	Strip and remove column form work	100%	1 day	Thu 21/08/25	Thu 21/08/25
1117	Install precast wall panels	100%	2 days	Wed 20/08/25	Thu 21/08/25
1118	Lift BD false work	100%	1 day	Tue 26/08/25	Tue 26/08/25
1119	Install BD false work	100%	5 days	Wed 27/08/25	Thu 4/09/25
1120	BD false work inspection and sign off	100%	1 day	Thu 4/09/25	Thu 4/09/25
1121	Install BD panels	100%	3 days	Thu 4/09/25	Sat 6/09/25
1122	Install scaffold handrail to live deck (pm)	100%	1 day	Sat 6/09/25	Sat 6/09/25
1123	Open Live deck (pm)	100%	1 day	Sat 6/09/25	Sat 6/09/25
1124	Lift BD reo	100%	1 day	Sat 6/09/25	Sat 6/09/25
1125	Install BD reo	100%	1 day	Sat 6/09/25	Sat 6/09/25
1126	Lift screw in bars	100%	1 day	Sat 6/09/25	Sat 6/09/25
1127	Install screw in bars	100%	1 day	Tue 9/09/25	Tue 9/09/25
1128	Install services	100%	1 day	Tue 9/09/25	Tue 9/09/25
1129	Pre-pour engineer inspections inspections Zone [B]	100%	1 day	Tue 9/09/25	Tue 9/09/25
1130	Install set downs	100%	1 day	Tue 9/09/25	Tue 9/09/25

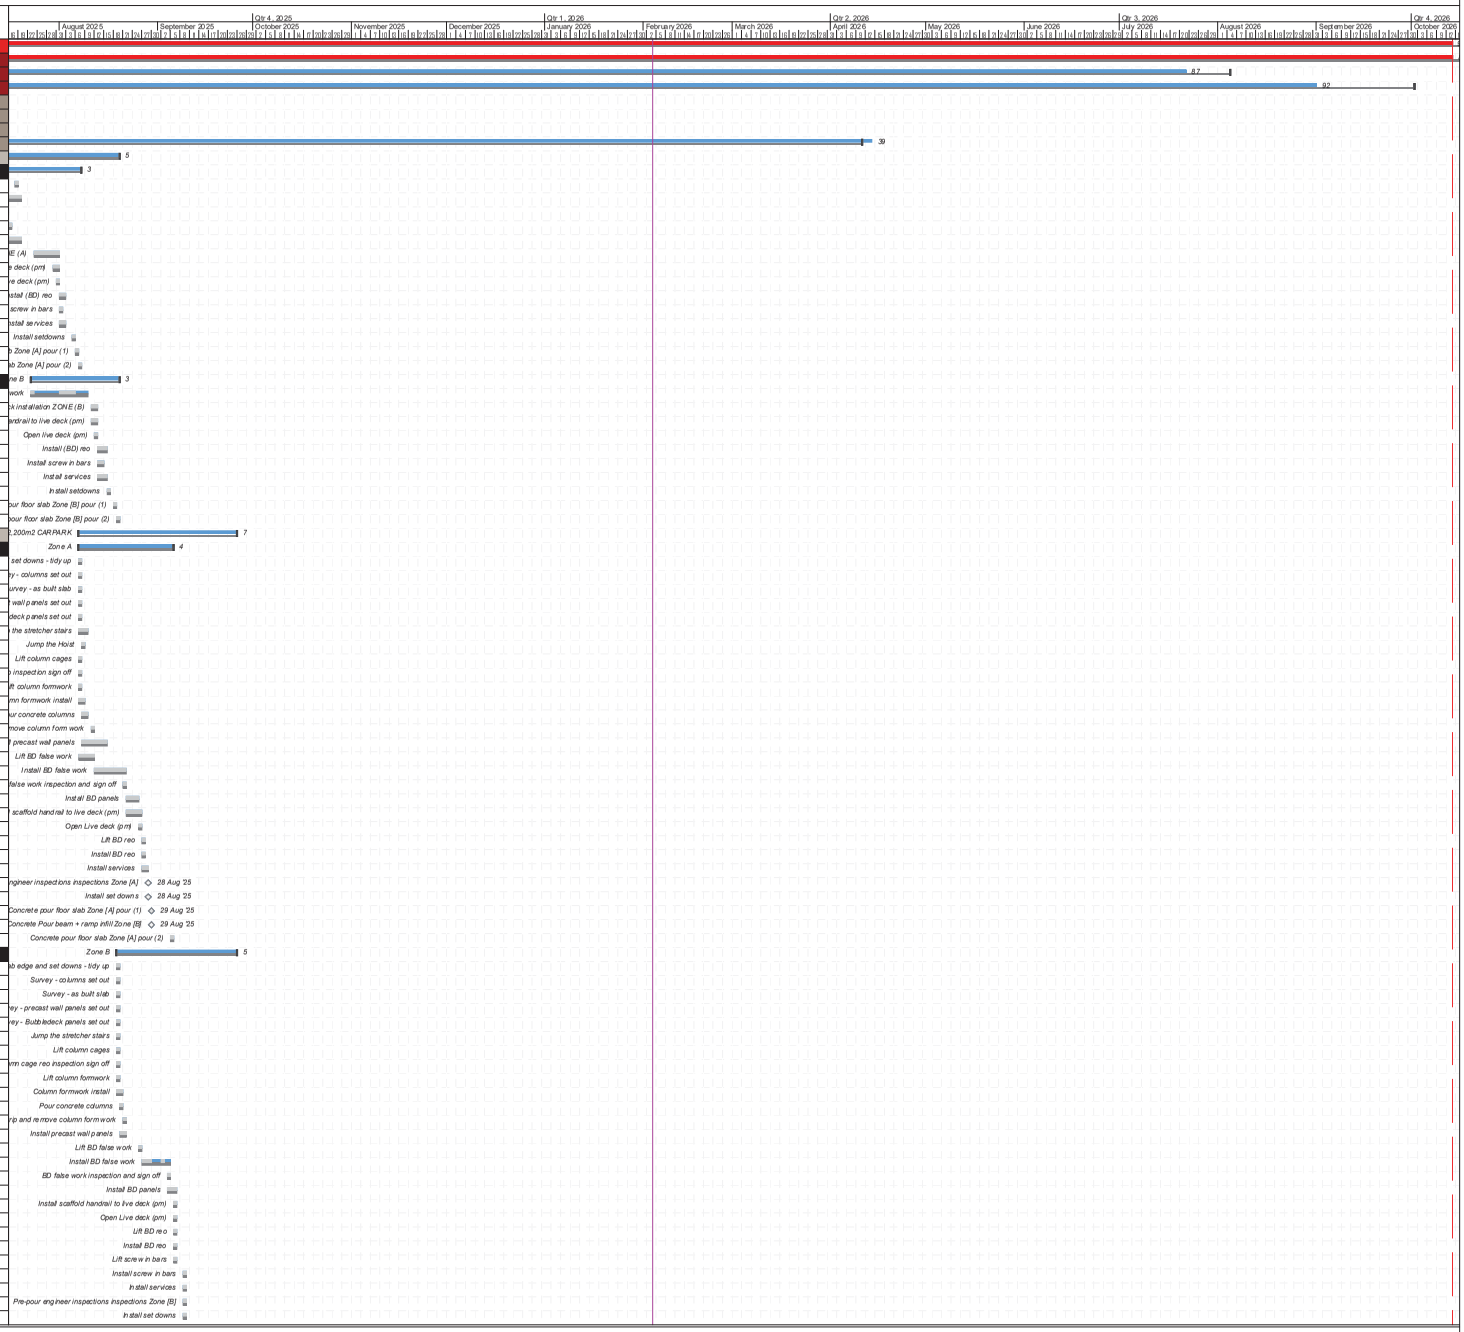

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

Planner: **Steve Church** Review: **Marcus Anderson**

ID	Name	% Complete	Duration	Start	Finish
1131	Concrete pour floor slab Zone [B] pour (3)	100%	1 day	Wed 10/09/25	Wed 10/09/25
1132	Concrete pour floor slab Zone [B] pour (4) (Exlcudes 1.2m strip adjacent West Precast)	100%	1 day	Fri 12/09/25	Fri 12/09/25
1133	Precast wall panels to the west side (Double late)	100%	2 days	Sat 20/09/25	Tue 23/09/25
1134	Concrete Pour (5) - Install Threaded Rod and Pour 1.2m Strip	100%	2 days	Wed 24/09/25	Thu 25/09/25
1135	**LEVEL 3 ~ 2,200m2 PODIUM**	**100%**	**31 days**	**Tue 2/09/25**	**Wed 15/10/25**
1136	**Zone A**	**100%**	**25 days**	**Tue 2/09/25**	**Wed 8/10/25**
1137	Strip slab edge and set downs - tidy up	100%	1 day	Tue 2/09/25	Tue 2/09/25
1138	Survey - columns set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1139	Survey - as built slab	100%	1 day	Tue 2/09/25	Tue 2/09/25
1140	Survey - precast wall panels set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1141	Survey - Bubbledeck panels set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1142	Jump the stretcher stairs	100%	1 day	Tue 2/09/25	Tue 2/09/25
1143	Jump the Hoist	100%	1 day	Wed 3/09/25	Wed 3/09/25
1144	Install precast wall panels	100%	2 days	Wed 3/09/25	Thu 4/09/25
1145	Lift BD false work	100%	1 day	Sat 6/09/25	Sat 6/09/25
1146	Install BD false work	100%	7 days	Sat 6/09/25	Mon 15/09/25
1147	BD false work inspection and sign off	100%	1 day	Mon 15/09/25	Mon 15/09/25
1148	Install BD panels	100%	3 days	Fri 12/09/25	Mon 15/09/25
1149	Install scaffold handrail to live deck (pm)	100%	1 day	Fri 19/09/25	Fri 19/09/25
1150	Open Live deck (pm)	100%	1 day	Fri 19/09/25	Fri 19/09/25
1151	Lift BD reo	100%	1 day	Fri 19/09/25	Fri 19/09/25
1152	Install BD reo	100%	2 days	Thu 2/10/25	Fri 3/10/25
1153	Lift screw in bars	100%	1 day	Fri 19/09/25	Fri 19/09/25
1154	Install screw in bars	100%	1 day	Fri 19/09/25	Fri 19/09/25
1155	Install services	100%	2 days	Thu 2/10/25	Fri 3/10/25
1156	Pre-pour engineer inspections inspections Zone [A]	100%	1 day	Wed 24/09/25	Wed 24/09/25
1157	Install set downs	100%	1 day	Fri 3/10/25	Fri 3/10/25
1158	Concrete pour floor slab Zone [A] pour (1)	100%	1 day	Fri 26/09/25	Fri 26/09/25
1159	Concrete pour floor slab Zone [A] pour (2)	100%	1 day	Wed 8/10/25	Wed 8/10/25
1160	**Zone B**	**100%**	**24 days**	**Thu 11/09/25**	**Wed 15/10/25**
1161	Strip slab edge and set downs - tidy up	100%	4 days	Thu 11/09/25	Mon 15/09/25
1162	Survey - columns set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1163	Survey - as built slab	100%	4 days	Thu 11/09/25	Mon 15/09/25
1164	Survey - precast wall panels set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1165	Survey - Bubbledeck panels set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1166	Jump the stretcher stairs	100%	4 days	Thu 11/09/25	Mon 15/09/25
1167	Lift BD false work	100%	4 days	Thu 11/09/25	Mon 15/09/25
1168	Install BD false work	100%	8 days	Thu 11/09/25	Tue 23/09/25
1169	BD false work inspection and sign off	100%	1 day	Tue 23/09/25	Tue 23/09/25
1170	Install BD panels	100%	3 days	Wed 24/09/25	Fri 26/09/25
1171	Install scaffold handrail to live deck (pm)	100%	2 days	Thu 25/09/25	Fri 26/09/25
1172	Open Live deck (pm)	100%	1 day	Fri 26/09/25	Fri 26/09/25
1173	Lift BD reo	100%	1 day	Fri 26/09/25	Fri 26/09/25
1174	Install BD reo	100%	2 days	Sat 27/09/25	Mon 29/09/25
1175	Lift screw in bars	100%	1 day	Sat 27/09/25	Sat 27/09/25
1176	Install screw in bars	100%	1 day	Mon 29/09/25	Mon 29/09/25
1177	Install services	100%	2 days	Sat 27/09/25	Mon 29/09/25
1178	Pre-pour engineer inspections inspections Zone [B]	100%	1 day	Fri 10/10/25	Fri 10/10/25
1179	Install set downs	100%	3 days	Sat 11/10/25	Tue 14/10/25
1180	Concrete pour floor slab and Columns Zone [B] pour (1)	100%	4 days	Thu 9/10/25	Mon 13/10/25
1181	Concrete pour floor slab and Columns Zone [B] pour (2)	100%	1 day	Wed 15/10/25	Wed 15/10/25
1182	**LEVEL 4 ~ 1,400m2**	**100%**	**21 days**	**Thu 2/10/25**	**Thu 23/10/25**
1183	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Thu 2/10/25	Thu 2/10/25
1184	Day 1 - Install pour one column cages	100%	1 day	Thu 2/10/25	Thu 2/10/25
1185	Day 1 - Commence precast install	100%	1 day	Thu 9/10/25	Thu 9/10/25
1186	Day 1 - Commence formwork to columns	100%	1 day	Thu 2/10/25	Thu 2/10/25
1187	Day 2 - Continue Precast	100%	1 day	Thu 9/10/25	Thu 9/10/25
1188	Day 2 - Continue forming columns	100%	1 day	Thu 9/10/25	Thu 9/10/25
1189	Day 3 - Install pour 2 column cages	100%	1 day	Fri 10/10/25	Fri 10/10/25
1190	Day 3 - Continue Precast	100%	2 days	Fri 10/10/25	Sat 11/10/25
1191	Day 3 - Commence shoring (6 men)	100%	1 day	Tue 14/10/25	Tue 14/10/25
1192	Day 3 - Pour columns to pour 1	100%	1 day	Fri 10/10/25	Fri 10/10/25
1193	Day 3 - Form columns pour 2	100%	1 day	Fri 10/10/25	Fri 10/10/25
1194	Day 4 - Complete precast installation	100%	1 day	Mon 13/10/25	Mon 13/10/25
1195	Day 4 - Continue shoring (6 men)	100%	1 day	Wed 15/10/25	Wed 15/10/25
1196	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Sat 11/10/25	Sat 11/10/25
1197	Day 4 - Continue forming pour 2 columns	100%	1 day	Sat 11/10/25	Sat 11/10/25
1198	Day 5 - Pour columns pour 2	100%	1 day	Mon 13/10/25	Mon 13/10/25
1199	Day 5 - Continue shoring (6 men)	100%	1 day	Thu 16/10/25	Thu 16/10/25
1200	Day 5 - Dog box works, caulking panels	100%	1 day	Tue 14/10/25	Tue 14/10/25
1201	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Wed 15/10/25	Wed 15/10/25
1202	Day 6 - Complete dog box works – caulking panels	100%	1 day	Wed 15/10/25	Wed 15/10/25
1203	Day 6 - Complete shoring (6 men)	100%	1 day	Fri 17/10/25	Fri 17/10/25
1204	Day 6 - Complete levelling pour 1	100%	1 day	Fri 17/10/25	Fri 17/10/25
1205	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Sat 18/10/25	Sat 18/10/25
1206	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Sat 18/10/25	Sat 18/10/25
1207	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Thu 23/10/25	Thu 23/10/25
1208	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Thu 23/10/25	Thu 23/10/25
1209	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Thu 23/10/25	Thu 23/10/25
1210	Day 9 - Reo delivery first thing	100%	1 day	Fri 24/10/25	Fri 24/10/25
1211	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Fri 24/10/25	Fri 24/10/25
1212	Day 9 - Commenced reo fixing	100%	1 day	Fri 24/10/25	Fri 24/10/25
1213	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Fri 24/10/25	Fri 24/10/25
1214	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Fri 24/10/25	Fri 24/10/25
1215	Day 10 - Continue Reo fixing, complete pour 1 & setdowns	100%	2 days	Sat 25/10/25	Mon 27/10/25
1216	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	2 days	Sat 25/10/25	Mon 27/10/25
1217	Day 11 - Continue reo fixing, complete pour 2 & setdowns	100%	2 days	Tue 28/10/25	Wed 29/10/25
1218	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	2 days	Wed 29/10/25	Thu 30/10/25
1219	Day 11 - Slab pour, pour 1	100%	1 day	Fri 31/10/25	Fri 31/10/25
1220	Day 12 - Slab pour, pour 2	100%	1 day	Tue 4/11/25	Tue 4/11/25
1221	**LEVEL 5 ~ 1,400m2**	**100%**	**16 days**	**Sat 1/11/25**	**Sat 22/11/25**
1222	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Sat 1/11/25	Sat 1/11/25

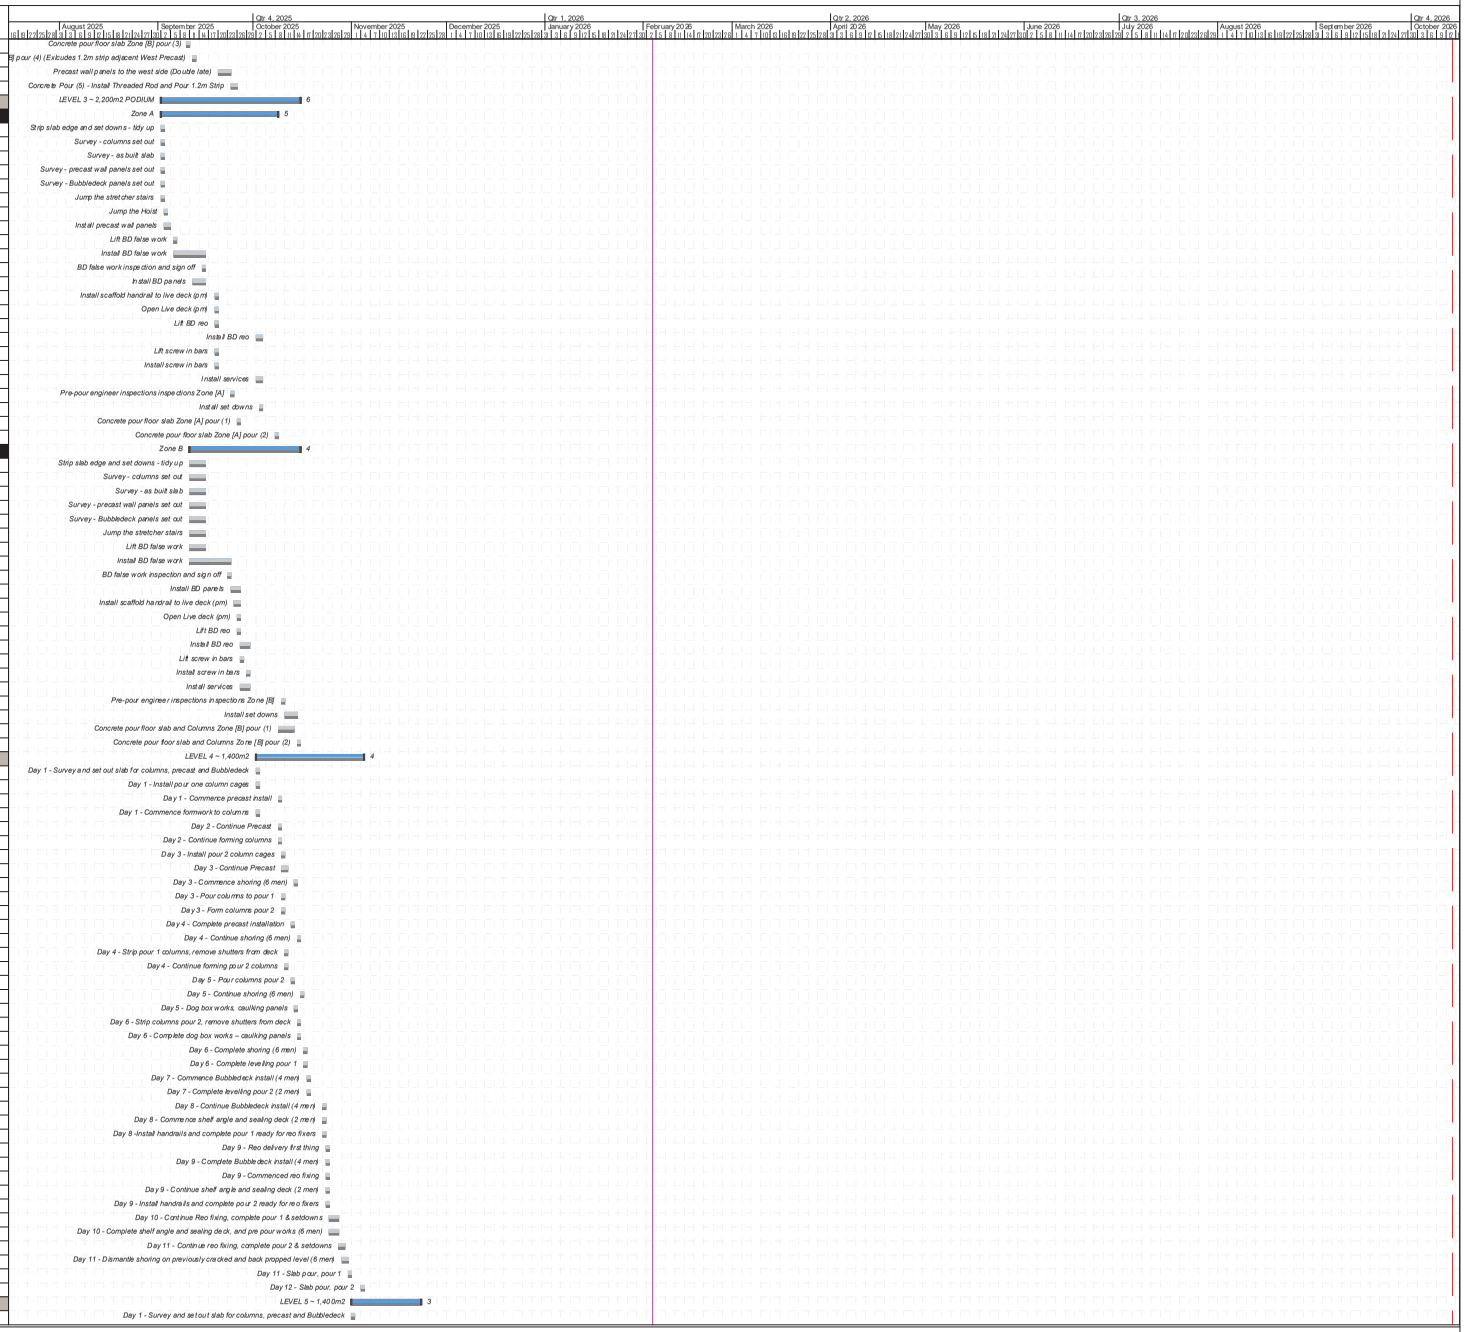

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34
FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1223	Day 1 - Install pour one column cages	100%	1 day	Sat 1/11 2:5	Sat 1/11/25
1224	Day 1 - Commence precast install	100%	1 day	Tue 4/11/25	Tue 4/11/25
1225	Day 1 - Commence formwork to columns	100%	1 day	Tue 4/11/25	Tue 4/11/25
1226	Day 2 - Continue Precast	100%	1 day	Wed 5/11/25	Wed 5/11/25
1227	Day 2 - Continue forming columns	100%	1 day	Wed 5/11/25	Wed 5/11/25
1228	Day 3 - Install pour 2 column cages	100%	1 day	Fri 7/11/25	Fri 7/11/25
1229	Day 3 - Continue Precast	100%	1 day	Thu 6/11/25	Thu 6/11/25
1230	Day 3 - Commence shoring (6 men)	100%	1 day	Thu 6/11/25	Thu 6/11/25
1231	Day 3 - Pour columns to pour 1	100%	1 day	Thu 6/11/25	Thu 6/11/25
1232	Day 3 - Form columns pour 2	100%	1 day	Fri 7/11/25	Fri 7/11/25
1233	Day 4 - Complete precast installation	100%	1 day	Fri 7/11/25	Fri 7/11/25
1234	Day 4 - Continue shoring (6 men)	100%	1 day	Fri 7/11/25	Fri 7/11/25
1235	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Fri 7/11/25	Fri 7/11/25
1236	Day 4 - Continue forming pour 2 columns	100%	1 day	Fri 7/11/25	Fri 7/11/25
1237	Day 5 - Pour columns pour 2	100%	1 day	Mon 10/11/25	Mon 10/11/25
1238	Day 5 - Continue shoring (6 men)	100%	1 day	Sat 8/11 2:5	Sat 8/11/25
1239	Day 5 - Dog box works, caulking panels	100%	1 day	Sat 8/11 2:5	Sat 8/11/25
1240	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Tue 11/11/25	Tue 11/11/25
1241	Day 6 - Complete dog box works – caulking panels	100%	1 day	Mon 10/11/25	Mon 10/11/25
1242	Day 6 - Complete shoring (6 men)	100%	1 day	Mon 10/11/25	Mon 10/11/25
1243	Day 6 - Complete levelling pour 1	100%	1 day	Mon 10/11/25	Mon 10/11/25
1244	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Tue 11/11/25	Tue 11/11/25
1245	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Tue 11/11/25	Tue 11/11/25
1246	Day 8 - Continue Bubbledeck install (4 men)	100%	2 days	Wed 12/11/25	Thu 13/11/25
1247	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Wed 12/11/25	Wed 12/11/25
1248	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Wed 12/11/25	Wed 12/11/25
1249	Day 9 - Reo delivery first thing	100%	1 day	Fri 14/11/25	Fri 14/11/25
1250	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Fri 14/11/25	Fri 14/11/25
1251	Day 9 - Commenced reo fixing	100%	1 day	Fri 14/11/25	Fri 14/11/25
1252	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Thu 13/11/25	Thu 13/11/25
1253	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Thu 13/11/25	Thu 13/11/25
1254	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	1 day	Wed 19/11/25	Wed 19/11/25
1255	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Fri 14/11/25	Fri 14/11/25
1256	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	1 day	Fri 21/11/25	Fri 21/11/25
1257	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	1 day	Sat 15/11/25	Sat 15/11/25
1258	Day 11 - Slab pour, pour 1	100%	1 day	Fri 21/11/25	Fri 21/11/25
1259	Day 12 - Slab pour, pour 2	100%	1 day	Sat 22/11/25	Sat 22/11/25
1260	LEVEL 6 – 1,400m2	100%	14 days	Sat 22/11/25	Wed 10/12/25
1261	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Mon 24/11/25	Mon 24/11/25
1262	Day 1 - Install pour one column cages	100%	1 day	Mon 24/11/25	Mon 24/11/25
1263	Day 1 - Commence precast install	100%	1 day	Mon 24/11/25	Mon 24/11/25
1264	Day 1 - Commence formwork to columns	100%	1 day	Sat 22/11/25	Sat 22/11/25
1265	Day 2 - Continue Precast	100%	1 day	Tue 25/11/25	Tue 25/11/25
1266	Day 2 - Continue forming columns	100%	1 day	Tue 25/11/25	Tue 25/11/25
1267	Day 3 - Install pour 2 column cages	100%	1 day	Wed 26/11/25	Wed 26/11/25
1268	Day 3 - Continue Precast	100%	1 day	Wed 26/11/25	Wed 26/11/25
1269	Day 3 - Commence shoring (6 men)	100%	1 day	Wed 26/11/25	Wed 26/11/25
1270	Day 3 - Pour columns to pour 1	100%	1 day	Wed 26/11/25	Wed 26/11/25
1271	Day 3 - Form columns pour 2	100%	1 day	Wed 26/11/25	Wed 26/11/25
1272	Day 4 - Complete precast installation	100%	1 day	Thu 27/11/25	Thu 27/11/25
1273	Day 4 - Continue shoring (6 men)	100%	1 day	Thu 27/11/25	Thu 27/11/25
1274	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Thu 27/11/25	Thu 27/11/25
1275	Day 4 - Continue forming pour 2 columns	100%	1 day	Thu 27/11/25	Thu 27/11/25
1276	Day 5 - Pour columns pour 2	100%	1 day	Fri 28/11/25	Fri 28/11/25
1277	Day 5 - Continue shoring (6 men)	100%	1 day	Fri 28/11/25	Fri 28/11/25
1278	Day 5 - Dog box works, caulking panels	100%	1 day	Fri 28/11/25	Fri 28/11/25
1279	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Tue 2/12/25	Tue 2/12/25
1280	Day 6 - Complete dog box works – caulking panels	100%	1 day	Tue 2/12/25	Tue 2/12/25
1281	Day 6 - Complete shoring (6 men)	100%	1 day	Tue 2/12/25	Tue 2/12/25
1282	Day 6 - Complete levelling pour 1	100%	1 day	Tue 2/12/25	Tue 2/12/25
1283	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Wed 3/12/25	Wed 3/12/25
1284	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Wed 3/12/25	Wed 3/12/25
1285	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1286	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1287	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Thu 4/12/25	Thu 4/12/25
1288	Day 9 - Reo delivery first thing	100%	1 day	Thu 4/12/25	Thu 4/12/25
1289	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1290	Day 9 - Commenced reo fixing	100%	1 day	Thu 4/12/25	Thu 4/12/25
1291	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1292	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Thu 4/12/25	Thu 4/12/25
1293	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	3 days	Thu 4/12/25	Sat 6/12/25
1294	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1295	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	2 days	Mon 8/12 2:5	Tue 9/12/25
1296	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	2 days	Fri 5/12/25	Sat 6/12/25
1297	Day 11 - Slab pour, pour 1	100%	1 day	Mon 8/12 2:5	Mon 8/12/25
1298	Day 12 - Strip Slab Edging and prepare for Pour 2	100%	1 day	Tue 9/12/25	Tue 9/12/25
1299	Day 13 - Slab pour, pour 2	100%	1 day	Wed 10/12/25	Wed 10/12/25
1300	LEVEL 7 – 1,400m2	5%	17 days	Tue 9/12/25	Fri 19/01/26
1301	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Tue 9/12/25	Tue 9/12/25
1302	Day 1 - Install pour one column cages	100%	1 day	Tue 9/12/25	Tue 9/12/25
1303	Day 1 - Commence precast install	100%	1 day	Tue 9/12/25	Tue 9/12/25
1304	Day 1 - Commence formwork to columns	100%	1 day	Tue 9/12/25	Tue 9/12/25
1305	Day 2 - Continue Precast	100%	1 day	Thu 11/12/25	Thu 11/12/25
1306	Day 2 - Continue forming columns	100%	1 day	Wed 10/12/25	Wed 10/12/25
1307	Day 3 - Install pour 2 column cages	100%	1 day	Thu 11/12/25	Thu 11/12/25
1308	Day 3 - Continue Precast	100%	1 day	Fri 12/12/25	Fri 12/12/25
1309	Day 3 - Commence shoring (6 men)	100%	1 day	Thu 11/12/25	Thu 11/12/25
1310	Day 3 - Pour columns to pour 1	100%	1 day	Thu 11/12/25	Thu 11/12/25
1311	Day 3 - Form columns pour 2	100%	1 day	Thu 11/12/25	Thu 11/12/25
1312	Day 4 - Complete precast installation	100%	1 day	Sat 13/12/25	Sat 13/12/25
1313	Day 4 - Continue shoring (6 men)	100%	1 day	Fri 12/12/25	Fri 12/12/25
1314	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Fri 12/12/25	Fri 12/12/25

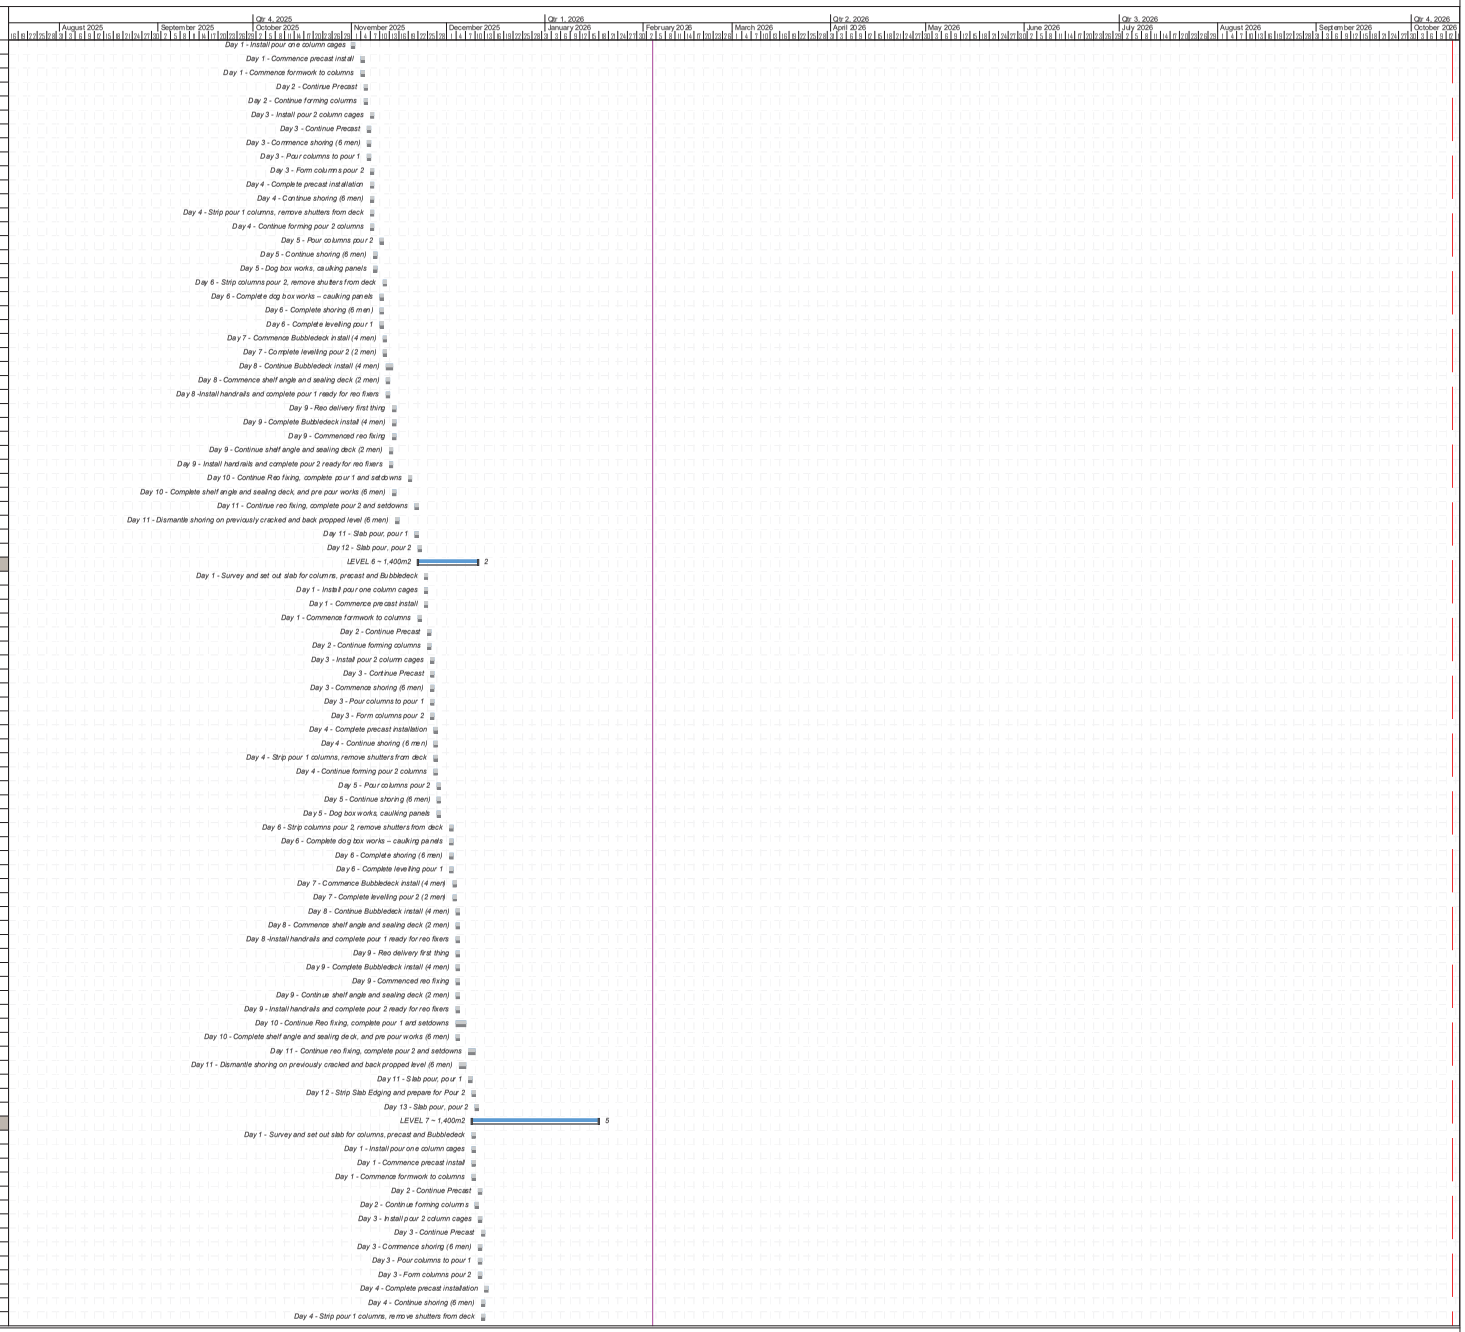

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
1315	Day 4 - Continue forming pour 2 columns	100%	1 day	Fri 12/12/25	Fri 12/12/25
1316	Day 5 - Pour columns pour 2	100%	1 day	Sat 13/12/25	Sat 13/12/25
1317	Day 5 - Continue shoring (6 men)	100%	1 day	Sat 13/12/25	Sat 13/12/25
1318	Day 5 - Dog box works, caulking panels	100%	1 day	Mon 15/12/25	Mon 15/12/25
1319	Day 6 - Strip columns pour 2, remove shutters from deck	100%	3 days	Tue 16/12/25	Thu 18/12/25
1320	Day 6 - Complete dog box works – caulking panels	100%	1 day	Tue 16/12/25	Tue 16/12/25
1321	Day 6 - Complete shoring (6 men)	100%	1 day	Mon 15/12/25	Mon 15/12/25
1322	Day 6 - Complete levelling pour 1	100%	1 day	Mon 15/12/25	Mon 15/12/25
1323	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1324	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1325	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Tue 13/01/26	Tue 13/01/26
1326	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	2 days	Mon 12/01/26	Tue 13/01/26
1327	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Tue 13/01/26	Tue 13/01/26
1328	Day 9 - Reo delivery first thing	100%	1 day	Mon 12/01/26	Mon 12/01/26
1329	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1330	Day 9 - Commenced reo fixing	100%	1 day	Mon 12/01/26	Mon 12/01/26
1331	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1332	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Sat 13/12/25	Sat 13/12/25
1333	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	2 days	Tue 13/01/26	Wed 14/01/26
1334	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Wed 14/01/26	Wed 14/01/26
1335	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	1 day	Thu 15/01/26	Thu 15/01/26
1336	Day 11 - Slab pour, pour 1	100%	0 days	Thu 15/01/26	Thu 15/01/26
1337	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Fri 16/01/26	Fri 16/01/26
1338	Day 13 - Slab pour, pour 2	0%	1 day	Sat 17/01/26	Sat 17/01/26
1339	LEVEL 8 – 1,400m2	0%	14 days	Sat 17/01/26	Fri 30/01/26
1340	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Fri 16/01/26	Fri 16/01/26
1341	Day 1 - Install pour one column cages	0%	1 day	Fri 16/01/26	Fri 16/01/26
1342	Day 1 - Commence precast install	0%	1 day	Sat 17/01/26	Sat 17/01/26
1343	Day 1 - Commence formwork to columns	0%	1 day	Sat 17/01/26	Sat 17/01/26
1344	Day 2 - Continue Precast	0%	1 day	Mon 19/01/26	Mon 19/01/26
1345	Day 2 - Continue forming columns	0%	1 day	Mon 19/01/26	Mon 19/01/26
1346	Day 3 - Install pour 2 column cages	0%	1 day	Tue 20/01/26	Tue 20/01/26
1347	Day 3 - Continue Precast	0%	1 day	Tue 20/01/26	Tue 20/01/26
1348	Day 3 - Commence shoring (6 men)	0%	1 day	Tue 20/01/26	Tue 20/01/26
1349	Day 3 - Pour columns to pour 1	0%	1 day	Tue 20/01/26	Tue 20/01/26
1350	Day 3 - Form columns pour 2	0%	1 day	Tue 20/01/26	Tue 20/01/26
1351	Day 4 - Complete precast installation	0%	1 day	Wed 21/01/26	Wed 21/01/26
1352	Day 4 - Continue shoring (6 men)	0%	1 day	Wed 21/01/26	Wed 21/01/26
1353	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Wed 21/01/26	Wed 21/01/26
1354	Day 4 - Continue forming pour 2 columns	0%	1 day	Wed 21/01/26	Wed 21/01/26
1355	Day 5 - Pour columns pour 2	0%	1 day	Thu 22/01/26	Thu 22/01/26
1356	Day 5 - Continue shoring (6 men)	0%	1 day	Thu 22/01/26	Thu 22/01/26
1357	Day 5 - Dog box works, caulking panels	0%	1 day	Thu 22/01/26	Thu 22/01/26
1358	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Fri 23/01/26	Fri 23/01/26
1359	Day 6 - Complete dog box works – caulking panels	0%	1 day	Fri 23/01/26	Fri 23/01/26
1360	Day 6 - Complete shoring (6 men)	0%	1 day	Fri 23/01/26	Fri 23/01/26
1361	Day 6 - Complete levelling pour 1	0%	1 day	Fri 23/01/26	Fri 23/01/26
1362	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Wed 28/01/26	Wed 28/01/26
1363	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Wed 28/01/26	Wed 28/01/26
1364	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Thu 29/01/26	Thu 29/01/26
1365	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Thu 29/01/26	Thu 29/01/26
1366	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Thu 29/01/26	Thu 29/01/26
1367	Day 9 - Reo delivery first thing	0%	1 day	Fri 30/01/26	Fri 30/01/26
1368	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Fri 30/01/26	Fri 30/01/26
1369	Day 9 - Commenced reo fixing	0%	1 day	Fri 30/01/26	Fri 30/01/26
1370	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Fri 30/01/26	Fri 30/01/26
1371	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Fri 30/01/26	Fri 30/01/26
1372	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Sat 31/01/26	Sat 31/01/26
1373	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Sat 31/01/26	Sat 31/01/26
1374	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Mon 2/02/26	Mon 2/02/26
1375	Day 11 - Slab pour, pour 1	0%	1 day	Wed 4/02/26	Wed 4/02/26
1376	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Thu 5/02/26	Thu 5/02/26
1377	Day 13 - Slab Pour, pour 2	0%	1 day	Fri 6/02/26	Fri 6/02/26
1378	LEVEL 9 – 1,400m2	0%	14 days	Thu 5/02/26	Wed 18/02/26
1379	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Thu 5/02/26	Thu 5/02/26
1380	Day 1 - Install pour one column cages	0%	1 day	Thu 5/02/26	Thu 5/02/26
1381	Day 1 - Commence precast install	0%	1 day	Thu 5/02/26	Thu 5/02/26
1382	Day 1 - Commence formwork to columns	0%	1 day	Thu 5/02/26	Thu 5/02/26
1383	Day 2 - Continue Precast	0%	1 day	Sat 7/02/26	Sat 7/02/26
1384	Day 2 - Continue forming columns	0%	1 day	Fri 6/02/26	Fri 6/02/26
1385	Day 3 - Install pour 2 column cages	0%	1 day	Sat 7/02/26	Sat 7/02/26
1386	Day 3 - Continue Precast	0%	1 day	Tue 10/02/26	Tue 10/02/26
1387	Day 3 - Commence shoring (6 men)	0%	1 day	Sat 7/02/26	Sat 7/02/26
1388	Day 3 - Pour columns to pour 1	0%	1 day	Sat 7/02/26	Sat 7/02/26
1389	Day 3 - Form columns pour 2	0%	1 day	Sat 7/02/26	Sat 7/02/26
1390	Day 4 - Complete precast installation	0%	1 day	Wed 11/02/26	Wed 11/02/26
1391	Day 4 - Continue shoring (6 men)	0%	1 day	Tue 10/02/26	Tue 10/02/26
1392	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Tue 10/02/26	Tue 10/02/26
1393	Day 4 - Continue forming pour 2 columns	0%	1 day	Tue 10/02/26	Tue 10/02/26
1394	Day 5 - Pour columns pour 2	0%	1 day	Wed 11/02/26	Wed 11/02/26
1395	Day 5 - Continue shoring (6 men)	0%	1 day	Wed 11/02/26	Wed 11/02/26
1396	Day 5 - Dog box works, caulking panels	0%	1 day	Thu 12/02/26	Thu 12/02/26
1397	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Fri 13/02/26	Fri 13/02/26
1398	Day 6 - Complete dog box works – caulking panels	0%	1 day	Fri 13/02/26	Fri 13/02/26
1399	Day 6 - Complete shoring (6 men)	0%	1 day	Thu 12/02/26	Thu 12/02/26
1400	Day 6 - Complete levelling pour 1	0%	1 day	Thu 12/02/26	Thu 12/02/26
1401	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Sat 14/02/26	Sat 14/02/26
1402	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Fri 13/02/26	Fri 13/02/26
1403	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Mon 16/02/26	Mon 16/02/26
1404	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Mon 16/02/26	Mon 16/02/26
1405	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Mon 16/02/26	Mon 16/02/26
1406	Day 9 - Reo delivery first thing	0%	1 day	Tue 17/02/26	Tue 17/02/26

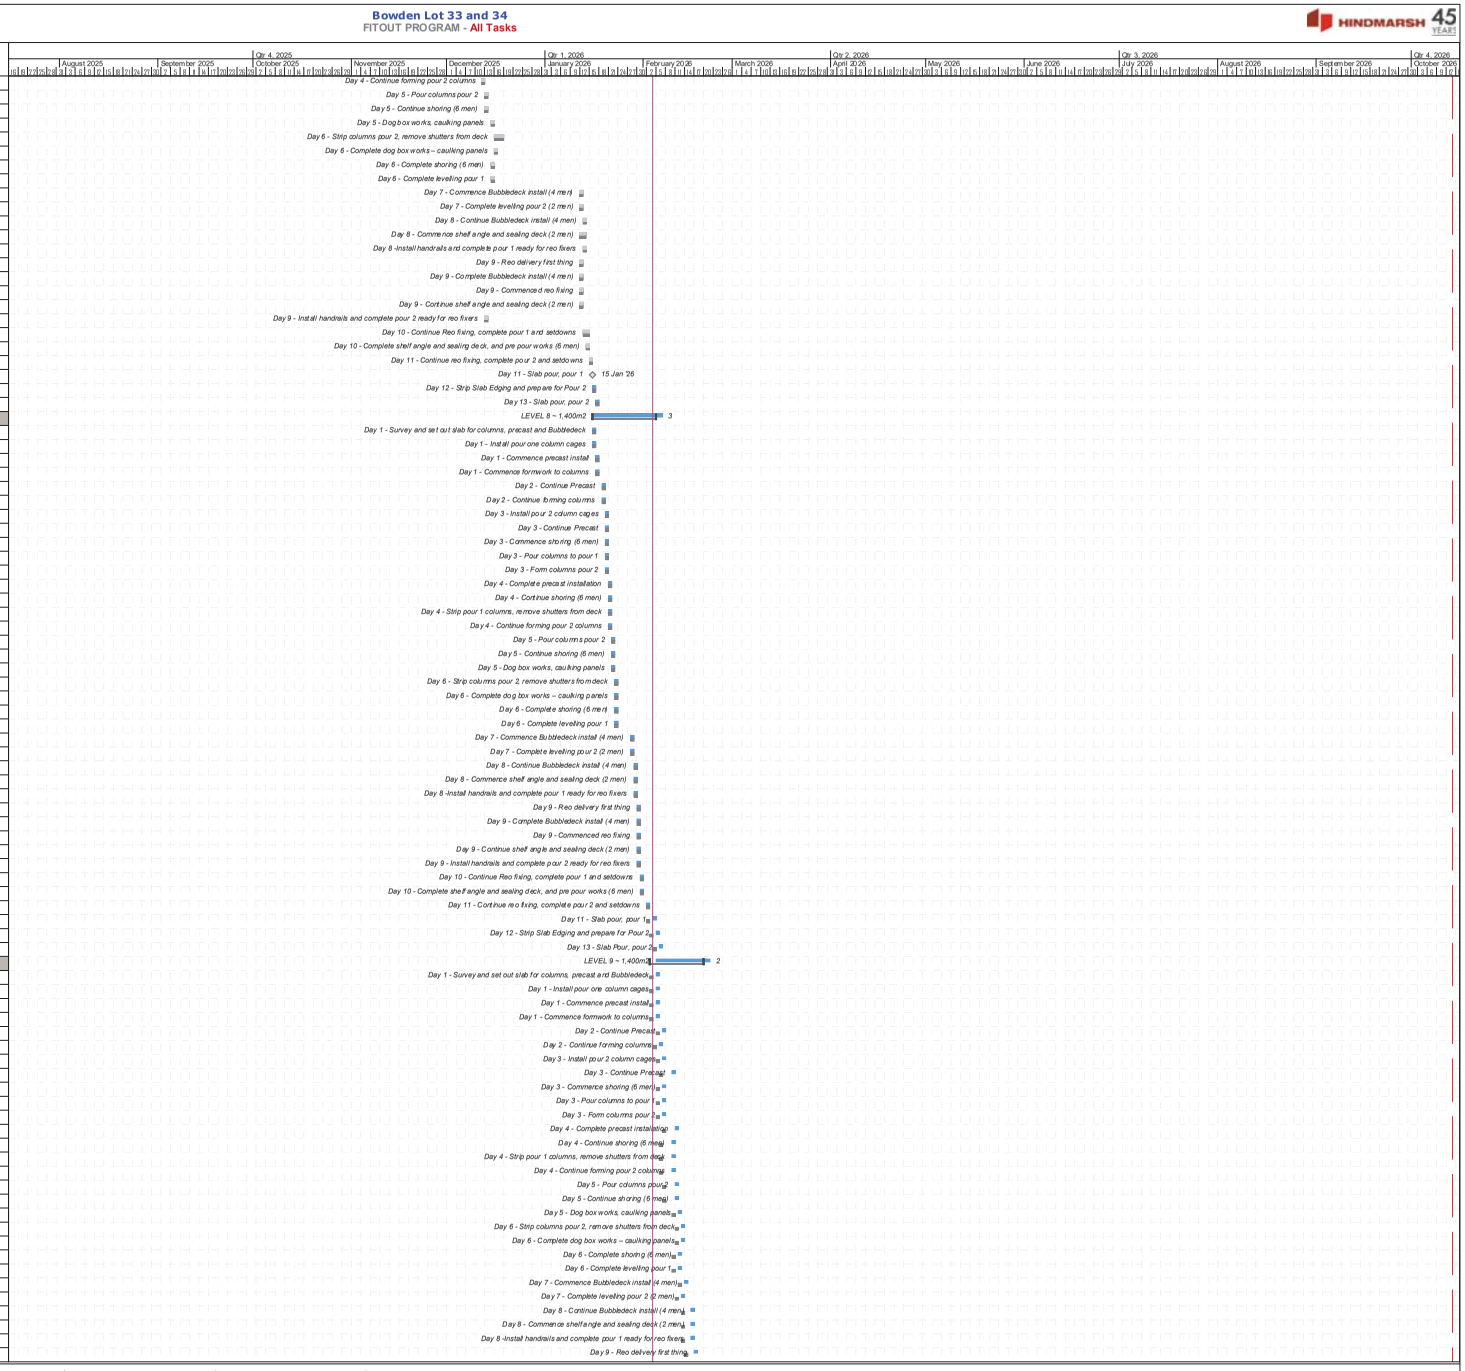

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones
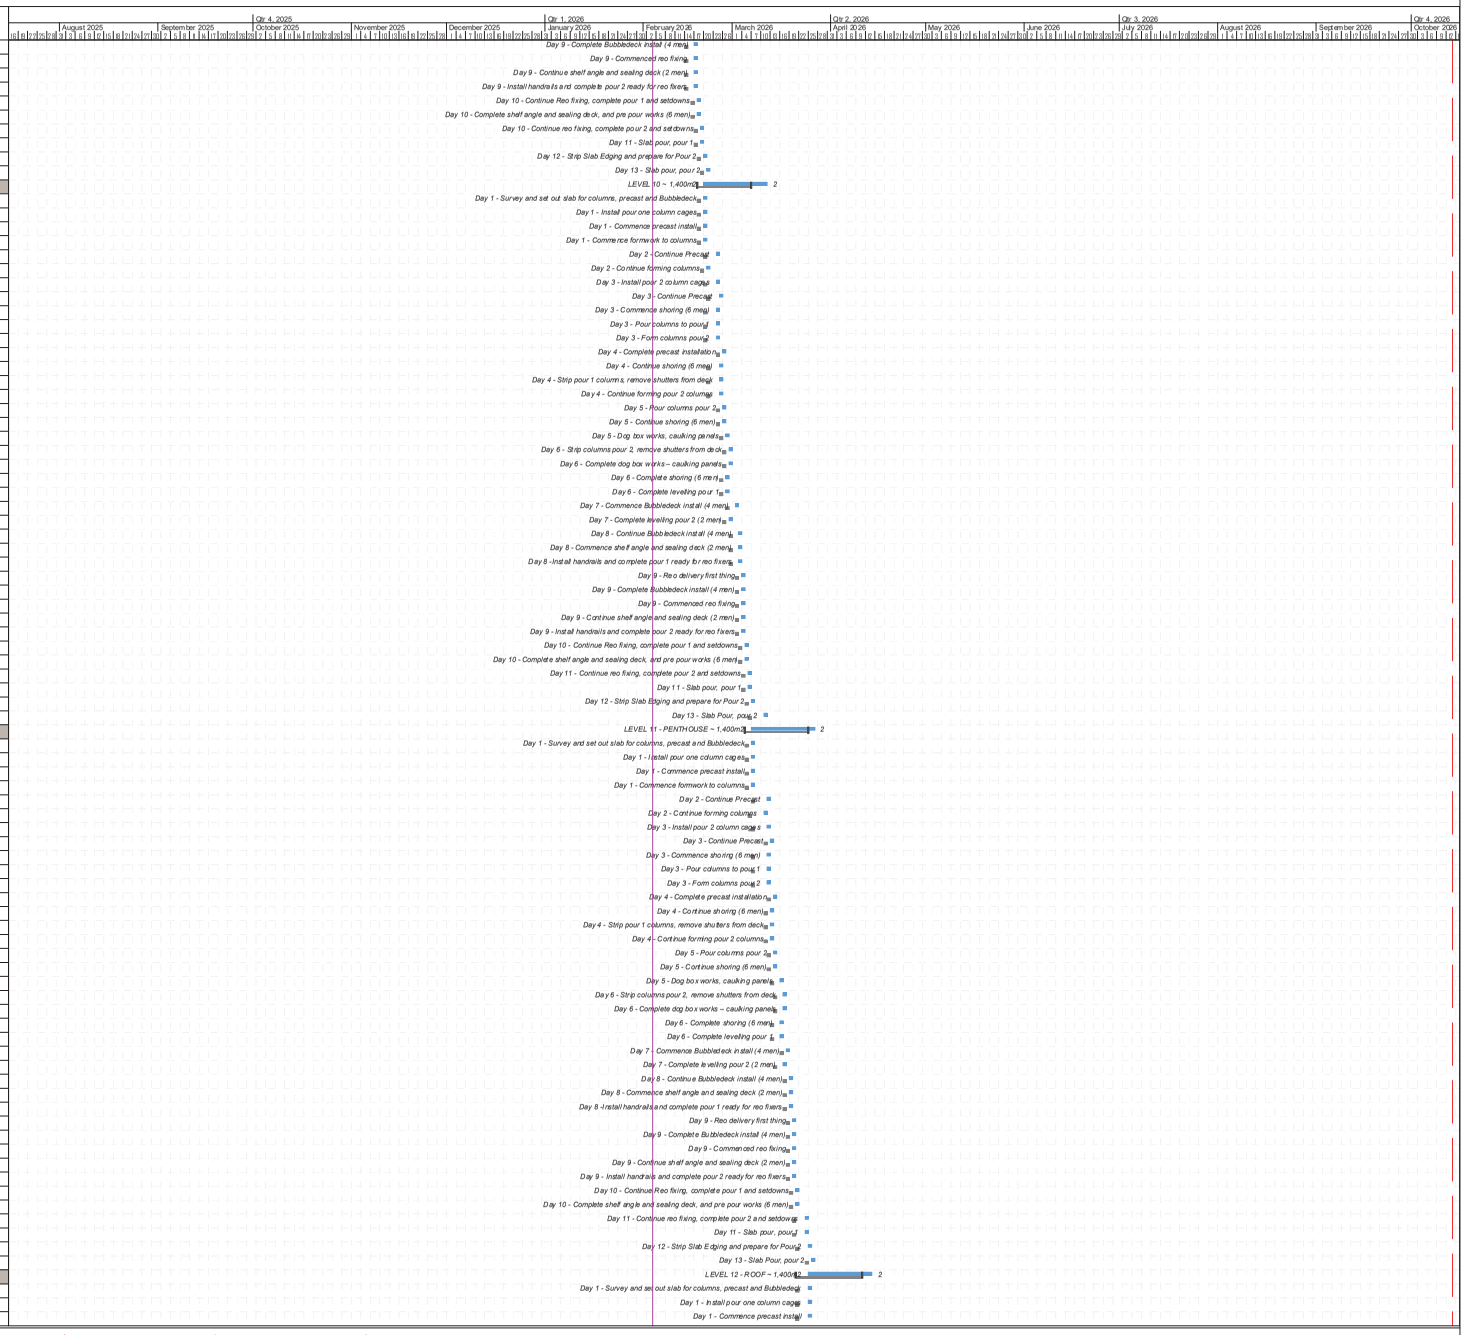
ID	Name	% Complete	Duration	Start	Finish
1407	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Tue 17/02/26	Tue 17/02/26
1408	Day 9 - Commenced reo fixing	0%	1 day	Tue 17/02/26	Tue 17/02/26
1409	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Tue 17/02/26	Tue 17/02/26
1410	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Tue 17/02/26	Tue 17/02/26
1411	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Wed 18/02/26	Wed 18/02/26
1412	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Wed 18/02/26	Wed 18/02/26
1413	Day 10 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Thu 19/02/26	Thu 19/02/26
1414	Day 11 - Slab pour, pour 1	0%	1 day	Thu 19/02/26	Thu 19/02/26
1415	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Fri 20/02/26	Fri 20/02/26
1416	Day 13 - Slab pour, pour 2	0%	1 day	Sat 21/02/26	Sat 21/02/26
1417	LEVEL 10 – 1,400m2	0%	14 days	Fri 20/02/26	Wed 11/03/26
1418	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Fri 20/02/26	Fri 20/02/26
1419	Day 1 - Install pour one column cages	0%	1 day	Fri 20/02/26	Fri 20/02/26
1420	Day 1 - Commence precast install	0%	1 day	Fri 20/02/26	Fri 20/02/26
1421	Day 1 - Commence formwork to columns	0%	1 day	Fri 20/02/26	Fri 20/02/26
1422	Day 2 - Continue Precast	0%	1 day	Tue 24/02/26	Tue 24/02/26
1423	Day 2 - Continue forming columns	0%	1 day	Sat 21/02/26	Sat 21/02/26
1424	Day 3 - Install pour 2 column cages	0%	1 day	Tue 24/02/26	Tue 24/02/26
1425	Day 3 - Continue Precast	0%	1 day	Wed 25/02/26	Wed 25/02/26
1426	Day 3 - Commence shoring (6 men)	0%	1 day	Tue 24/02/26	Tue 24/02/26
1427	Day 3 - Pour columns to pour 1	0%	1 day	Tue 24/02/26	Tue 24/02/26
1428	Day 3 - Form columns pour 2	0%	1 day	Tue 24/02/26	Tue 24/02/26
1429	Day 4 - Complete precast installation	0%	1 day	Thu 26/02/26	Thu 26/02/26
1430	Day 4 - Continue shoring (6 men)	0%	1 day	Wed 25/02/26	Wed 25/02/26
1431	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Wed 25/02/26	Wed 25/02/26
1432	Day 4 - Continue forming pour 2 columns	0%	1 day	Wed 25/02/26	Wed 25/02/26
1433	Day 5 - Pour columns pour 2	0%	1 day	Thu 26/02/26	Thu 26/02/26
1434	Day 5 - Continue shoring (6 men)	0%	1 day	Thu 26/02/26	Thu 26/02/26
1435	Day 5 - Dog box works, caulking panels	0%	1 day	Fri 27/02/26	Fri 27/02/26
1436	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Sat 28/02/26	Sat 28/02/26
1437	Day 6 - Complete dog box works – caulking panels	0%	1 day	Sat 28/02/26	Sat 28/02/26
1438	Day 6 - Complete shoring (6 men)	0%	1 day	Fri 27/02/26	Fri 27/02/26
1439	Day 6 - Complete levelling pour 1	0%	1 day	Fri 27/02/26	Fri 27/02/26
1440	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Mon 2/03/26	Mon 2/03/26
1441	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Sat 28/02/26	Sat 28/02/26
1442	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Tue 3/03/26	Tue 3/03/26
1443	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Tue 3/03/26	Tue 3/03/26
1444	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Tue 3/03/26	Tue 3/03/26
1445	Day 9 - Reo delivery first thing	0%	1 day	Wed 4/03/26	Wed 4/03/26
1446	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Wed 4/03/26	Wed 4/03/26
1447	Day 9 - Commenced reo fixing	0%	1 day	Wed 4/03/26	Wed 4/03/26
1448	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Wed 4/03/26	Wed 4/03/26
1449	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Wed 4/03/26	Wed 4/03/26
1450	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Thu 5/03/26	Thu 5/03/26
1451	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Thu 5/03/26	Thu 5/03/26
1452	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Fri 6/03/26	Fri 6/03/26
1453	Day 11 - Slab pour, pour 1	0%	1 day	Fri 6/03/26	Fri 6/03/26
1454	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Sat 7/03/26	Sat 7/03/26
1455	Day 13 - Slab Pour, pour 2	0%	1 day	Wed 11/03/26	Wed 11/03/26
1456	LEVEL 11 - PENTHOUSE – 1,400m2	0%	14 days	Sat 7/03/26	Thu 26/03/26
1457	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Sat 7/03/26	Sat 7/03/26
1458	Day 1 - Install pour one column cages	0%	1 day	Sat 7/03/26	Sat 7/03/26
1459	Day 1 - Commence precast install	0%	1 day	Sat 7/03/26	Sat 7/03/26
1460	Day 1 - Commence formwork to columns	0%	1 day	Sat 7/03/26	Sat 7/03/26
1461	Day 2 - Continue Precast	0%	1 day	Thu 12/03/26	Thu 12/03/26
1462	Day 2 - Continue forming columns	0%	1 day	Wed 11/03/26	Wed 11/03/26
1463	Day 3 - Install pour 2 column cages	0%	1 day	Thu 12/03/26	Thu 12/03/26
1464	Day 3 - Continue Precast	0%	1 day	Fri 13/03/26	Fri 13/03/26
1465	Day 3 - Commence shoring (6 men)	0%	1 day	Thu 12/03/26	Thu 12/03/26
1466	Day 3 - Pour columns to pour 1	0%	1 day	Thu 12/03/26	Thu 12/03/26
1467	Day 3 - Form columns pour 2	0%	1 day	Thu 12/03/26	Thu 12/03/26
1468	Day 4 - Complete precast installation	0%	1 day	Sat 14/03/26	Sat 14/03/26
1469	Day 4 - Continue shoring (6 men)	0%	1 day	Fri 13/03/26	Fri 13/03/26
1470	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Fri 13/03/26	Fri 13/03/26
1471	Day 4 - Continue forming pour 2 columns	0%	1 day	Fri 13/03/26	Fri 13/03/26
1472	Day 5 - Pour columns pour 2	0%	1 day	Sat 14/03/26	Sat 14/03/26
1473	Day 5 - Continue shoring (6 men)	0%	1 day	Sat 14/03/26	Sat 14/03/26
1474	Day 5 - Dog box works, caulking panels	0%	1 day	Mon 16/03/26	Mon 16/03/26
1475	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Tue 17/03/26	Tue 17/03/26
1476	Day 6 - Complete dog box works – caulking panels	0%	1 day	Tue 17/03/26	Tue 17/03/26
1477	Day 6 - Complete shoring (6 men)	0%	1 day	Mon 16/03/26	Mon 16/03/26
1478	Day 6 - Complete levelling pour 1	0%	1 day	Mon 16/03/26	Mon 16/03/26
1479	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Wed 18/03/26	Wed 18/03/26
1480	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Tue 17/03/26	Tue 17/03/26
1481	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Thu 19/03/26	Thu 19/03/26
1482	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Thu 19/03/26	Thu 19/03/26
1483	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Thu 19/03/26	Thu 19/03/26
1484	Day 9 - Reo delivery first thing	0%	1 day	Fri 20/03/26	Fri 20/03/26
1485	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Fri 20/03/26	Fri 20/03/26
1486	Day 9 - Commenced reo fixing	0%	1 day	Fri 20/03/26	Fri 20/03/26
1487	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Fri 20/03/26	Fri 20/03/26
1488	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Fri 20/03/26	Fri 20/03/26
1489	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Sat 21/03/26	Sat 21/03/26
1490	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Sat 21/03/26	Sat 21/03/26
1491	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Tue 24/03/26	Tue 24/03/26
1492	Day 11 - Slab pour, pour 1	0%	1 day	Tue 24/03/26	Tue 24/03/26
1493	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Wed 25/03/26	Wed 25/03/26
1494	Day 13 - Slab Pour, pour 2	0%	1 day	Thu 26/03/26	Thu 26/03/26
1495	LEVEL 12 - ROOF – 1,400m2	0%	13 days	Wed 25/03/26	Mon 13/04/26
1496	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Wed 25/03/26	Wed 25/03/26
1497	Day 1 - Install pour one column cages	0%	1 day	Wed 25/03/26	Wed 25/03/26
1498	Day 1 - Commence precast install	0%	1 day	Wed 25/03/26	Wed 25/03/26
