ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1	5041 - ARC BOWDEN APARTMENTS PROJECT	52%	491 days	Mon 18/11/24	Tue 13/10/26
2	KEY MILESTONES	0%	449 days	Thu 23/01/25	Tue 13/10/26
18	OFF SITE WORKS	78%	427 days	Mon 18/11/24	Tue 21/07/26
1023	ON SITE WORKS	17%	459 days	Tue 19/11/24	Mon 31/08/26
1024	SITE ESTABLISHMENT	100%	54 days	Sat 18/01/25	Mon 31/03/25
1028	SITE CLEARANCE	100%	17 days	Fri 17/01/25	Sat 8/02/25
1030	CONSTRUCTION (EARLY WORKS)	100%	102 days	Mon 17/02/25	Sat 5/07/25
1046	SUPERSTRUCTURE	68%	185 days	Mon 14/07/25	Mon 13/04/26
1047	LEVEL 1 – 2,200m2 CARPARK	100%	38 days	Mon 14/07/25	Tue 19/08/25
1048	Zone A	100%	20 days	Mon 14/07/25	Thu 7/08/25
1049	SA Water fire main installation	100%	1 day	Fri 18/07/25	Fri 18/07/25
1050	Precast Concrete install (A+B)	100%	6 days	Mon 14/07/25	Sat 19/07/25
1051	Ground floor column pour	100%	1 day	Tue 15/07/25	Tue 15/07/25
1052	Ground floor strip columns	100%	1 day	Wed 16/07/25	Wed 16/07/25
1053	Bubbledeck false work	100%	5 days	Tue 15/07/25	Sat 19/07/25
1054	Bubbledeck installation ZONE (A)	100%	6 days	Thu 24/07/25	Thu 31/07/25
1055	Install scaffold handrail to live deck (pm)	100%	2 days	Wed 30/07/25	Thu 31/07/25
1056	Open live deck (pm)	100%	1 day	Thu 31/07/25	Thu 31/07/25
1057	Install (BD) reo	100%	2 days	Fri 1/08/25	Sat 2/08/25
1058	Install screw in bars	100%	1 day	Fri 1/08/25	Fri 1/08/25
1059	Install services	100%	2 days	Fri 1/08/25	Sat 2/08/25
1060	Install setdowns	100%	1 day	Tue 5/08/25	Tue 5/08/25
1061	Concrete pour floor slab Zone [A] pour (1)	100%	1 day	Wed 6/08/25	Wed 6/08/25
1062	Concrete pour floor slab Zone [A] pour (2)	100%	1 day	Thu 7/08/25	Thu 7/08/25
1063	Zone B	100%	22 days	Wed 23/07/25	Tue 19/08/25
1064	Bubbledeck false work	100%	14 days	Wed 23/07/25	Sat 9/08/25
1065	Bubbledeck installation ZONE (B)	100%	2 days	Mon 11/08/25	Tue 12/08/25
1066	Install scaffold handrail to live deck (pm)	100%	2 days	Mon 11/08/25	Tue 12/08/25
1067	Open live deck (pm)	100%	1 day	Tue 12/08/25	Tue 12/08/25
1068	Install (BD) reo	100%	3 days	Wed 13/08/25	Fri 15/08/25
1069	Install screw in bars	100%	2 days	Wed 13/08/25	Thu 14/08/25
1070	Install services	100%	3 days	Wed 13/08/25	Fri 15/08/25
1071	Install setdowns	100%	1 day	Sat 16/08/25	Sat 16/08/25
1072	Concrete pour floor slab Zone [B] pour (1)	100%	1 day	Mon 18/08/25	Mon 18/08/25
1073	Concrete pour floor slab Zone [B] pour (2)	100%	1 day	Tue 19/08/25	Tue 19/08/25
1074	LEVEL 2 – 2,200m2 CARPARK	100%	36 days	Thu 7/08/25	Thu 25/09/25
1075	Zone A	100%	23 days	Thu 7/08/25	Fri 5/09/25
1076	Strip slab edge and set downs - tidy up	100%	1 day	Thu 7/08/25	Thu 7/08/25
1077	Survey - columns set out	100%	1 day	Thu 7/08/25	Thu 7/08/25
1078	Survey - as built slab	100%	1 day	Thu 7/08/25	Thu 7/08/25
1079	Survey - precast wall panels set out	100%	1 day	Thu 7/08/25	Thu 7/08/25
1080	Survey - Bubbledeck panels set out	100%	1 day	Thu 7/08/25	Thu 7/08/25
1081	Jump the stretcher stairs	100%	3 days	Thu 7/08/25	Sat 9/08/25
1082	Jump the Hoist	100%	1 day	Fri 8/08/25	Fri 8/08/25
1083	Lift column cages	100%	1 day	Thu 7/08/25	Thu 7/08/25
1084	Column cage reo inspection sign off	100%	1 day	Thu 7/08/25	Thu 7/08/25
1085	Lift column formwork	100%	1 day	Thu 7/08/25	Thu 7/08/25
1086	Column formwork install	100%	2 days	Thu 7/08/25	Fri 8/08/25
1087	Pour concrete columns	100%	2 days	Fri 8/08/25	Sat 9/08/25
1088	Strip and remove column form work	100%	1 day	Mon 11/08/25	Mon 11/08/25
1089	Install precast wall panels	100%	7 days	Fri 8/08/25	Fri 15/08/25
1090	Lift BD false work	100%	4 days	Thu 7/08/25	Mon 11/08/25
1091	Install BD false work	100%	9 days	Tue 12/08/25	Thu 21/08/25
1092	BD false work inspection and sign off	100%	1 day	Thu 21/08/25	Thu 21/08/25
1093	Install BD panels	100%	3 days	Fri 22/08/25	Mon 25/08/25
1094	Install scaffold handrail to live deck (pm)	100%	4 days	Fri 22/08/25	Tue 26/08/25
1095	Open Live deck (pm)	100%	1 day	Tue 26/08/25	Tue 26/08/25
1096	Lift BD reo	100%	1 day	Wed 27/08/25	Wed 27/08/25
1097	Install BD reo	100%	1 day	Wed 27/08/25	Wed 27/08/25
1098	Install services	100%	1 day	Wed 27/08/25	Thu 28/08/25
1099	Pre-pour engineer inspections inspections Zone [A]	100%	0 days	Thu 28/08/25	Thu 28/08/25
1100	Install set downs	100%	0 days	Thu 28/08/25	Thu 28/08/25
1101	Concrete pour floor slab Zone [A] pour (1)	100%	0 days	Fri 29/08/25	Fri 29/08/25
1102	Concrete Pour beam + ramp infill Zone [B]	100%	0 days	Fri 29/08/25	Fri 29/08/25
1103	Concrete pour floor slab Zone [A] pour (2)	100%	1 day	Fri 5/09/25	Fri 5/09/25
1104	Zone B	100%	26 days	Tue 19/08/25	Thu 25/09/25
1105	Strip slab edge and set downs - tidy up	100%	1 day	Tue 19/08/25	Tue 19/08/25
1106	Survey - columns set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1107	Survey - as built slab	100%	1 day	Tue 19/08/25	Tue 19/08/25
1108	Survey - precast wall panels set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1109	Survey - Bubbledeck panels set out	100%	1 day	Tue 19/08/25	Tue 19/08/25
1110	Jump the stretcher stairs	100%	1 day	Tue 19/08/25	Tue 19/08/25
1111	Lift column cages	100%	1 day	Tue 19/08/25	Tue 19/08/25
1112	Column cage reo inspection sign off	100%	1 day	Tue 19/08/25	Tue 19/08/25
1113	Lift column formwork	100%	1 day	Tue 19/08/25	Tue 19/08/25
1114	Column formwork install	100%	2 days	Tue 19/08/25	Wed 20/08/25
1115	Pour concrete columns	100%	1 day	Wed 20/08/25	Wed 20/08/25
1116	Strip and remove column form work	100%	1 day	Thu 21/08/25	Thu 21/08/25
1117	Install precast wall panels	100%	2 days	Wed 20/08/25	Thu 21/08/25
1118	Lift BD false work	100%	1 day	Tue 26/08/25	Tue 26/08/25
1119	Install BD false work	100%	5 days	Wed 27/08/25	Thu 4/09/25
1120	BD false work inspection and sign off	100%	1 day	Thu 4/09/25	Thu 4/09/25
1121	Install BD panels	100%	3 days	Thu 4/09/25	Sat 6/09/25
1122	Install scaffold handrail to live deck (pm)	100%	1 day	Sat 6/09/25	Sat 6/09/25
1123	Open Live deck (pm)	100%	1 day	Sat 6/09/25	Sat 6/09/25
1124	Lift BD reo	100%	1 day	Sat 6/09/25	Sat 6/09/25
1125	Install BD reo	100%	1 day	Sat 6/09/25	Sat 6/09/25
1126	Lift screw in bars	100%	1 day	Sat 6/09/25	Sat 6/09/25
1127	Install screw in bars	100%	1 day	Tue 9/09/25	Tue 9/09/25
1128	Install services	100%	1 day	Tue 9/09/25	Tue 9/09/25
1129	Pre-pour engineer inspections inspections Zone [B]	100%	1 day	Tue 9/09/25	Tue 9/09/25
1130	Install set downs	100%	1 day	Tue 9/09/25	Tue 9/09/25

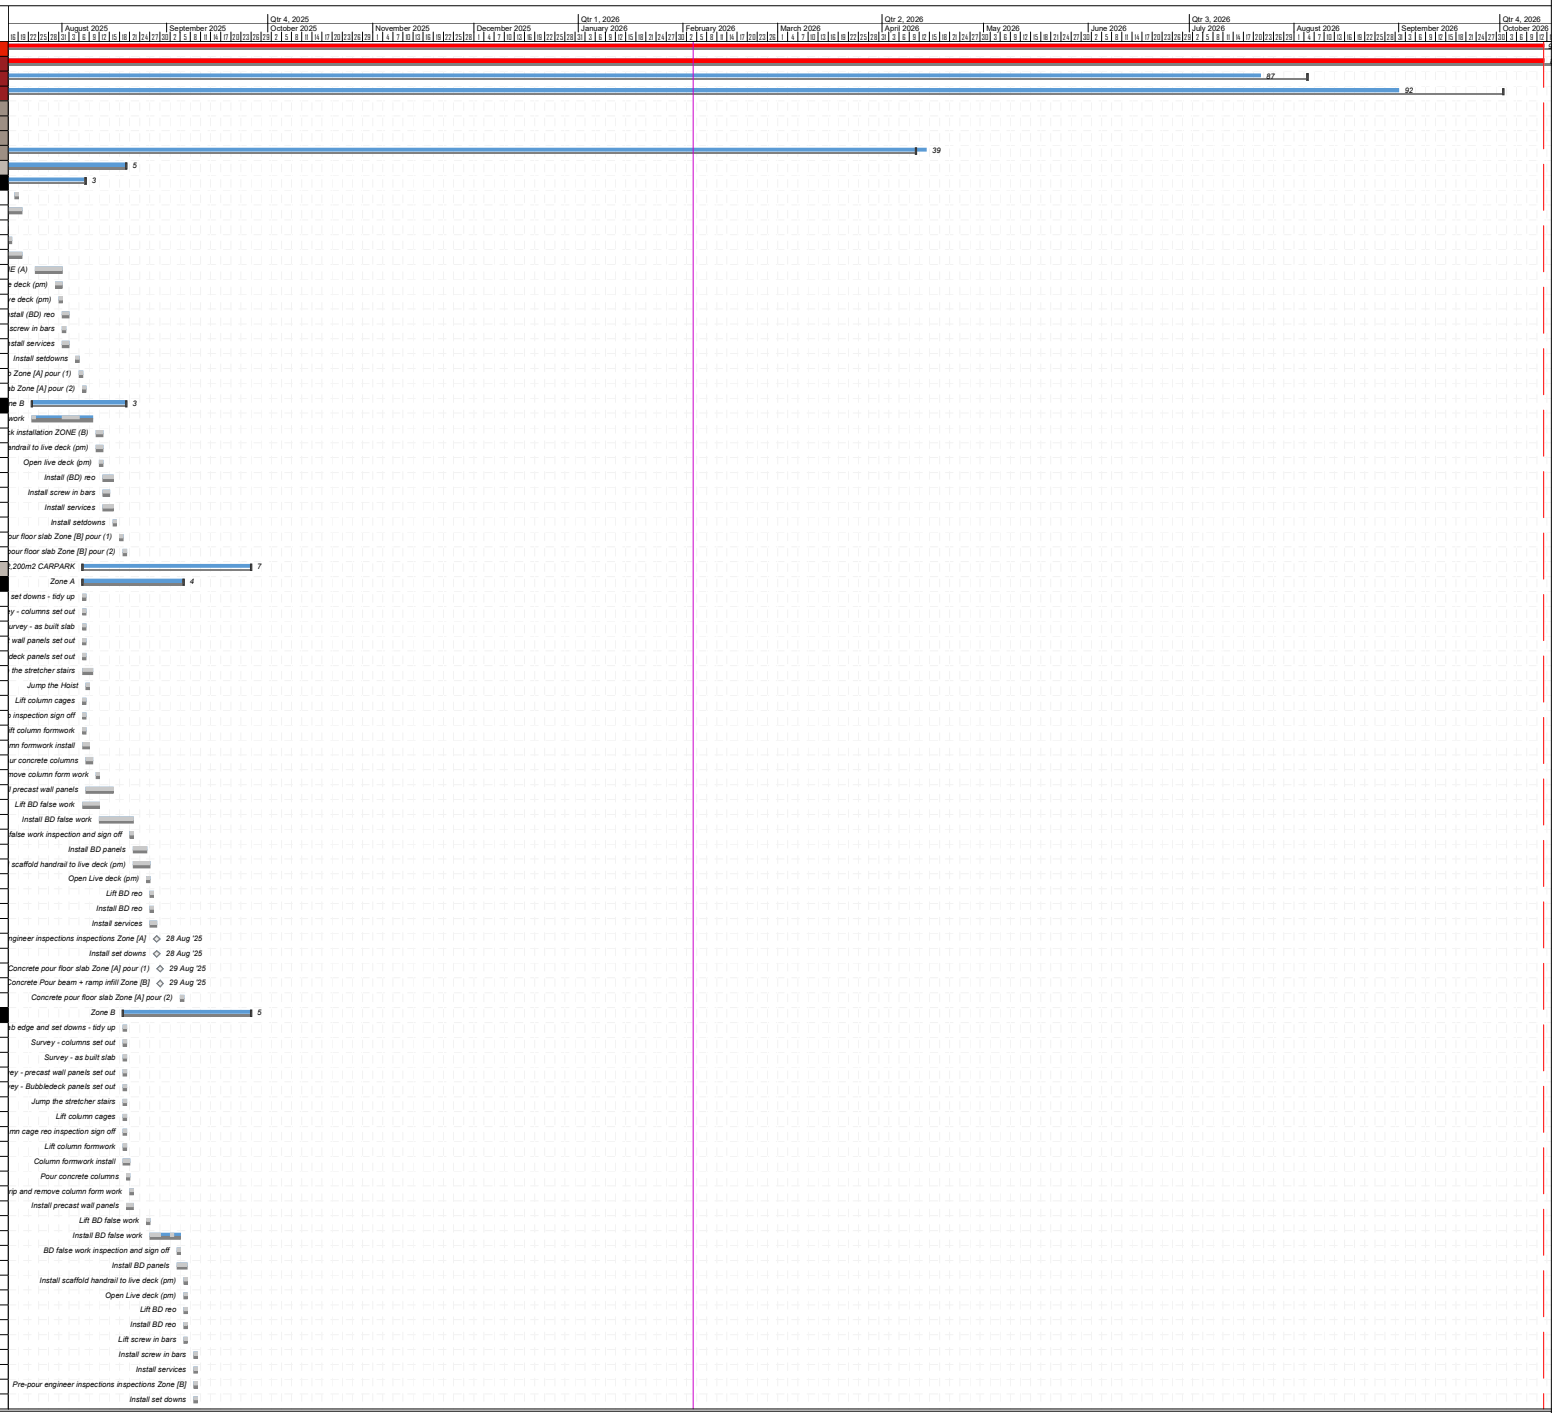

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

Planner: **Steve Church** Review: **Marcus Anderson**

ID	Name	% Complete	Duration	Start	Finish
1131	Concrete pour floor slab Zone [B] pour (3)	100%	1 day	Wed 10/09/25	Wed 10/09/25
1132	Concrete pour floor slab Zone [B] pour (4) (Exlcudes 1.2m strip adjacent West Precast)	100%	1 day	Fri 12/09/25	Fri 12/09/25
1133	Precast wall panels to the west side (Double late)	100%	2 days	Sat 20/09/25	Tue 23/09/25
1134	Concrete Pour (5) - Install Threaded Rod and Pour 1.2m Strip	100%	2 days	Wed 24/09/25	Thu 25/09/25
1135	LEVEL 3 ~ 2,200m2 PODIUM	100%	31 days	Tue 2/09/25	Wed 8/10/25
1136	**Zone A**	**100%**	**25 days**	**Tue 2/09/25**	**Wed 8/10/25**
1137	Strip slab edge and set downs - tidy up	100%	1 day	Tue 2/09/25	Tue 2/09/25
1138	Survey - columns set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1139	Survey - as built slab	100%	1 day	Tue 2/09/25	Tue 2/09/25
1140	Survey - precast wall panels set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1141	Survey - Bubbledeck panels set out	100%	1 day	Tue 2/09/25	Tue 2/09/25
1142	Jump the stretcher stairs	100%	1 day	Tue 2/09/25	Tue 2/09/25
1143	Jump the Hoist	100%	1 day	Wed 3/09/25	Wed 3/09/25
1144	Install precast wall panels	100%	2 days	Wed 3/09/25	Thu 4/09/25
1145	Lift BD false work	100%	1 day	Sat 6/09/25	Sat 6/09/25
1146	Install BD false work	100%	7 days	Sat 6/09/25	Mon 15/09/25
1147	BD false work inspection and sign off	100%	1 day	Mon 15/09/25	Mon 15/09/25
1148	Install BD panels	100%	3 days	Fri 12/09/25	Mon 15/09/25
1149	Install scaffold handrail to live deck (pm)	100%	1 day	Fri 19/09/25	Fri 19/09/25
1150	Open Live deck (pm)	100%	1 day	Fri 19/09/25	Fri 19/09/25
1151	Lift BD reo	100%	1 day	Fri 19/09/25	Fri 19/09/25
1152	Install BD reo	100%	2 days	Thu 2/10/25	Fri 3/10/25
1153	Lift screw in bars	100%	1 day	Fri 19/09/25	Fri 19/09/25
1154	Install screw in bars	100%	1 day	Fri 19/09/25	Fri 19/09/25
1155	Install services	100%	2 days	Thu 2/10/25	Fri 3/10/25
1156	Pre-pour engineer inspections inspections Zone [A]	100%	1 day	Wed 24/09/25	Wed 24/09/25
1157	Install set downs	100%	1 day	Fri 3/10/25	Fri 3/10/25
1158	Concrete pour floor slab Zone [A] pour (1)	100%	1 day	Fri 26/09/25	Fri 26/09/25
1159	Concrete pour floor slab Zone [A] pour (2)	100%	**1 day**	Wed 8/10/25	Wed 8/10/25
1160	**Zone B**	**100%**	**24 days**	**Thu 11/09/25**	**Wed 15/10/25**
1161	Strip slab edge and set downs - tidy up	100%	4 days	Thu 11/09/25	Mon 15/09/25
1162	Survey - columns set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1163	Survey - as built slab	100%	4 days	Thu 11/09/25	Mon 15/09/25
1164	Survey - precast wall panels set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1165	Survey - Bubbledeck panels set out	100%	4 days	Thu 11/09/25	Mon 15/09/25
1166	Jump the stretcher stairs	100%	4 days	Thu 11/09/25	Mon 15/09/25
1167	Lift BD false work	100%	4 days	Thu 11/09/25	Mon 15/09/25
1168	Install BD false work	100%	8 days	Thu 11/09/25	Tue 23/09/25
1169	BD false work inspection and sign off	100%	1 day	Tue 23/09/25	Tue 23/09/25
1170	Install BD panels	100%	3 days	Wed 24/09/25	Fri 26/09/25
1171	Install scaffold handrail to live deck (pm)	100%	2 days	Thu 25/09/25	Fri 26/09/25
1172	Open Live deck (pm)	100%	1 day	Fri 26/09/25	Fri 26/09/25
1173	Lift BD reo	100%	1 day	Fri 26/09/25	Fri 26/09/25
1174	Install BD reo	100%	2 days	Sat 27/09/25	Mon 29/09/25
1175	Lift screw in bars	100%	1 day	Sat 27/09/25	Sat 27/09/25
1176	Install screw in bars	100%	1 day	Mon 29/09/25	Mon 29/09/25
1177	Install services	100%	2 days	Sat 27/09/25	Mon 29/09/25
1178	Pre-pour engineer inspections inspections Zone [B]	100%	1 day	Fri 10/10/25	Fri 10/10/25
1179	Install set downs	100%	3 days	Sat 11/10/25	Tue 14/10/25
1180	Concrete pour floor slab and Columns Zone [B] pour (1)	100%	4 days	Thu 9/10/25	Mon 13/10/25
1181	Concrete pour floor slab and Columns Zone [B] pour (2)	100%	1 day	Wed 15/10/25	Wed 15/10/25
1182	LEVEL 4 ~ 1,400m2	100%	21 days	Thu 2/10/25	Tue 4/11/25
1183	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Thu 2/10/25	Thu 2/10/25
1184	Day 1 - Install pour one column cages	100%	1 day	Thu 2/10/25	Thu 2/10/25
1185	Day 1 - Commence precast install	100%	1 day	Thu 9/10/25	Thu 9/10/25
1186	Day 1 - Commence formwork to columns	100%	1 day	Thu 2/10/25	Thu 2/10/25
1187	Day 2 - Continue Precast	100%	1 day	Thu 9/10/25	Thu 9/10/25
1188	Day 2 - Continue forming columns	100%	1 day	Thu 9/10/25	Thu 9/10/25
1189	Day 3 - Install pour 2 column cages	100%	1 day	Fri 10/10/25	Fri 10/10/25
1190	Day 3 - Continue Precast	100%	2 days	Fri 10/10/25	Sat 11/10/25
1191	Day 3 - Commence shoring (6 men)	100%	1 day	Tue 14/10/25	Tue 14/10/25
1192	Day 3 - Pour columns to pour 1	100%	1 day	Fri 10/10/25	Fri 10/10/25
1193	Day 3 - Form columns pour 2	100%	1 day	Fri 10/10/25	Fri 10/10/25
1194	Day 4 - Complete precast installation	100%	1 day	Mon 13/10/25	Mon 13/10/25
1195	Day 4 - Continue shoring (6 men)	100%	1 day	Wed 15/10/25	Wed 15/10/25
1196	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Sat 11/10/25	Sat 11/10/25
1197	Day 4 - Continue forming pour 2 columns	100%	1 day	Sat 11/10/25	Sat 11/10/25
1198	Day 5 - Pour columns pour 2	100%	1 day	Mon 13/10/25	Mon 13/10/25
1199	Day 5 - Continue shoring (6 men)	100%	1 day	Thu 16/10/25	Thu 16/10/25
1200	Day 5 - Dog box works, caulking panels	100%	1 day	Tue 14/10/25	Tue 14/10/25
1201	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Wed 15/10/25	Wed 15/10/25
1202	Day 6 - Complete dog box works – caulking panels	100%	1 day	Wed 15/10/25	Wed 15/10/25
1203	Day 6 - Complete shoring (6 men)	100%	1 day	Fri 17/10/25	Fri 17/10/25
1204	Day 6 - Complete levelling pour 1	100%	1 day	Fri 17/10/25	Fri 17/10/25
1205	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Sat 18/10/25	Sat 18/10/25
1206	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Sat 18/10/25	Sat 18/10/25
1207	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Thu 23/10/25	Thu 23/10/25
1208	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Thu 23/10/25	Thu 23/10/25
1209	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Thu 23/10/25	Thu 23/10/25
1210	Day 9 - Reo delivery first thing	100%	1 day	Fri 24/10/25	Fri 24/10/25
1211	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Fri 24/10/25	Fri 24/10/25
1212	Day 9 - Commenced reo fixing	100%	1 day	Fri 24/10/25	Fri 24/10/25
1213	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Fri 24/10/25	Fri 24/10/25
1214	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Fri 24/10/25	Fri 24/10/25
1215	Day 10 - Continue Reo fixing, complete pour 1 & setdowns	100%	2 days	Sat 25/10/25	Mon 27/10/25
1216	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	2 days	Sat 25/10/25	Mon 27/10/25
1217	Day 11 - Continue reo fixing, complete pour 2 & setdowns	100%	2 days	Tue 28/10/25	Wed 29/10/25
1218	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	2 days	Wed 29/10/25	Thu 30/10/25
1219	Day 11 - Slab pour, pour 1	100%	1 day	Fri 31/10/25	Fri 31/10/25
1220	Day 12 - Slab pour, pour 2	100%	1 day	Tue 4/11/25	Tue 4/11/25
1221	LEVEL 5 ~ 1,400m2	100%	16 days	Sat 1/11/25	Sat 22/11/25
1222	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Sat 1/11/25	Sat 1/11/25

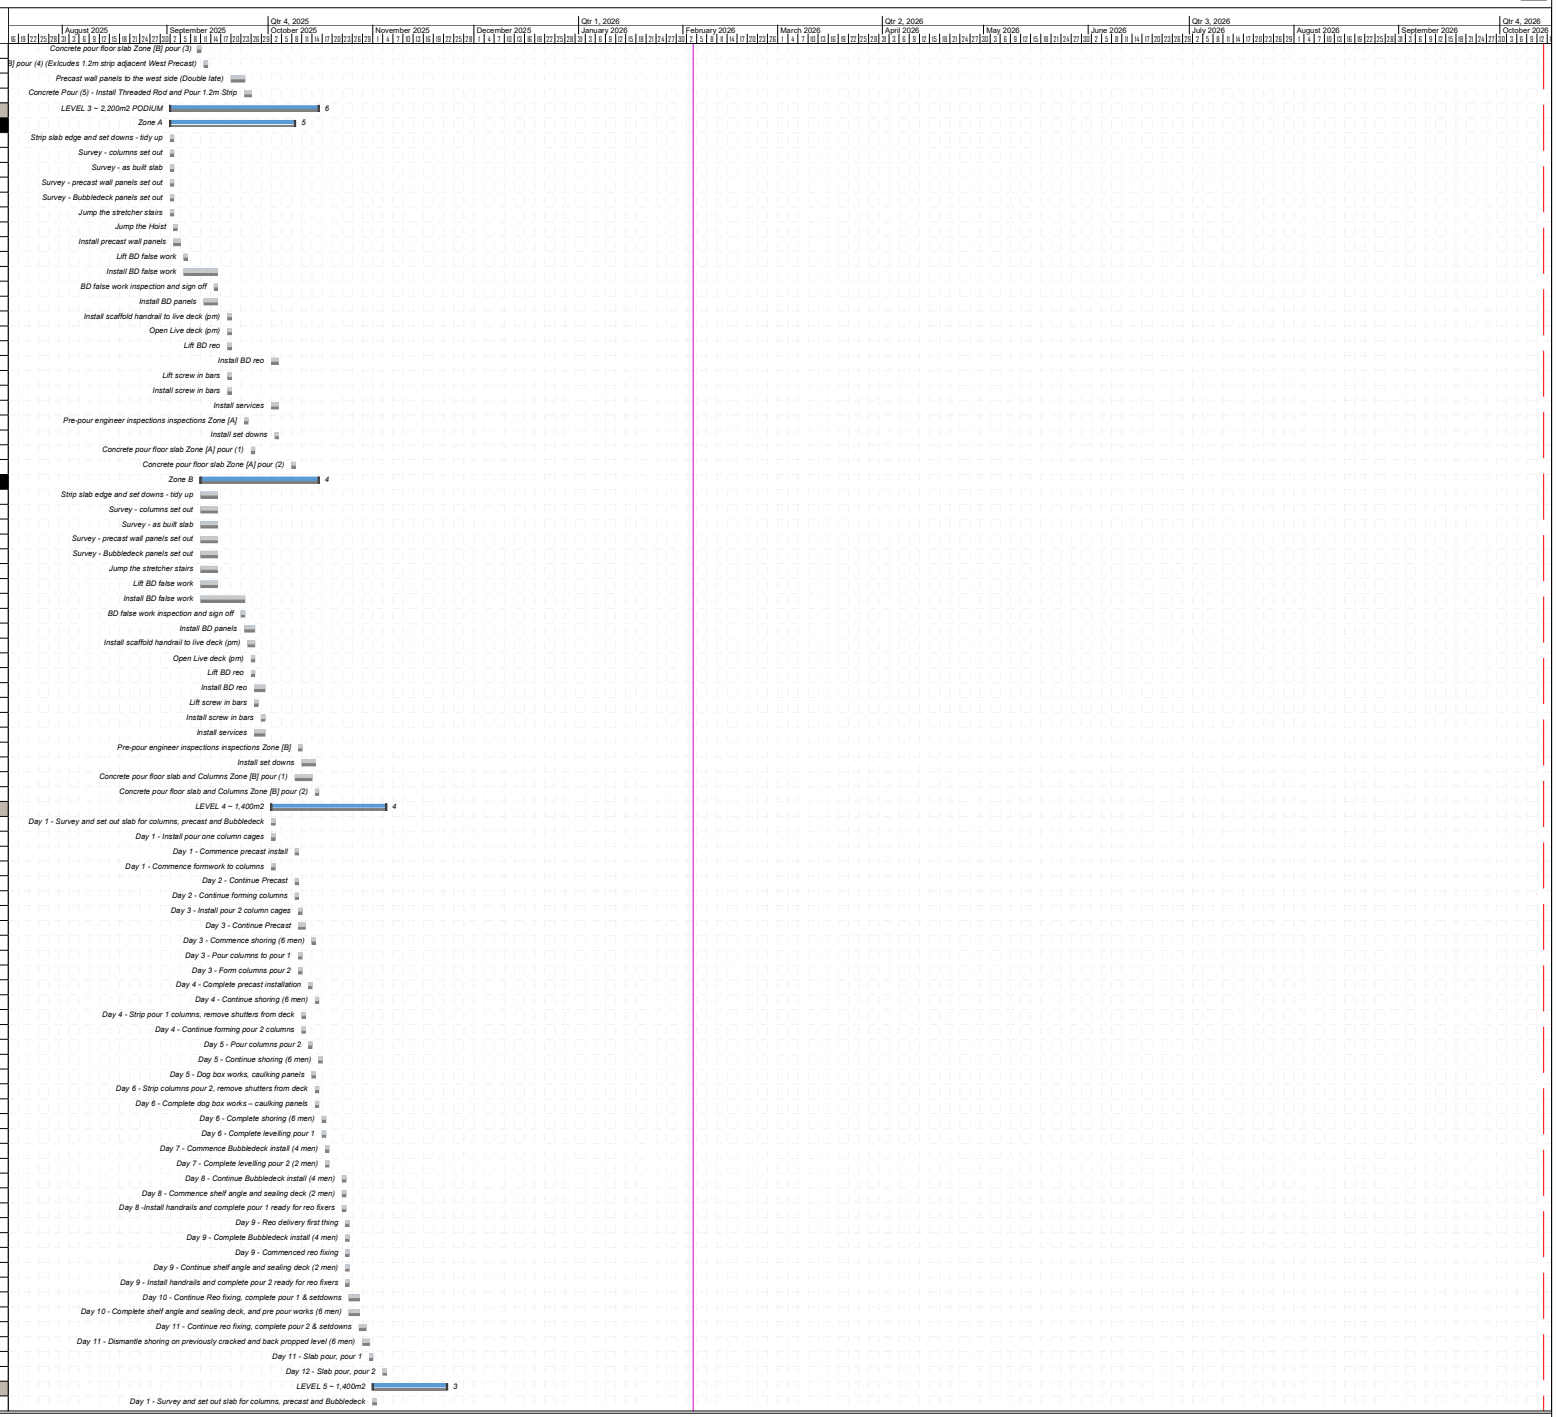

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Milestone | Summary | Critical | Critical Milestone | Client Tasks | Client Milestones | Baseline | Baseline Milestone | Baseline Summary | Progress | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
1223	Day 1 - Install pour one column cages	100%	1 day	Sat 1/11/25	Sat 1/11/25
1224	Day 1 - Commence precast install	100%	1 day	Tue 4/11/25	Tue 4/11/25
1225	Day 1 - Commence formwork to columns	100%	1 day	Tue 4/11/25	Tue 4/11/25
1226	Day 2 - Continue Precast	100%	1 day	Wed 5/11/25	Wed 5/11/25
1227	Day 2 - Continue forming columns	100%	1 day	Wed 5/11/25	Wed 5/11/25
1228	Day 3 - Install pour 2 column cages	100%	1 day	Fri 7/11/25	Fri 7/11/25
1229	Day 3 - Continue Precast	100%	1 day	Thu 6/11/25	Thu 6/11/25
1230	Day 3 - Commence shoring (6 men)	100%	1 day	Thu 6/11/25	Thu 6/11/25
1231	Day 3 - Pour columns to pour 1	100%	1 day	Thu 6/11/25	Thu 6/11/25
1232	Day 3 - Form columns pour 2	100%	1 day	Fri 7/11/25	Fri 7/11/25
1233	Day 4 - Complete precast installation	100%	1 day	Fri 7/11/25	Fri 7/11/25
1234	Day 4 - Continue shoring (6 men)	100%	1 day	Fri 7/11/25	Fri 7/11/25
1235	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Fri 7/11/25	Fri 7/11/25
1236	Day 4 - Continue forming pour 2 columns	100%	1 day	Fri 7/11/25	Fri 7/11/25
1237	Day 5 - Pour columns pour 2	100%	1 day	Mon 10/11/25	Mon 10/11/25
1238	Day 5 - Continue shoring (6 men)	100%	1 day	Sat 8/11/25	Sat 8/11/25
1239	Day 5 - Dog box works, caulking panels	100%	1 day	Sat 8/11/25	Sat 8/11/25
1240	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Tue 11/11/25	Tue 11/11/25
1241	Day 6 - Complete dog box works – caulking panels	100%	1 day	Mon 10/11/25	Mon 10/11/25
1242	Day 6 - Complete shoring (6 men)	100%	1 day	Mon 10/11/25	Mon 10/11/25
1243	Day 6 - Complete levelling pour 1	100%	1 day	Mon 10/11/25	Mon 10/11/25
1244	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Tue 11/11/25	Tue 11/11/25
1245	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Tue 11/11/25	Tue 11/11/25
1246	Day 8 - Continue Bubbledeck install (4 men)	100%	2 days	Wed 12/11/25	Thu 13/11/25
1247	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Wed 12/11/25	Wed 12/11/25
1248	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Wed 12/11/25	Wed 12/11/25
1249	Day 9 - Reo delivery first thing	100%	1 day	Fri 14/11/25	Fri 14/11/25
1250	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Fri 14/11/25	Fri 14/11/25
1251	Day 9 - Commenced reo fixing	100%	1 day	Fri 14/11/25	Fri 14/11/25
1252	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Thu 13/11/25	Thu 13/11/25
1253	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Thu 13/11/25	Thu 13/11/25
1254	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	1 day	Wed 19/11/25	Wed 19/11/25
1255	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Fri 14/11/25	Fri 14/11/25
1256	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	1 day	Fri 21/11/25	Fri 21/11/25
1257	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	1 day	Sat 15/11/25	Sat 15/11/25
1258	Day 11 - Slab pour, pour 1	100%	1 day	Fri 21/11/25	Fri 21/11/25
1259	Day 12 - Slab pour, pour 2	100%	1 day	Sat 22/11/25	Sat 22/11/25
1260	LEVEL 6 ~ 1,400m2	100%	14 days	Sat 8/22/11/25	Wed 8/10/12/25
1261	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Mon 24/11/25	Mon 24/11/25
1262	Day 1 - Install pour one column cages	100%	1 day	Mon 24/11/25	Mon 24/11/25
1263	Day 1 - Commence precast install	100%	1 day	Mon 24/11/25	Mon 24/11/25
1264	Day 1 - Commence formwork to columns	100%	1 day	Sat 22/11/25	Sat 22/11/25
1265	Day 2 - Continue Precast	100%	1 day	Tue 25/11/25	Tue 25/11/25
1266	Day 2 - Continue forming columns	100%	1 day	Tue 25/11/25	Tue 25/11/25
1267	Day 3 - Install pour 2 column cages	100%	1 day	Wed 26/11/25	Wed 26/11/25
1268	Day 3 - Continue Precast	100%	1 day	Wed 26/11/25	Wed 26/11/25
1269	Day 3 - Commence shoring (6 men)	100%	1 day	Wed 26/11/25	Wed 26/11/25
1270	Day 3 - Pour columns to pour 1	100%	1 day	Wed 26/11/25	Wed 26/11/25
1271	Day 3 - Form columns pour 2	100%	1 day	Wed 26/11/25	Wed 26/11/25
1272	Day 4 - Complete precast installation	100%	1 day	Thu 27/11/25	Thu 27/11/25
1273	Day 4 - Continue shoring (6 men)	100%	1 day	Thu 27/11/25	Thu 27/11/25
1274	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Thu 27/11/25	Thu 27/11/25
1275	Day 4 - Continue forming pour 2 columns	100%	1 day	Thu 27/11/25	Thu 27/11/25
1276	Day 5 - Pour columns pour 2	100%	1 day	Fri 28/11/25	Fri 28/11/25
1277	Day 5 - Continue shoring (6 men)	100%	1 day	Fri 28/11/25	Fri 28/11/25
1278	Day 5 - Dog box works, caulking panels	100%	1 day	Fri 28/11/25	Fri 28/11/25
1279	Day 6 - Strip columns pour 2, remove shutters from deck	100%	1 day	Tue 2/12/25	Tue 2/12/25
1280	Day 6 - Complete dog box works – caulking panels	100%	1 day	Tue 2/12/25	Tue 2/12/25
1281	Day 6 - Complete shoring (6 men)	100%	1 day	Tue 2/12/25	Tue 2/12/25
1282	Day 6 - Complete levelling pour 1	100%	1 day	Tue 2/12/25	Tue 2/12/25
1283	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Wed 3/12/25	Wed 3/12/25
1284	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Wed 3/12/25	Wed 3/12/25
1285	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1286	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1287	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Thu 4/12/25	Thu 4/12/25
1288	Day 9 - Reo delivery first thing	100%	1 day	Thu 4/12/25	Thu 4/12/25
1289	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1290	Day 9 - Commenced reo fixing	100%	1 day	Thu 4/12/25	Thu 4/12/25
1291	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1292	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Thu 4/12/25	Thu 4/12/25
1293	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	3 days	Thu 4/12/25	Sat 6/12/25
1294	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Thu 4/12/25	Thu 4/12/25
1295	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	2 days	Mon 8/12/25	Tue 9/12/25
1296	Day 11 - Dismantle shoring on previously cracked and back propped level (6 men)	100%	2 days	Fri 5/12/25	Sat 6/12/25
1297	Day 11 - Slab pour, pour 1	100%	1 day	Mon 8/12/25	Mon 8/12/25
1298	Day 12 - Strip Slab Edging and prepare for Pour 2	100%	1 day	Tue 9/12/25	Tue 9/12/25
1299	Day 13 - Slab pour, pour 2	100%	1 day	Wed 10/12/25	Wed 10/12/25
1300	LEVEL 7 ~ 1,400m2	99%	17 days	Tue 9/12/25	Sat 17/01/26
1301	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	100%	1 day	Tue 9/12/25	Tue 9/12/25
1302	Day 1 - Install pour one column cages	100%	1 day	Tue 9/12/25	Tue 9/12/25
1303	Day 1 - Commence precast install	100%	1 day	Tue 9/12/25	Tue 9/12/25
1304	Day 1 - Commence formwork to columns	100%	1 day	Tue 9/12/25	Tue 9/12/25
1305	Day 2 - Continue Precast	100%	1 day	Thu 11/12/25	Thu 11/12/25
1306	Day 2 - Continue forming columns	100%	1 day	Wed 10/12/25	Wed 10/12/25
1307	Day 3 - Install pour 2 column cages	100%	1 day	Thu 11/12/25	Thu 11/12/25
1308	Day 3 - Continue Precast	100%	1 day	Fri 12/12/25	Fri 12/12/25
1309	Day 3 - Commence shoring (6 men)	100%	1 day	Thu 11/12/25	Thu 11/12/25
1310	Day 3 - Pour columns to pour 1	100%	1 day	Thu 11/12/25	Thu 11/12/25
1311	Day 3 - Form columns pour 2	100%	1 day	Thu 11/12/25	Thu 11/12/25
1312	Day 4 - Complete precast installation	100%	1 day	Sat 13/12/25	Sat 13/12/25
1313	Day 4 - Continue shoring (6 men)	100%	1 day	Fri 12/12/25	Fri 12/12/25
1314	Day 4 - Strip pour 1 columns, remove shutters from deck	100%	1 day	Fri 12/12/25	Fri 12/12/25

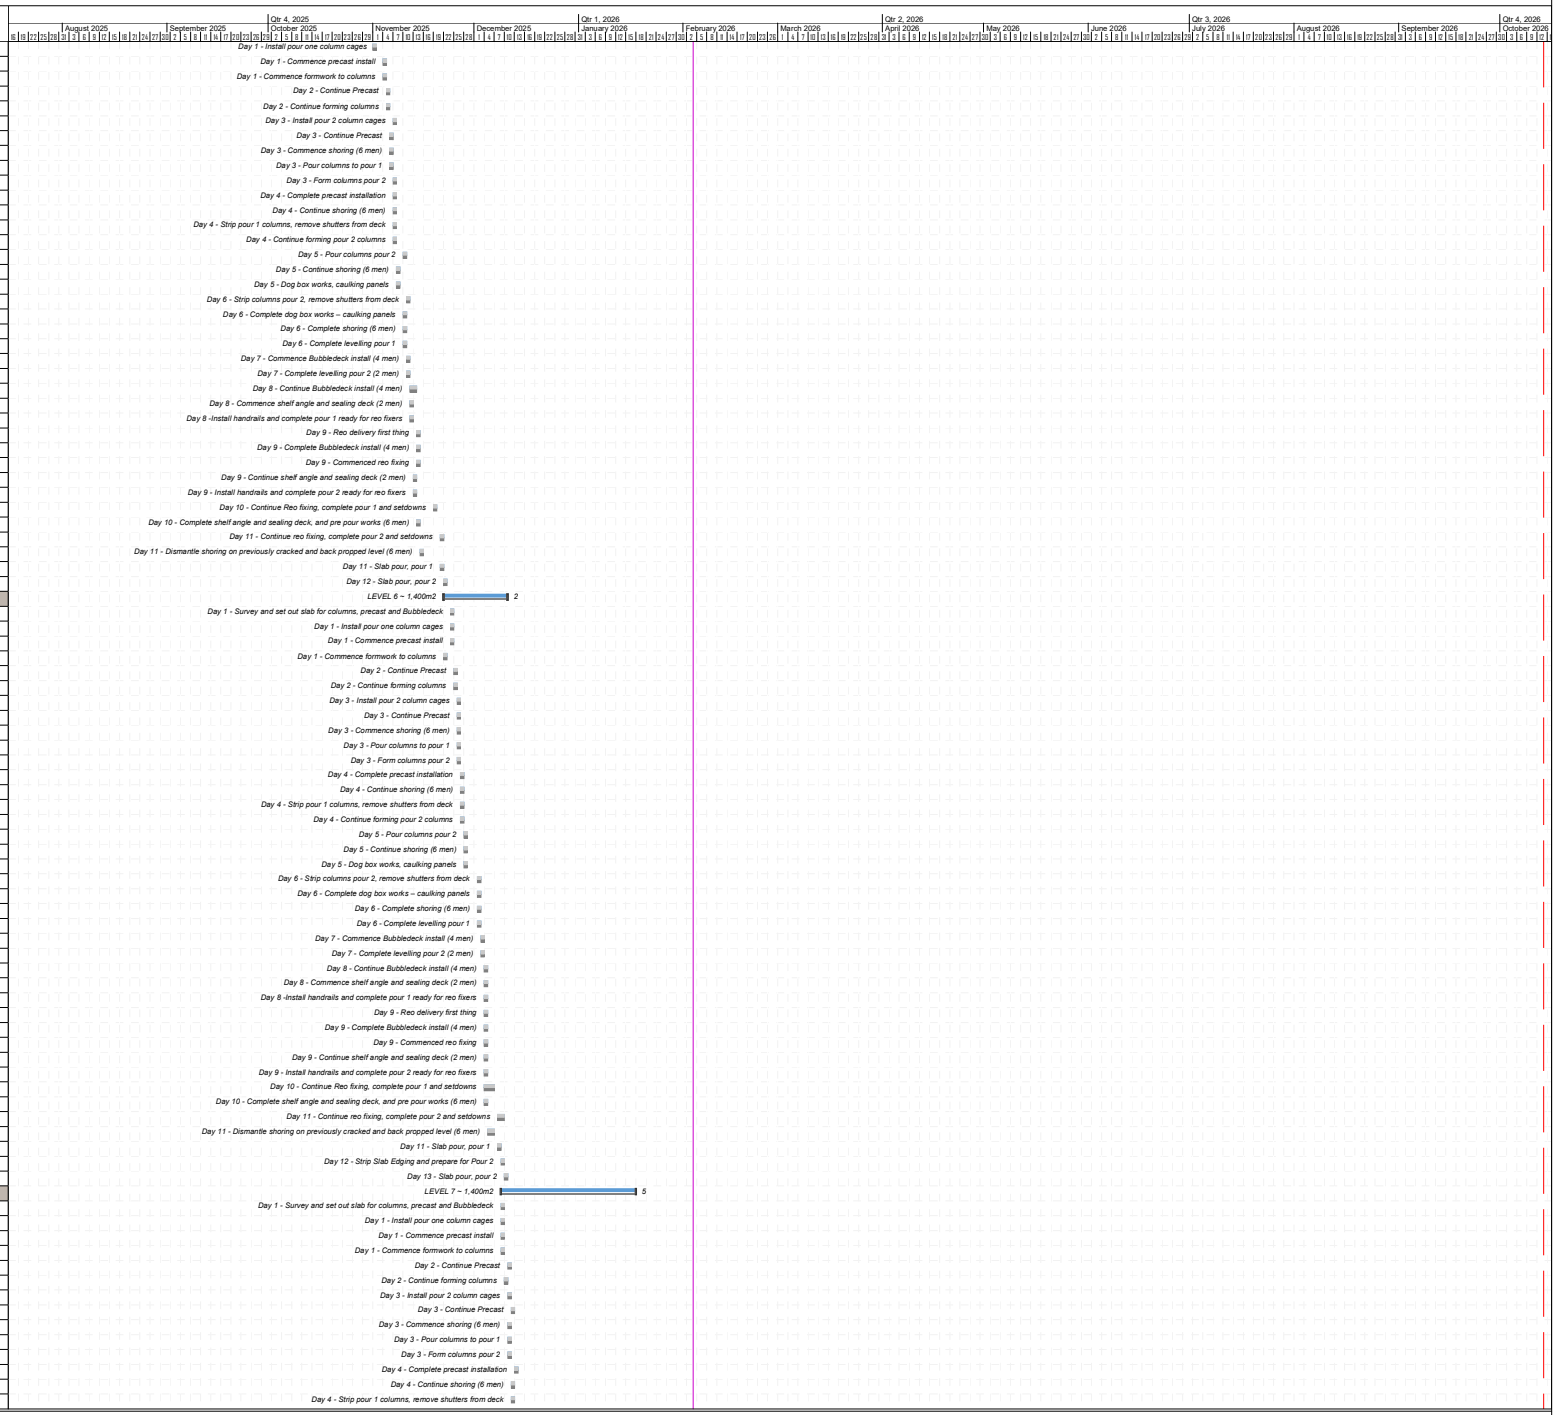

ID	Name	% Complete	Duration	Start	Finish
1315	Day 4 - Continue forming pour 2 columns	100%	1 day	Fri 12/12/25	Fri 12/12/25
1316	Day 5 - Pour columns pour 2	100%	1 day	Sat 13/12/25	Sat 13/12/25
1317	Day 5 - Continue shoring (6 men)	100%	1 day	Sat 13/12/25	Sat 13/12/25
1318	Day 5 - Dog box works, caulking panels	100%	1 day	Mon 15/12/25	Mon 15/12/25
1319	Day 6 - Strip columns pour 2, remove shutters from deck	100%	3 days	Tue 16/12/25	Thu 18/12/25
1320	Day 6 - Complete dog box works – caulking panels	100%	1 day	Tue 16/12/25	Tue 16/12/25
1321	Day 6 - Complete shoring (6 men)	100%	1 day	Mon 15/12/25	Mon 15/12/25
1322	Day 6 - Complete levelling pour 1	100%	1 day	Mon 15/12/25	Mon 15/12/25
1323	Day 7 - Commence Bubbledeck install (4 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1324	Day 7 - Complete levelling pour 2 (2 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1325	Day 8 - Continue Bubbledeck install (4 men)	100%	1 day	Tue 13/01/26	Tue 13/01/26
1326	Day 8 - Commence shelf angle and sealing deck (2 men)	100%	2 days	Mon 12/01/26	Tue 13/01/26
1327	Day 8 -Install handrails and complete pour 1 ready for reo fixers	100%	1 day	Tue 13/01/26	Tue 13/01/26
1328	Day 9 - Reo delivery first thing	100%	1 day	Mon 12/01/26	Mon 12/01/26
1329	Day 9 - Complete Bubbledeck install (4 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1330	Day 9 - Commenced reo fixing	100%	1 day	Mon 12/01/26	Mon 12/01/26
1331	Day 9 - Continue shelf angle and sealing deck (2 men)	100%	1 day	Mon 12/01/26	Mon 12/01/26
1332	Day 9 - Install handrails and complete pour 2 ready for reo fixers	100%	1 day	Sat 13/12/25	Sat 13/12/25
1333	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	100%	2 days	Tue 13/01/26	Wed 14/01/26
1334	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	100%	1 day	Wed 14/01/26	Wed 14/01/26
1335	Day 11 - Continue reo fixing, complete pour 2 and setdowns	100%	1 day	Thu 15/01/26	Thu 15/01/26
1336	Day 11 - Slab pour, pour 1	100%	0 days	Thu 15/01/26	Thu 15/01/26
1337	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Fri 16/01/26	Fri 16/01/26
1338	Day 13 - Slab pour, pour 2	0%	1 day	Sat 17/01/26	Sat 17/01/26
1339	LEVEL 8 – 1,400m2	0%	16 days	Fri 16/01/26	Fri 6/02/26
1340	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Fri 16/01/26	Fri 16/01/26
1341	Day 1 - Install pour one column cages	0%	1 day	Fri 16/01/26	Fri 16/01/26
1342	Day 1 - Commence precast install	0%	1 day	Sat 17/01/26	Sat 17/01/26
1343	Day 1 - Commence formwork to columns	0%	1 day	Sat 17/01/26	Sat 17/01/26
1344	Day 2 - Continue Precast	0%	1 day	Mon 19/01/26	Mon 19/01/26
1345	Day 2 - Continue forming columns	0%	1 day	Mon 19/01/26	Mon 19/01/26
1346	Day 3 - Install pour 2 column cages	0%	1 day	Tue 20/01/26	Tue 20/01/26
1347	Day 3 - Continue Precast	0%	1 day	Tue 20/01/26	Tue 20/01/26
1348	Day 3 - Commence shoring (6 men)	0%	1 day	Tue 20/01/26	Tue 20/01/26
1349	Day 3 - Pour columns to pour 1	0%	1 day	Tue 20/01/26	Tue 20/01/26
1350	Day 3 - Form columns pour 2	0%	1 day	Tue 20/01/26	Tue 20/01/26
1351	Day 4 - Complete precast installation	0%	1 day	Wed 21/01/26	Wed 21/01/26
1352	Day 4 - Continue shoring (6 men)	0%	1 day	Wed 21/01/26	Wed 21/01/26
1353	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Wed 21/01/26	Wed 21/01/26
1354	Day 4 - Continue forming pour 2 columns	0%	1 day	Wed 21/01/26	Wed 21/01/26
1355	Day 5 - Pour columns pour 2	0%	1 day	Thu 22/01/26	Thu 22/01/26
1356	Day 5 - Continue shoring (6 men)	0%	1 day	Thu 22/01/26	Thu 22/01/26
1357	Day 5 - Dog box works, caulking panels	0%	1 day	Thu 22/01/26	Thu 22/01/26
1358	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Fri 23/01/26	Fri 23/01/26
1359	Day 6 - Complete dog box works – caulking panels	0%	1 day	Fri 23/01/26	Fri 23/01/26
1360	Day 6 - Complete shoring (6 men)	0%	1 day	Fri 23/01/26	Fri 23/01/26
1361	Day 6 - Complete levelling pour 1	0%	1 day	Fri 23/01/26	Fri 23/01/26
1362	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Wed 28/01/26	Wed 28/01/26
1363	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Wed 28/01/26	Wed 28/01/26
1364	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Thu 29/01/26	Thu 29/01/26
1365	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Thu 29/01/26	Thu 29/01/26
1366	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Thu 29/01/26	Thu 29/01/26
1367	Day 9 - Reo delivery first thing	0%	1 day	Fri 30/01/26	Fri 30/01/26
1368	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Fri 30/01/26	Fri 30/01/26
1369	Day 9 - Commenced reo fixing	0%	1 day	Fri 30/01/26	Fri 30/01/26
1370	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Fri 30/01/26	Fri 30/01/26
1371	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Fri 30/01/26	Fri 30/01/26
1372	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Sat 31/01/26	Sat 31/01/26
1373	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Sat 31/01/26	Sat 31/01/26
1374	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Mon 2/02/26	Mon 2/02/26
1375	Day 11 - Slab pour, pour 1	0%	1 day	Wed 4/02/26	Wed 4/02/26
1376	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Thu 5/02/26	Thu 5/02/26
1377	Day 13 - Slab Pour, pour 2	0%	1 day	Fri 6/02/26	Fri 6/02/26
1378	LEVEL 9 – 1,400m2	0%	14 days	Thu 5/02/26	Sat 21/02/26
1379	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Thu 5/02/26	Thu 5/02/26
1380	Day 1 - Install pour one column cages	0%	1 day	Thu 5/02/26	Thu 5/02/26
1381	Day 1 - Commence precast install	0%	1 day	Thu 5/02/26	Thu 5/02/26
1382	Day 1 - Commence formwork to columns	0%	1 day	Thu 5/02/26	Thu 5/02/26
1383	Day 2 - Continue Precast	0%	1 day	Sat 7/02/26	Sat 7/02/26
1384	Day 2 - Continue forming columns	0%	1 day	Fri 6/02/26	Fri 6/02/26
1385	Day 3 - Install pour 2 column cages	0%	1 day	Sat 7/02/26	Sat 7/02/26
1386	Day 3 - Continue Precast	0%	1 day	Tue 10/02/26	Tue 10/02/26
1387	Day 3 - Commence shoring (6 men)	0%	1 day	Sat 7/02/26	Sat 7/02/26
1388	Day 3 - Pour columns to pour 1	0%	1 day	Sat 7/02/26	Sat 7/02/26
1389	Day 3 - Form columns pour 2	0%	1 day	Sat 7/02/26	Sat 7/02/26
1390	Day 4 - Complete precast installation	0%	1 day	Wed 11/02/26	Wed 11/02/26
1391	Day 4 - Continue shoring (6 men)	0%	1 day	Tue 10/02/26	Tue 10/02/26
1392	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Tue 10/02/26	Tue 10/02/26
1393	Day 4 - Continue forming pour 2 columns	0%	1 day	Tue 10/02/26	Tue 10/02/26
1394	Day 5 - Pour columns pour 2	0%	1 day	Wed 11/02/26	Wed 11/02/26
1395	Day 5 - Continue shoring (6 men)	0%	1 day	Wed 11/02/26	Wed 11/02/26
1396	Day 5 - Dog box works, caulking panels	0%	1 day	Thu 12/02/26	Thu 12/02/26
1397	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Fri 13/02/26	Fri 13/02/26
1398	Day 6 - Complete dog box works – caulking panels	0%	1 day	Fri 13/02/26	Fri 13/02/26
1399	Day 6 - Complete shoring (6 men)	0%	1 day	Thu 12/02/26	Thu 12/02/26
1400	Day 6 - Complete levelling pour 1	0%	1 day	Thu 12/02/26	Thu 12/02/26
1401	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Sat 14/02/26	Sat 14/02/26
1402	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Fri 13/02/26	Fri 13/02/26
1403	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Mon 16/02/26	Mon 16/02/26
1404	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Mon 16/02/26	Mon 16/02/26
1405	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Mon 16/02/26	Mon 16/02/26
1406	Day 9 - Reo delivery first thing	0%	1 day	Tue 17/02/26	Tue 17/02/26

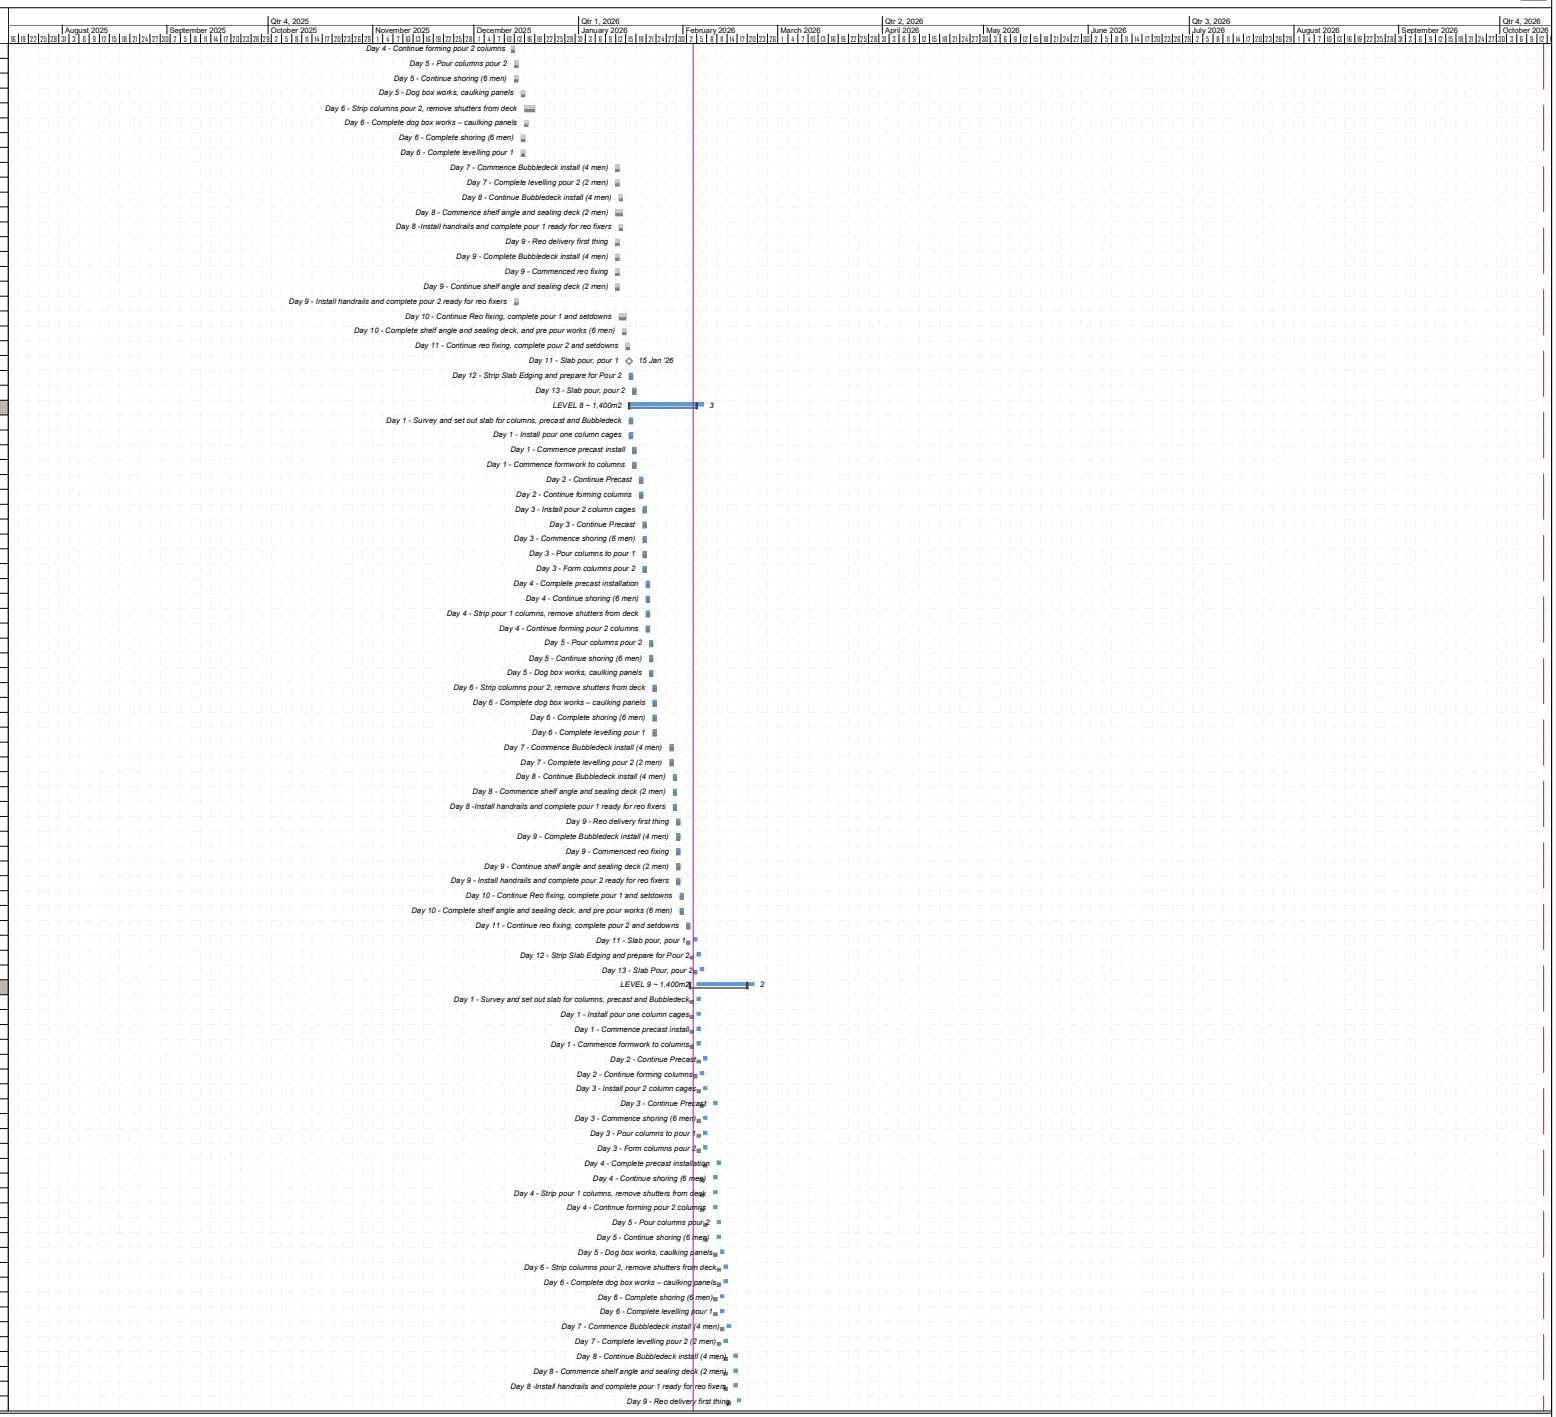

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Milestone | Summary | Critical | Critical Milestone | Client Tasks | Client Milestones | Baseline | Baseline Milestone | Baseline Summary | Progress | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
1407	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Tue 17/02/26	Tue 17/02/26
1408	Day 9 - Commenced reo fixing	0%	1 day	Tue 17/02/26	Tue 17/02/26
1409	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Tue 17/02/26	Tue 17/02/26
1410	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Tue 17/02/26	Tue 17/02/26
1411	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Wed 18/02/26	Wed 18/02/26
1412	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Wed 18/02/26	Wed 18/02/26
1413	Day 10 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Thu 19/02/26	Thu 19/02/26
1414	Day 11 - Slab pour, pour 1	0%	1 day	Thu 19/02/26	Thu 19/02/26
1415	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Fri 20/02/26	Fri 20/02/26
1416	Day 13 - Slab pour, pour 2	0%	1 day	Sat 21/02/26	Sat 21/02/26
1417	LEVEL 10 – 1,400m2	0%	14 days	Fri 20/02/26	Wed 11/03/26
1418	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Fri 20/02/26	Fri 20/02/26
1419	Day 1 - Install pour one column cages	0%	1 day	Fri 20/02/26	Fri 20/02/26
1420	Day 1 - Commence precast install	0%	1 day	Fri 20/02/26	Fri 20/02/26
1421	Day 1 - Commence formwork to columns	0%	1 day	Fri 20/02/26	Fri 20/02/26
1422	Day 2 - Continue Precast	0%	1 day	Tue 24/02/26	Tue 24/02/26
1423	Day 2 - Continue forming columns	0%	1 day	Sat 21/02/26	Sat 21/02/26
1424	Day 3 - Install pour 2 column cages	0%	1 day	Tue 24/02/26	Tue 24/02/26
1425	Day 3 - Continue Precast	0%	1 day	Wed 25/02/26	Wed 25/02/26
1426	Day 3 - Commence shoring (6 men)	0%	1 day	Tue 24/02/26	Tue 24/02/26
1427	Day 3 - Pour columns to pour 1	0%	1 day	Tue 24/02/26	Tue 24/02/26
1428	Day 3 - Form columns pour 2	0%	1 day	Tue 24/02/26	Tue 24/02/26
1429	Day 4 - Complete precast installation	0%	1 day	Thu 26/02/26	Thu 26/02/26
1430	Day 4 - Continue shoring (6 men)	0%	1 day	Wed 25/02/26	Wed 25/02/26
1431	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Wed 25/02/26	Wed 25/02/26
1432	Day 4 - Continue forming pour 2 columns	0%	1 day	Wed 25/02/26	Wed 25/02/26
1433	Day 5 - Pour columns pour 2	0%	1 day	Thu 26/02/26	Thu 26/02/26
1434	Day 5 - Continue shoring (6 men)	0%	1 day	Thu 26/02/26	Thu 26/02/26
1435	Day 5 - Dog box works, caulking panels	0%	1 day	Fri 27/02/26	Fri 27/02/26
1436	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Sat 28/02/26	Sat 28/02/26
1437	Day 6 - Complete dog box works – caulking panels	0%	1 day	Sat 28/02/26	Sat 28/02/26
1438	Day 6 - Complete shoring (6 men)	0%	1 day	Fri 27/02/26	Fri 27/02/26
1439	Day 6 - Complete levelling pour 1	0%	1 day	Fri 27/02/26	Fri 27/02/26
1440	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Mon 2/03/26	Mon 2/03/26
1441	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Sat 28/02/26	Sat 28/02/26
1442	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Tue 3/03/26	Tue 3/03/26
1443	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Tue 3/03/26	Tue 3/03/26
1444	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Tue 3/03/26	Tue 3/03/26
1445	Day 9 - Reo delivery first thing	0%	1 day	Wed 4/03/26	Wed 4/03/26
1446	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Wed 4/03/26	Wed 4/03/26
1447	Day 9 - Commenced reo fixing	0%	1 day	Wed 4/03/26	Wed 4/03/26
1448	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Wed 4/03/26	Wed 4/03/26
1449	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Wed 4/03/26	Wed 4/03/26
1450	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Thu 5/03/26	Thu 5/03/26
1451	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Thu 5/03/26	Thu 5/03/26
1452	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Fri 6/03/26	Fri 6/03/26
1453	Day 11 - Slab pour, pour 1	0%	1 day	Fri 6/03/26	Fri 6/03/26
1454	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Sat 7/03/26	Sat 7/03/26
1455	Day 13 - Slab Pour, pour 2	0%	1 day	Wed 11/03/26	Wed 11/03/26
1456	LEVEL 11 - PENTHOUSE – 1,400m2	0%	14 days	Sat 7/03/26	Thu 26/03/26
1457	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Sat 7/03/26	Sat 7/03/26
1458	Day 1 - Install pour one column cages	0%	1 day	Sat 7/03/26	Sat 7/03/26
1459	Day 1 - Commence precast install	0%	1 day	Sat 7/03/26	Sat 7/03/26
1460	Day 1 - Commence formwork to columns	0%	1 day	Sat 7/03/26	Sat 7/03/26
1461	Day 2 - Continue Precast	0%	1 day	Thu 12/03/26	Thu 12/03/26
1462	Day 2 - Continue forming columns	0%	1 day	Wed 11/03/26	Wed 11/03/26
1463	Day 3 - Install pour 2 column cages	0%	1 day	Thu 12/03/26	Thu 12/03/26
1464	Day 3 - Continue Precast	0%	1 day	Fri 13/03/26	Fri 13/03/26
1465	Day 3 - Commence shoring (6 men)	0%	1 day	Thu 12/03/26	Thu 12/03/26
1466	Day 3 - Pour columns to pour 1	0%	1 day	Thu 12/03/26	Thu 12/03/26
1467	Day 3 - Form columns pour 2	0%	1 day	Thu 12/03/26	Thu 12/03/26
1468	Day 4 - Complete precast installation	0%	1 day	Sat 14/03/26	Sat 14/03/26
1469	Day 4 - Continue shoring (6 men)	0%	1 day	Fri 13/03/26	Fri 13/03/26
1470	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Fri 13/03/26	Fri 13/03/26
1471	Day 4 - Continue forming pour 2 columns	0%	1 day	Fri 13/03/26	Fri 13/03/26
1472	Day 5 - Pour columns pour 2	0%	1 day	Sat 14/03/26	Sat 14/03/26
1473	Day 5 - Continue shoring (6 men)	0%	1 day	Sat 14/03/26	Sat 14/03/26
1474	Day 5 - Dog box works, caulking panels	0%	1 day	Mon 16/03/26	Mon 16/03/26
1475	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Tue 17/03/26	Tue 17/03/26
1476	Day 6 - Complete dog box works – caulking panels	0%	1 day	Tue 17/03/26	Tue 17/03/26
1477	Day 6 - Complete shoring (6 men)	0%	1 day	Mon 16/03/26	Mon 16/03/26
1478	Day 6 - Complete levelling pour 1	0%	1 day	Mon 16/03/26	Mon 16/03/26
1479	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Wed 18/03/26	Wed 18/03/26
1480	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Tue 17/03/26	Tue 17/03/26
1481	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Thu 19/03/26	Thu 19/03/26
1482	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Thu 19/03/26	Thu 19/03/26
1483	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Thu 19/03/26	Thu 19/03/26
1484	Day 9 - Reo delivery first thing	0%	1 day	Fri 20/03/26	Fri 20/03/26
1485	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Fri 20/03/26	Fri 20/03/26
1486	Day 9 - Commenced reo fixing	0%	1 day	Fri 20/03/26	Fri 20/03/26
1487	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Fri 20/03/26	Fri 20/03/26
1488	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Fri 20/03/26	Fri 20/03/26
1489	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Sat 21/03/26	Sat 21/03/26
1490	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Sat 21/03/26	Sat 21/03/26
1491	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Tue 24/03/26	Tue 24/03/26
1492	Day 11 - Slab pour, pour 1	0%	1 day	Tue 24/03/26	Tue 24/03/26
1493	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Wed 25/03/26	Wed 25/03/26
1494	Day 13 - Slab Pour, pour 2	0%	1 day	Thu 26/03/26	Thu 26/03/26
1495	LEVEL 12 - ROOF – 1,400m2	0%	13 days	Wed 25/03/26	Mon 13/04/26
1496	Day 1 - Survey and set out slab for columns, precast and Bubbledeck	0%	1 day	Wed 25/03/26	Wed 25/03/26
1497	Day 1 - Install pour one column cages	0%	1 day	Wed 25/03/26	Wed 25/03/26
1498	Day 1 - Commence precast install	0%	1 day	Wed 25/03/26	Wed 25/03/26

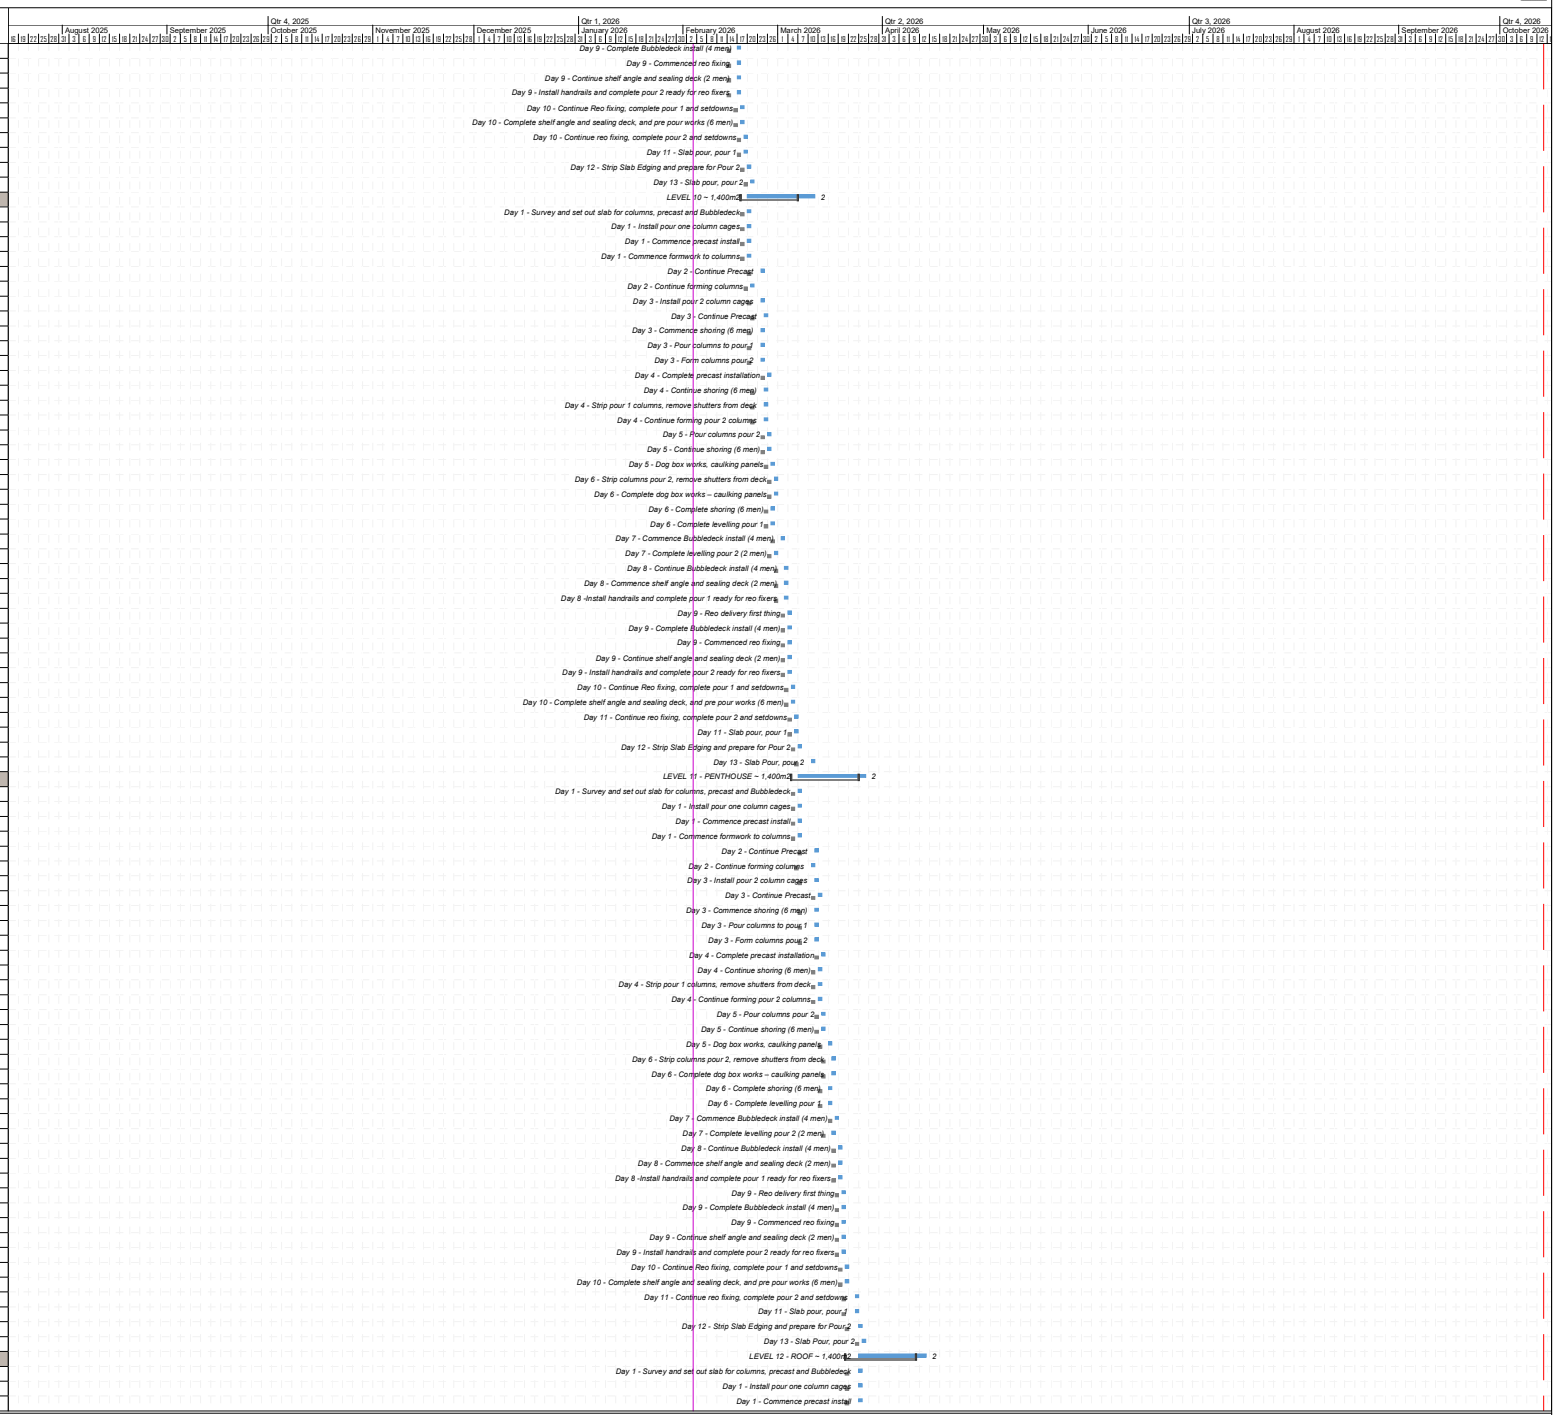

ID	Name	% Complete	Duration	Start	Finish
1499	Day 1 - Commence formwork to columns	0%	1 day	Wed 25/03/26	Wed 25/03/26
1500	Day 2 - Continue Precast	0%	1 day	Fri 27/03/26	Fri 27/03/26
1501	Day 2 - Continue forming columns	0%	1 day	Thu 26/03/26	Thu 26/03/26
1502	Day 3 - Install pour 2 column cages	0%	1 day	Fri 27/03/26	Fri 27/03/26
1503	Day 3 - Continue Precast	0%	1 day	Sat 28/03/26	Sat 28/03/26
1504	Day 3 - Commence shoring (6 men)	0%	1 day	Fri 27/03/26	Fri 27/03/26
1505	Day 3 - Pour columns to pour 1	0%	1 day	Fri 27/03/26	Fri 27/03/26
1506	Day 3 - Form columns pour 2	0%	1 day	Fri 27/03/26	Fri 27/03/26
1507	Day 4 - Complete precast installation	0%	1 day	Mon 30/03/26	Mon 30/03/26
1508	Day 4 - Continue shoring (6 men)	0%	1 day	Sat 28/03/26	Sat 28/03/26
1509	Day 4 - Strip pour 1 columns, remove shutters from deck	0%	1 day	Sat 28/03/26	Sat 28/03/26
1510	Day 4 - Continue forming pour 2 columns	0%	1 day	Sat 28/03/26	Sat 28/03/26
1511	Day 5 - Pour columns pour 2	0%	1 day	Mon 30/03/26	Mon 30/03/26
1512	Day 5 - Continue shoring (6 men)	0%	1 day	Mon 30/03/26	Mon 30/03/26
1513	Day 5 - Dog box works, caulking panels	0%	1 day	Tue 31/03/26	Tue 31/03/26
1514	Day 6 - Strip columns pour 2, remove shutters from deck	0%	1 day	Wed 1/04/26	Wed 1/04/26
1515	Day 6 - Complete dog box works – caulking panels	0%	1 day	Wed 1/04/26	Wed 1/04/26
1516	Day 6 - Complete shoring (6 men)	0%	1 day	Tue 31/03/26	Tue 31/03/26
1517	Day 6 - Complete levelling pour 1	0%	1 day	Tue 31/03/26	Tue 31/03/26
1518	Day 7 - Commence Bubbledeck install (4 men)	0%	1 day	Thu 2/04/26	Thu 2/04/26
1519	Day 7 - Complete levelling pour 2 (2 men)	0%	1 day	Wed 1/04/26	Wed 1/04/26
1520	Day 8 - Continue Bubbledeck install (4 men)	0%	1 day	Wed 8/04/26	Wed 8/04/26
1521	Day 8 - Commence shelf angle and sealing deck (2 men)	0%	1 day	Wed 8/04/26	Wed 8/04/26
1522	Day 8 -Install handrails and complete pour 1 ready for reo fixers	0%	1 day	Wed 8/04/26	Wed 8/04/26
1523	Day 9 - Reo delivery first thing	0%	1 day	Thu 9/04/26	Thu 9/04/26
1524	Day 9 - Complete Bubbledeck install (4 men)	0%	1 day	Thu 9/04/26	Thu 9/04/26
1525	Day 9 - Commenced reo fixing	0%	1 day	Thu 9/04/26	Thu 9/04/26
1526	Day 9 - Continue shelf angle and sealing deck (2 men)	0%	1 day	Thu 9/04/26	Thu 9/04/26
1527	Day 9 - Install handrails and complete pour 2 ready for reo fixers	0%	1 day	Thu 9/04/26	Thu 9/04/26
1528	Day 10 - Continue Reo fixing, complete pour 1 and setdowns	0%	1 day	Fri 10/04/26	Fri 10/04/26
1529	Day 10 - Complete shelf angle and sealing deck, and pre pour works (6 men)	0%	1 day	Fri 10/04/26	Fri 10/04/26
1530	Day 11 - Continue reo fixing, complete pour 2 and setdowns	0%	1 day	Sat 11/04/26	Sat 11/04/26
1531	Day 11 - Slab pour, pour 1	0%	1 day	Sat 11/04/26	Sat 11/04/26
1532	Day 12 - Strip Slab Edging and prepare for Pour 2	0%	1 day	Thu 9/04/26	Thu 9/04/26
1533	Day 13 - Slab Pour, pour 2	0%	1 day	Mon 13/04/26	Mon 13/04/26
1534	STRIP PROPS (50% Back to Individual Props to allow fitout to start)	34%	134 days	Thu 16/10/25	Thu 7/05/26
1535	Pour L03 / Strip Props L1 / Clear for Fitout GF	100%	4 days	Thu 16/10/25	Thu 23/10/25
1536	Pour L04/ Strip Props L2 / Clear for Fitout L1	100%	2 days	Tue 4/11/25	Thu 6/11/25
1537	Pour L05 / Strip Props L3 / Clear for Fitout L2	100%	4 days	Mon 24/11/25	Thu 27/11/25
1538	Pour L06 / Strip Props L4 / Clear for Fitout L3	100%	**3 days**	Wed 17/12/25	Fri 19/12/25
1539	Pour L07 / Strip Props L5 / Clear for Fitout L4	0%	**3 days**	Mon 19/01/26	Wed 21/01/26
1540	Pour L08 / Strip Props L6 / Clear for Fitout L5	0%	3 days	Sat 7/02/26	Wed 11/02/26
1541	Pour L9 / Strip Props L7 / Clear for Fitout L6	0%	3 days	Tue 24/02/26	Thu 26/02/26
1542	Pour L10 Penthouse / Strip Props L8 / Clear for Fitout L7	0%	3 days	Thu 12/03/26	Sat 14/03/26
1543	Pour L11 Roof / Strip Props L9 / Clear for Fitout L8	0%	3 days	Fri 27/03/26	Mon 30/03/26
1544	Pour L12 + Cure / Strip Props L10 / Clear for Fitout L9	0%	**3 days**	Tue 14/04/26	Thu 16/04/26
1545	Strip and Back Prop Underside Level 12	0%	1 day	Fri 17/04/26	Fri 17/04/26
1546	Curing L11 Penthouse /Clear for Fitout L10	0%	3 days	Fri 17/04/26	Mon 20/04/26
1547	Curing L12 / Clear for Fitout L11 Penthouse	0%	3 days	Tue 5/05/26	Thu 7/05/26
1548	ROOF PLANT INSTALLATION	0%	89 days	Tue 14/04/26	Thu 6/08/26
1549	Install Parapet wall/ Facia/ flashing and capping	0%	15 days	Tue 14/04/26	Sat 2/05/26
1550	FRP Services Plant plinth and Concrete Bunds	0%	10 days	Tue 14/04/26	Fri 24/04/26
1551	Roof Waterproofing	0%	6 days	Tue 5/05/26	Mon 11/05/26
1552	Deliver services plant before crane removal	0%	3 days	Tue 12/05/26	Thu 14/05/26
1553	Install mechanical Plants	0%	20 days	Fri 15/05/26	Thu 11/06/26
1554	Install Hydraulic Plants	0%	15 days	Tue 2/06/26	Mon 22/06/26
1555	Install Solar Panels	0%	6 days	Tue 23/06/26	Tue 30/06/26
1556	Roof Safety System / Access / Services	0%	**5 days**	Wed 1/07/26	Mon 6/07/26
1557	Plant Commissioning	0%	**25 days**	Tue 7/07/26	Thu 6/08/26
1558	FITOUT	9%	448.5 days	Tue 19/11/24	Tue 18/08/26
1559	FITOUT GROUND LEVEL - CARPARK / RETAIL	28%	439 days	Tue 19/11/24	Wed 5/08/26
1560	**High Level Services**	**100%**	**33 days**	**Fri 24/10/25**	**Sat 6/12/25**
1561	Hydraulic - High level services	100%	9 days	Fri 24/10/25	Wed 5/11/25
1562	Fire - High level services	100%	19 days	Thu 6/11/25	Fri 28/11/25
1563	Mechanical - High level services	100%	4 days	Tue 25/11/25	Fri 28/11/25
1564	Electrical + Com + Security - High level services	100%	13 days	Thu 20/11/25	Sat 6/12/25
1565	**Retail**	**23%**	**117 days**	**Tue 2/12/25**	**Tue 26/05/26**
1566	Head track survey + fixing	100%	2 days	Tue 2/12/25	Wed 3/12/25
1567	Studwall framing - PB Sheet 1 x side when possible	100%	5 days	Thu 4/12/25	Tue 9/12/25
1568	Ceiling framing + support bracing	100%	3 days	Wed 10/12/25	Fri 12/12/25
1569	Steel door frame installation	0%	1 day	Sat 31/01/26	Sat 31/01/26
1570	Paint - Door frame sealer[1]	0%	1 day	Mon 2/02/26	Mon 2/02/26
1571	Inspection + sign off - Services	0%	2 days	Tue 3/02/26	Wed 4/02/26
1572	2nd fix Services (Fire, Elec, Mech, Hyd)	0%	3 days	Thu 5/02/26	Sat 7/02/26
1573	Insulation installation to wall + ceiling	0%	1 day	Tue 10/02/26	Tue 10/02/26
1574	PB wall sheeting	0%	4 days	Wed 11/02/26	Sat 14/02/26
1575	PB bulkhead + ceiling sheeting	0%	4 days	Mon 16/02/26	Thu 19/02/26
1576	Flush + sand PB wall and ceiling (1)	0%	3 days	Fri 20/02/26	Tue 24/02/26
1577	Paint - Sealer coat to wall + ceiling [1]	0%	2 days	Wed 25/02/26	Thu 26/02/26
1578	Inspection + sign off - Flushing / Painting coat 1	0%	1 day	Fri 27/02/26	Fri 27/02/26
1579	Flush + sand PB wall and ceiling (2)	0%	2 days	Sat 28/02/26	Mon 2/03/26
1580	Flush + sand PB wall and ceiling (3)	0%	2 days	Tue 14/04/26	Wed 15/04/26
1581	Defect inspection and rectification & Handover	0%	3 days	Sat 16/05/26	Wed 20/05/26
1582	Commission + trade clean	0%	2 days	Thu 21/05/26	Fri 22/05/26
1583	10% Final clean	0%	3 days	Sat 23/05/26	Tue 26/05/26
1584	**Bathroom / End of Trip**	**0%**	**68 days**	**Wed 25/02/26**	**Wed 27/05/26**
1585	Screed wet area to fall	0%	2 days	Wed 25/02/26	Thu 26/02/26
1586	Waterproof / test wet area - membrane floor + wall	0%	2 days	Fri 27/02/26	Sat 28/02/26
1587	Floor tiling	0%	8 days	Mon 2/03/26	Thu 12/03/26
1588	Wall tiling	0%	8 days	Fri 13/03/26	Sat 21/03/26
1589	Grout + silicon seal	0%	2 days	Tue 24/03/26	Wed 25/03/26
1590	Sanitaryware + tapware	0%	4 days	Thu 26/03/26	Mon 30/03/26

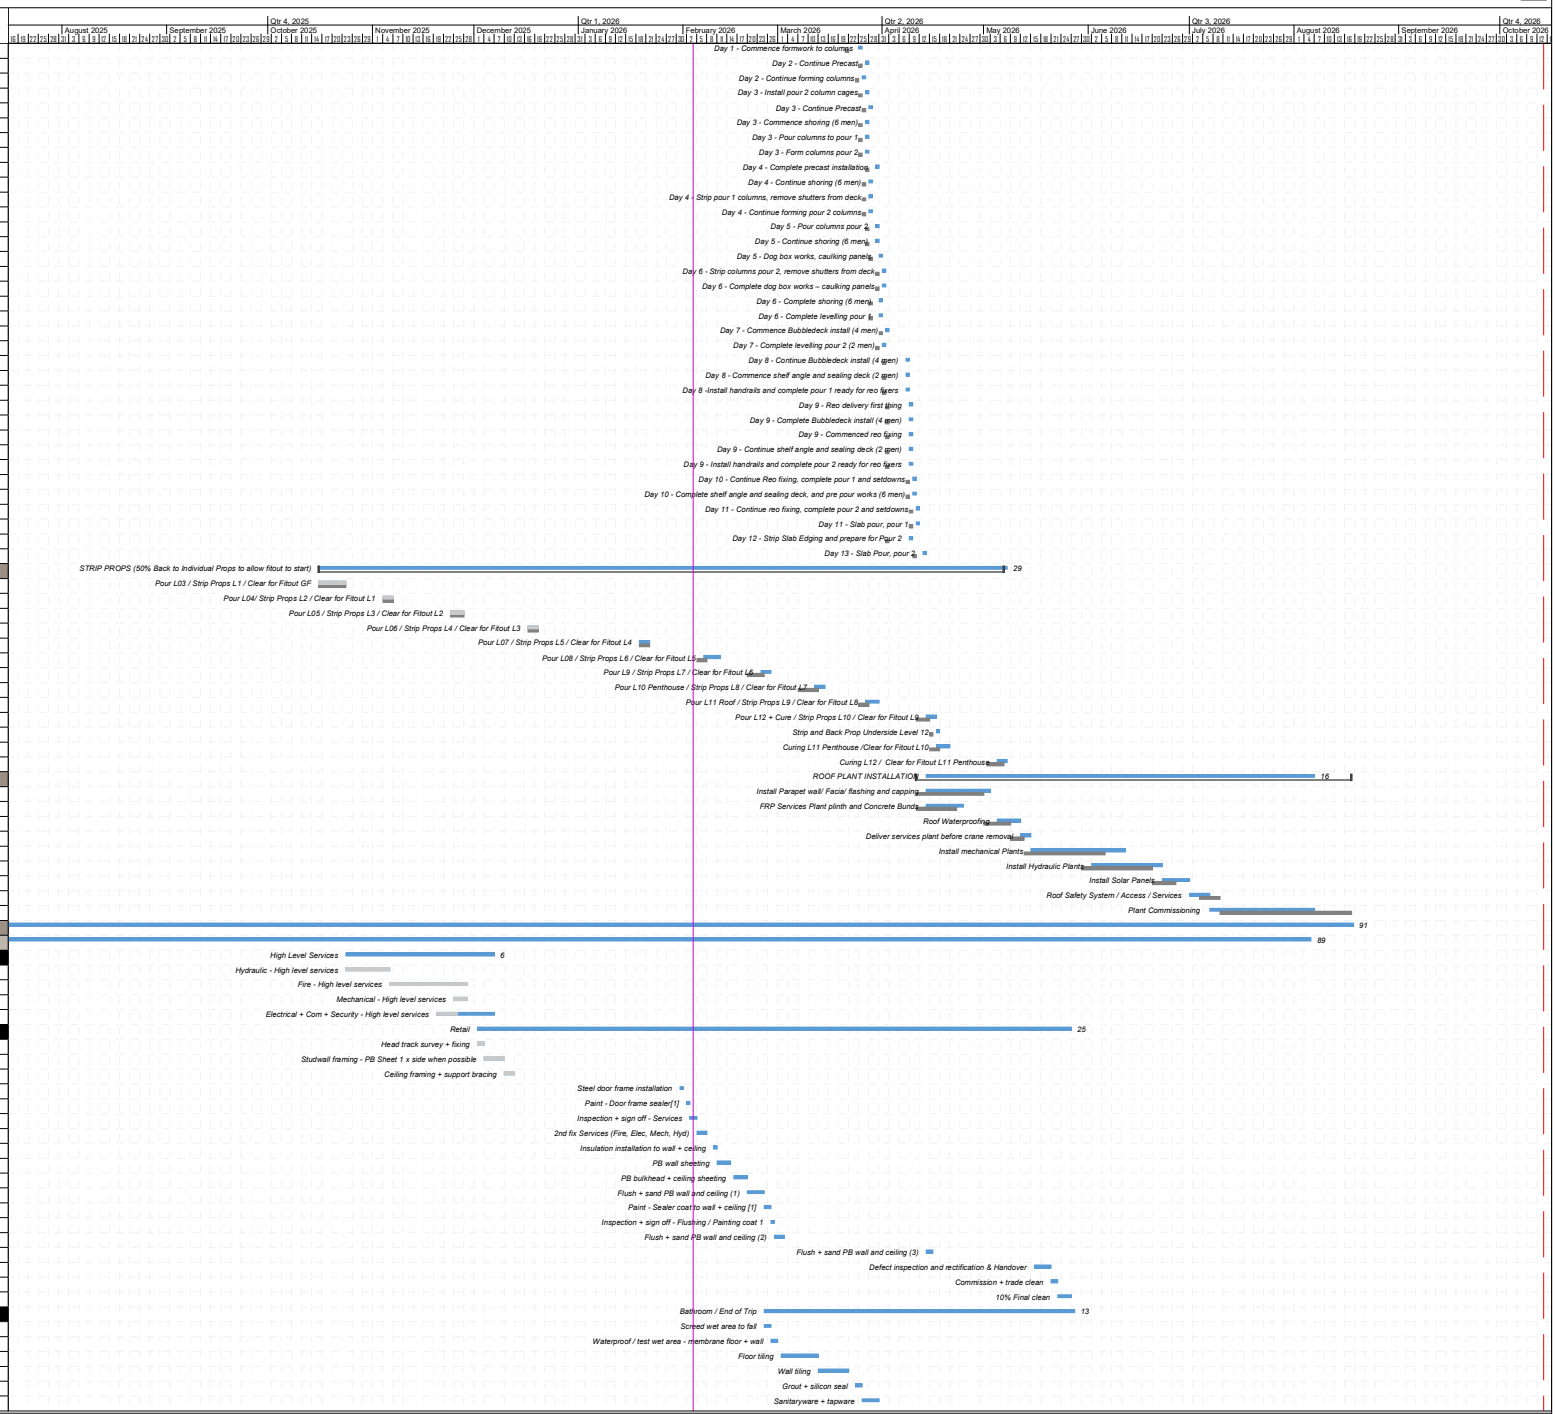

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Milestone | Summary | Critical | Critical Milestone | Client Tasks | Client Milestones | Baseline | Baseline Milestone | Baseline Summary | Progress | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
1591	Shower screen + doors	0%	2 days	Tue 31/03/26	Wed 1/04/26
1592	Sundry fixtures + fittings	0%	2 days	Sat 11/04/26	Mon 13/04/26
1593	70% Builders Clean	0%	1 day	Wed 27/05/26	Wed 27/05/26
1594	**Carpark**	**25%**	**439 days**	**Tue 19/11/24**	**Wed 5/08/26**
1595	Strip carpark props from pour 1	100%	2 days	Wed 5/11/25	Thu 6/11/25
1596	Strip carpark props from pour 2	100%	2 days	Fri 7/11/25	Sat 8/11/25
1597	Carpark 1st fix fire services high level	100%	4 days	Mon 10/11/25	Thu 13/11/25
1598	Carpark 1st fix mechanical services	100%	4 days	Thu 13/11/25	Tue 18/11/25
1599	Carpark 1st fix electrical services	100%	4 days	Tue 18/11/25	Fri 21/11/25
1600	Carpark 1st fix hydraulic services	100%	4 days	Fri 21/11/25	Tue 25/11/25
1601	Complete all carpark external cladding	100%	6 days	Tue 19/11/24	Mon 25/11/24
1602	Recycle props to upper levels	100%	1 day	Mon 10/11/25	Mon 10/11/25
1603	Area Used as lay down area	15%	165 days	Wed 26/11/25	Thu 23/07/26
1604	Services 2nd Fix	0%	**3 days**	Fri 24/07/26	Tue 28/07/26
1605	Line Marking	0%	1 day	Wed 29/07/26	Wed 29/07/26
1606	Car Park FF&E	0%	1 day	Thu 30/07/26	Thu 30/07/26
1607	Inspection + sign off	0%	1 day	Fri 31/07/26	Fri 31/07/26
1608	Commission + trade clean	0%	2 days	Sat 1/08/26	Mon 3/08/26
1609	10% Final clean	0%	2 days	Tue 4/08/26	Wed 5/08/26
1610	**Façade**	**2%**	**378 days**	**Tue 19/11/24**	**Tue 19/05/26**
1611	Studwork - External Wall / Soffit Framing / Sarking	29%	7 days	Tue 2/12/25	Tue 9/12/25
1612	Install subsill, subhead + sub jamb	0%	7 days	Tue 19/11/24	Tue 26/11/24
1613	Install Windows / Door Frames / Flashings	0%	5 days	Wed 27/11/24	Thu 5/12/24
1614	Cladding / Sheeting ~ @ 100m2/d inc site measure	0%	20 days	Wed 27/11/24	Mon 6/01/25
1615	Area Mostly Waterproof	0%	0 days	Thu 9/01/25	Thu 9/01/25
1616	External Paint ~ @ 100m2/d	0%	9 days	Tue 7/01/25	Thu 16/01/25
1617	Install Doors / Door Furniture ~ @ 20/d	0%	9 days	Fri 10/01/25	Mon 20/01/25
1618	Install Balustrades / Metalwork ~ @ 20/d	0%	9 days	Fri 17/04/26	Wed 29/04/26
1619	WP & Tile Beds	0%	9 days	Tue 21/04/26	Sat 2/05/26
1620	Sunshade Channels / Framing	0%	9 days	Tue 5/05/26	Thu 14/05/26
1621	Sunshades & Louvres	0%	9 days	Wed 6/05/26	Fri 15/05/26
1622	Defect Inspections & Rectification	0%	6 days	Tue 12/05/26	Tue 19/05/26
1623	GF Façade complete	0%	0 days	Tue 19/05/26	Tue 19/05/26
1624	**FITOUT LEVEL 1- CARPARK**	**25%**	**439 days**	**Tue 19/11/24**	**Wed 5/08/26**
1625	**High Level Services**	**100%**	**45 days**	**Mon 13/10/25**	**Fri 12/12/25**
1626	Hydraulic - High level services	100%	7 days	Thu 6/11/25	Thu 13/11/25
1627	Fire - High level services	100%	6 days	Mon 13/10/25	Sat 18/10/25
1628	Mechanical - High level services	100%	13 days	Thu 20/11/25	Sat 6/12/25
1629	Electrical + Com + Security - High level services	100%	5 days	Mon 8/12/25	Fri 12/12/25
1630	**Prototype Room**	**25%**	**165 days**	**Fri 24/10/25**	**Mon 22/06/26**
1631	**High level services**	**78%**	**56 days**	**Fri 24/10/25**	**Fri 23/01/26**
1632	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Fri 24/10/25	Sat 25/10/25
1633	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Mon 27/10/25	Wed 29/10/25
1634	Set out all grid lines ready for plasterboard linings	100%	1 day	Thu 30/10/25	Thu 30/10/25
1635	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Wed 10/12/25	Wed 17/12/25
1636	Prototype 1st fix fire services high level	100%	4 days	Sat 13/12/25	Wed 17/12/25
1637	Prototype 1st fix Hydraulic services high level	100%	4 days	Tue 16/12/25	Fri 19/12/25
1638	Prototype 1st fix mechanical services high level	58%	12 days	Thu 18/12/25	Wed 21/01/26
1639	Prototype 1st fix electrical services high level	25%	4 days	Fri 19/12/25	Fri 23/01/26
1640	**General Area**	**0%**	**111 days**	**Thu 22/01/26**	**Mon 22/06/26**
1641	Prototype 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 22/01/26	Fri 23/01/26
1642	1st Fix Hydraulic in-wall	0%	5 days	Wed 28/01/26	Mon 2/02/26
1643	Prototype 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 3/02/26	Wed 4/02/26
1644	Complete all services ITP's - high level & In-wall	0%	2 days	Thu 5/02/26	Fri 6/02/26
1645	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight external	0%	2 days	Sat 7/02/26	Tue 10/02/26
1646	All relevant ITP's for window/ door install	0%	1 day	Wed 11/02/26	Wed 11/02/26
1647	Complete all services ITP's wall framing	0%	1 day	Thu 12/02/26	Thu 12/02/26
1648	Install all internal steel door frames	0%	2 days	Fri 13/02/26	Sat 14/02/26
1649	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Fri 13/02/26	Thu 19/02/26
1650	Complete all ceiling framing	0%	3 days	Fri 20/02/26	Tue 24/02/26
1651	Complete all ceiling grid ITP's	0%	1 day	Wed 25/02/26	Wed 25/02/26
1652	Complete all ceiling sheeting + flushing	0%	4 days	Thu 26/02/26	Mon 2/03/26
1653	All 2nd fix fire services cut outs	0%	1 day	Tue 3/03/26	Tue 3/03/26
1654	All 2nd fix mechanical services cut outs	0%	1 day	Tue 3/03/26	Tue 3/03/26
1655	All 2nd fix electrical services cut outs	0%	1 day	Tue 3/03/26	Tue 3/03/26
1656	All 2nd fix hydraulic services cut outs	0%	1 day	Tue 3/03/26	Tue 3/03/26
1657	Delivery of all internal timber doors	0%	1 day	Wed 4/03/26	Wed 4/03/26
1658	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Thu 5/03/26	Sat 7/03/26
1659	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Thu 5/03/26	Wed 11/03/26
1660	Complete all floor coverings - Timber	0%	3 days	Thu 12/03/26	Sat 14/03/26
1661	Complete all floor coverings - Carpet	0%	2 days	Mon 16/03/26	Tue 17/03/26
1662	Complete and install all timber skirtings over floor coverings	0%	2 days	Wed 18/03/26	Thu 19/03/26
1663	Prototype 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General inwa	0%	3 days	Fri 20/03/26	Tue 24/03/26
1664	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Wed 25/03/26	Thu 26/03/26
1665	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 8/05/26	Sat 9/05/26
1666	Complete all 2nd fix fit offs - mechanical	0%	2 days	Fri 8/05/26	Sat 9/05/26
1667	Complete all 2nd fix fit offs - plumbing	0%	3 days	Fri 8/05/26	Mon 11/05/26
1668	Complete all final top coat painting	0%	3 days	Fri 19/06/26	Mon 22/06/26
1669	**Bathroom**	**0%**	**13 days**	**Wed 11/03/26**	**Thu 26/03/26**
1670	Primer & First Coat of Waterproofing	0%	3 days	Wed 11/03/26	Fri 13/03/26
1671	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Fri 13/03/26	Tue 17/03/26
1672	Wet area floor and wall tiling	0%	6 days	Wed 18/03/26	Wed 25/03/26
1673	Measure all wet area shower screens (book install)	0%	1 day	Thu 26/03/26	Thu 26/03/26
1674	**Zone A (Northern Half)**	**28%**	**173 days**	**Fri 24/10/25**	**Thu 2/07/26**
1675	**Apartments**	**33%**	**168 days**	**Fri 24/10/25**	**Thu 25/06/26**
1676	**High level services**	**100%**	**40 days**	**Fri 24/10/25**	**Mon 15/12/25**
1677	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Fri 24/10/25	Sat 25/10/25
1678	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Fri 28/11/25	Wed 3/12/25
1679	Set out all grid lines ready for plasterboard linings	100%	1 day	Fri 28/11/25	Fri 28/11/25
1680	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Wed 3/12/25	Wed 10/12/25
1681	Apartment 1st fix fire services high level	100%	4 days	Thu 4/12/25	Mon 8/12/25
1682	Apartment 1st fix Hydraulic services high level	100%	4 days	Sat 6/12/25	Wed 10/12/25

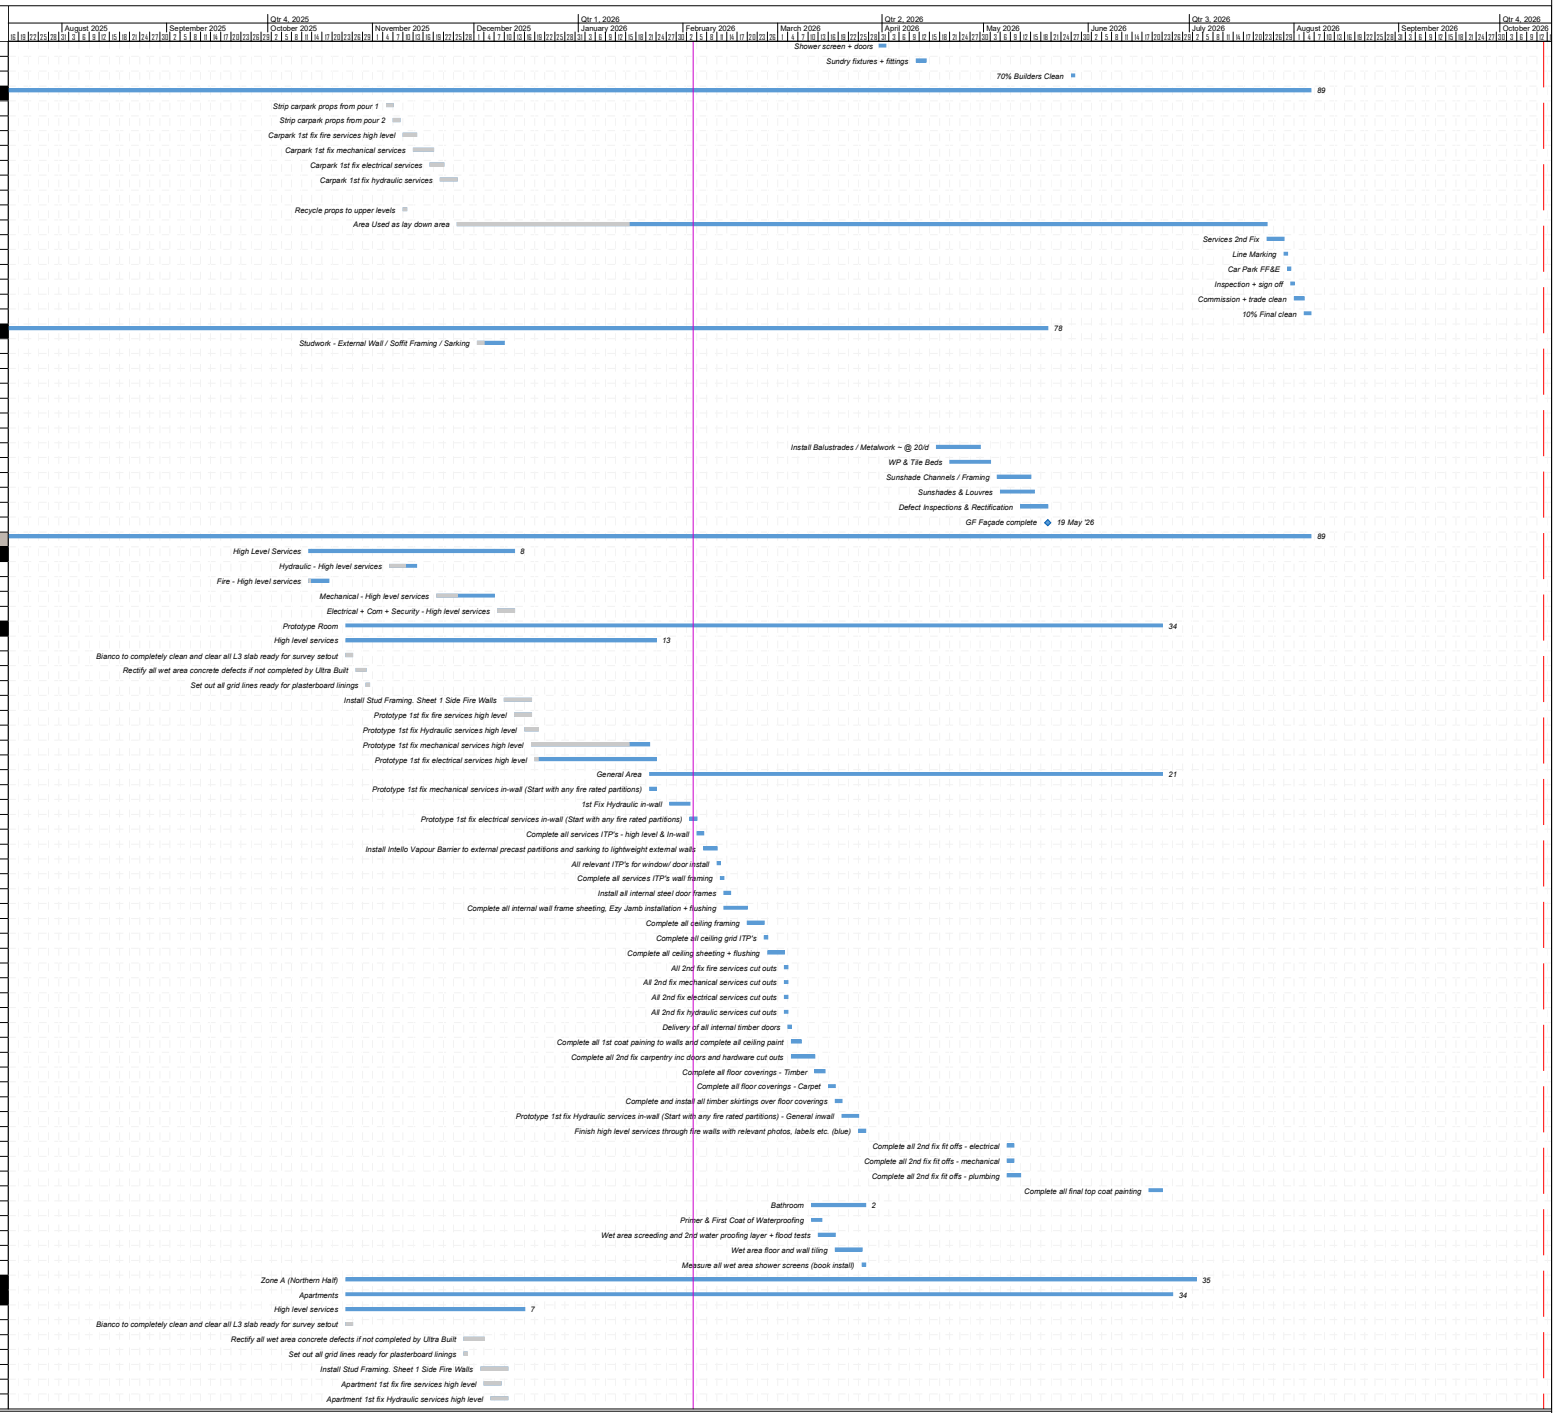

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1683	Apartment 1st fix mechanical services high level	100%	4 days	Tue 9/12/25	Fri 12/12/25
1684	Apartment 1st fix electrical services high level	100%	4 days	Thu 11/12/25	Mon 15/12/25
1685	**General Area**	**16%**	**130 days**	**Sat 13/12/25**	**Thu 25/06/26**
1686	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	100%	2 days	Sat 13/12/25	Mon 15/12/25
1687	1st Fix Hydraulic in-wall	64%	14 days	Tue 16/12/25	Wed 21/01/26
1688	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 22/01/26	Fri 23/01/26
1689	Complete all services ITP's - high level & In-wall	0%	2 days	Wed 28/01/26	Thu 29/01/26
1690	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	100%	2 days	Wed 14/01/26	Thu 15/01/26
1691	All relevant ITP's for window/ door install	0%	1 day	Fri 30/01/26	Fri 30/01/26
1692	Complete all services ITP's wall framing	0%	1 day	Sat 31/01/26	Sat 31/01/26
1693	Install all internal steel door frames	0%	2 days	Mon 2/02/26	Tue 3/02/26
1694	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Mon 2/02/26	Sat 7/02/26
1695	Complete all ceiling framing	0%	3 days	Tue 10/02/26	Thu 12/02/26
1696	Complete all ceiling grid ITP's	0%	1 day	Fri 13/02/26	Fri 13/02/26
1697	Complete all ceiling sheeting + flushing	0%	4 days	Sat 14/02/26	Wed 18/02/26
1698	All 2nd fix fire services cut outs	0%	1 day	Thu 19/02/26	Thu 19/02/26
1699	All 2nd fix mechanical services cut outs	0%	1 day	Thu 19/02/26	Thu 19/02/26
1700	All 2nd fix electrical services cut outs	0%	1 day	Thu 19/02/26	Thu 19/02/26
1701	All 2nd fix hydraulic services cut outs	0%	1 day	Thu 19/02/26	Thu 19/02/26
1702	Measure all bedroom robes (book install)	0%	1 day	Fri 20/02/26	Fri 20/02/26
1703	Delivery of all internal timber doors	0%	1 day	Fri 20/02/26	Fri 20/02/26
1704	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Sat 21/02/26	Wed 25/02/26
1705	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Sat 21/02/26	Thu 26/02/26
1706	Joinery Site Mobilisation and Install	0%	3 days	Tue 24/02/26	Thu 26/02/26
1707	Measure and book install for all stone tops	0%	1 day	Fri 27/02/26	Fri 27/02/26
1708	Measure and install all glass splash backs	0%	1 day	Sat 28/02/26	Sat 28/02/26
1709	Complete all floor coverings - Timber	0%	3 days	Mon 2/03/26	Wed 4/03/26
1710	Complete all floor coverings - Carpet	0%	2 days	Thu 5/03/26	Fri 6/03/26
1711	Complete and install all timber skirtings over floor coverings	0%	2 days	Sat 7/03/26	Wed 11/03/26
1712	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Thu 12/03/26	Sat 14/03/26
1713	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Mon 16/03/26	Tue 17/03/26
1714	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 18/03/26	Thu 19/03/26
1715	Complete all 2nd fix fit offs - mechanical	0%	2 days	Mon 11/05/26	Tue 12/05/26
1716	Complete all 2nd fix fit offs - plumbing	0%	3 days	Mon 11/05/26	Wed 13/05/26
1717	Complete all final top coat painting	0%	3 days	Tue 23/06/26	Thu 25/06/26
1718	**Bathroom**	**0%**	**23 days**	**Thu 26/02/26**	**Fri 27/03/26**
1719	Primer & First Coat of Waterproofing	0%	3 days	Thu 26/02/26	Sat 28/02/26
1720	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Sat 28/02/26	Wed 4/03/26
1721	Wet area floor and wall tiling	0%	6 days	Thu 5/03/26	Fri 13/03/26
1722	Measure all wet area shower screens (book install)	0%	1 day	Fri 27/03/26	Fri 27/03/26
1723	**Balcony & Façade**	**27%**	**70 days**	**Tue 28/10/25**	**Tue 17/02/26**
1724	External Stud Framing	100%	3 days	Tue 28/10/25	Thu 30/10/25
1725	Waterproofing to all external balconies before window subs are installed	100%	2 days	Sat 20/12/25	Mon 12/01/26
1726	Installation of sarking to balcony walls, returning into the jamb	100%	1 day	Tue 13/01/26	Tue 13/01/26
1727	Delivery and installation of all aluminium sub framing	100%	2 days	Wed 14/01/26	Thu 15/01/26
1728	Caulking to all external windows/ doors	0%	3 days	Mon 19/01/26	Wed 21/01/26
1729	Deliver and install of aluminium window panels	0%	1 day	Thu 22/01/26	Thu 22/01/26
1730	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 23/01/26	Mon 2/02/26
1731	Complete all external balcony balustrading	0%	4 days	Tue 3/02/26	Fri 6/02/26
1732	Complete all balcony water proofing	0%	3 days	Sat 7/02/26	Wed 11/02/26
1733	Complete all balcony tiling	0%	3 days	Thu 12/02/26	Sat 14/02/26
1734	Complete all external painting to the cladding	0%	2 days	Mon 16/02/26	Tue 17/02/26
1735	**Common Area**	**0%**	**57 days**	**Thu 12/03/26**	**Wed 27/05/26**
1736	Complete all 2nd fix fit offs - fire	0%	2 days	Thu 12/03/26	Fri 13/03/26
1737	Complete all 2nd fix fit offs - electrical	0%	2 days	Thu 12/03/26	Fri 13/03/26
1738	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 24/03/26	Wed 25/03/26
1739	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 12/05/26	Thu 14/05/26
1740	Complete all final top coat painting	0%	3 days	Fri 15/05/26	Tue 19/05/26
1741	Complete all floor coverings - Timber	0%	3 days	Wed 20/05/26	Fri 22/05/26
1742	Complete all floor coverings - Carpet	0%	2 days	Sat 23/05/26	Mon 25/05/26
1743	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 26/05/26	Wed 27/05/26
1744	**Inspection Activities**	**0%**	**5 days**	**Fri 26/06/26**	**Thu 2/07/26**
1745	Defect Inspection & Rectification	0%	4 days	Fri 26/06/26	Wed 1/07/26
1746	Testing and commissioning	0%	1 day	Thu 2/07/26	Thu 2/07/26
1747	**Zone B (Southern Half)**	**25%**	**171 days**	**Thu 30/10/25**	**Mon 6/07/26**
1748	**Apartments**	**29%**	**166 days**	**Thu 30/10/25**	**Tue 30/06/26**
1749	**High level services**	**100%**	**39 days**	**Thu 30/10/25**	**Fri 19/12/25**
1750	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Thu 30/10/25	Fri 31/10/25
1751	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Sat 1/11/25	Thu 6/11/25
1752	Set out all grid lines ready for plasterboard linings	100%	1 day	Sat 1/11/25	Sat 1/11/25
1753	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Thu 6/11/25	Thu 13/11/25
1754	Apartment 1st fix fire services high level	100%	4 days	Tue 9/12/25	Fri 12/12/25
1755	Apartment 1st fix Hydraulic services high level	100%	4 days	Thu 11/12/25	Mon 15/12/25
1756	Apartment 1st fix mechanical services high level	100%	4 days	Sat 13/12/25	Wed 17/12/25
1757	Apartment 1st fix electrical services high level	100%	4 days	Tue 16/12/25	Fri 19/12/25
1758	**General Area**	**10%**	**129 days**	**Thu 18/12/25**	**Tue 30/06/26**
1759	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	100%	2 days	Thu 18/12/25	Fri 19/12/25
1760	1st Fix Hydraulic in-wall	55%	11 days	Fri 19/12/25	Wed 21/01/26
1761	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 22/01/26	Fri 23/01/26
1762	Complete all services ITP's - high level & In-wall	0%	2 days	Wed 28/01/26	Thu 29/01/26
1763	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	0%	2 days	Fri 30/01/26	Sat 31/01/26
1764	All relevant ITP's for window/ door install	0%	1 day	Mon 2/02/26	Mon 2/02/26
1765	Complete all services ITP's wall framing	0%	1 day	Tue 3/02/26	Tue 3/02/26
1766	Install all internal steel door frames	0%	2 days	Wed 4/02/26	Thu 5/02/26
1767	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Wed 4/02/26	Wed 11/02/26
1768	Complete all ceiling framing	0%	3 days	Thu 12/02/26	Sat 14/02/26
1769	Complete all ceiling grid ITP's	0%	1 day	Mon 16/02/26	Mon 16/02/26
1770	Complete all ceiling sheeting + flushing	0%	4 days	Tue 17/02/26	Fri 20/02/26
1771	All 2nd fix fire services cut outs	0%	1 day	Sat 21/02/26	Sat 21/02/26
1772	All 2nd fix mechanical services cut outs	0%	1 day	Sat 21/02/26	Sat 21/02/26
1773	All 2nd fix electrical services cut outs	0%	1 day	Sat 21/02/26	Sat 21/02/26
1774	All 2nd fix hydraulic services cut outs	0%	1 day	Sat 21/02/26	Sat 21/02/26

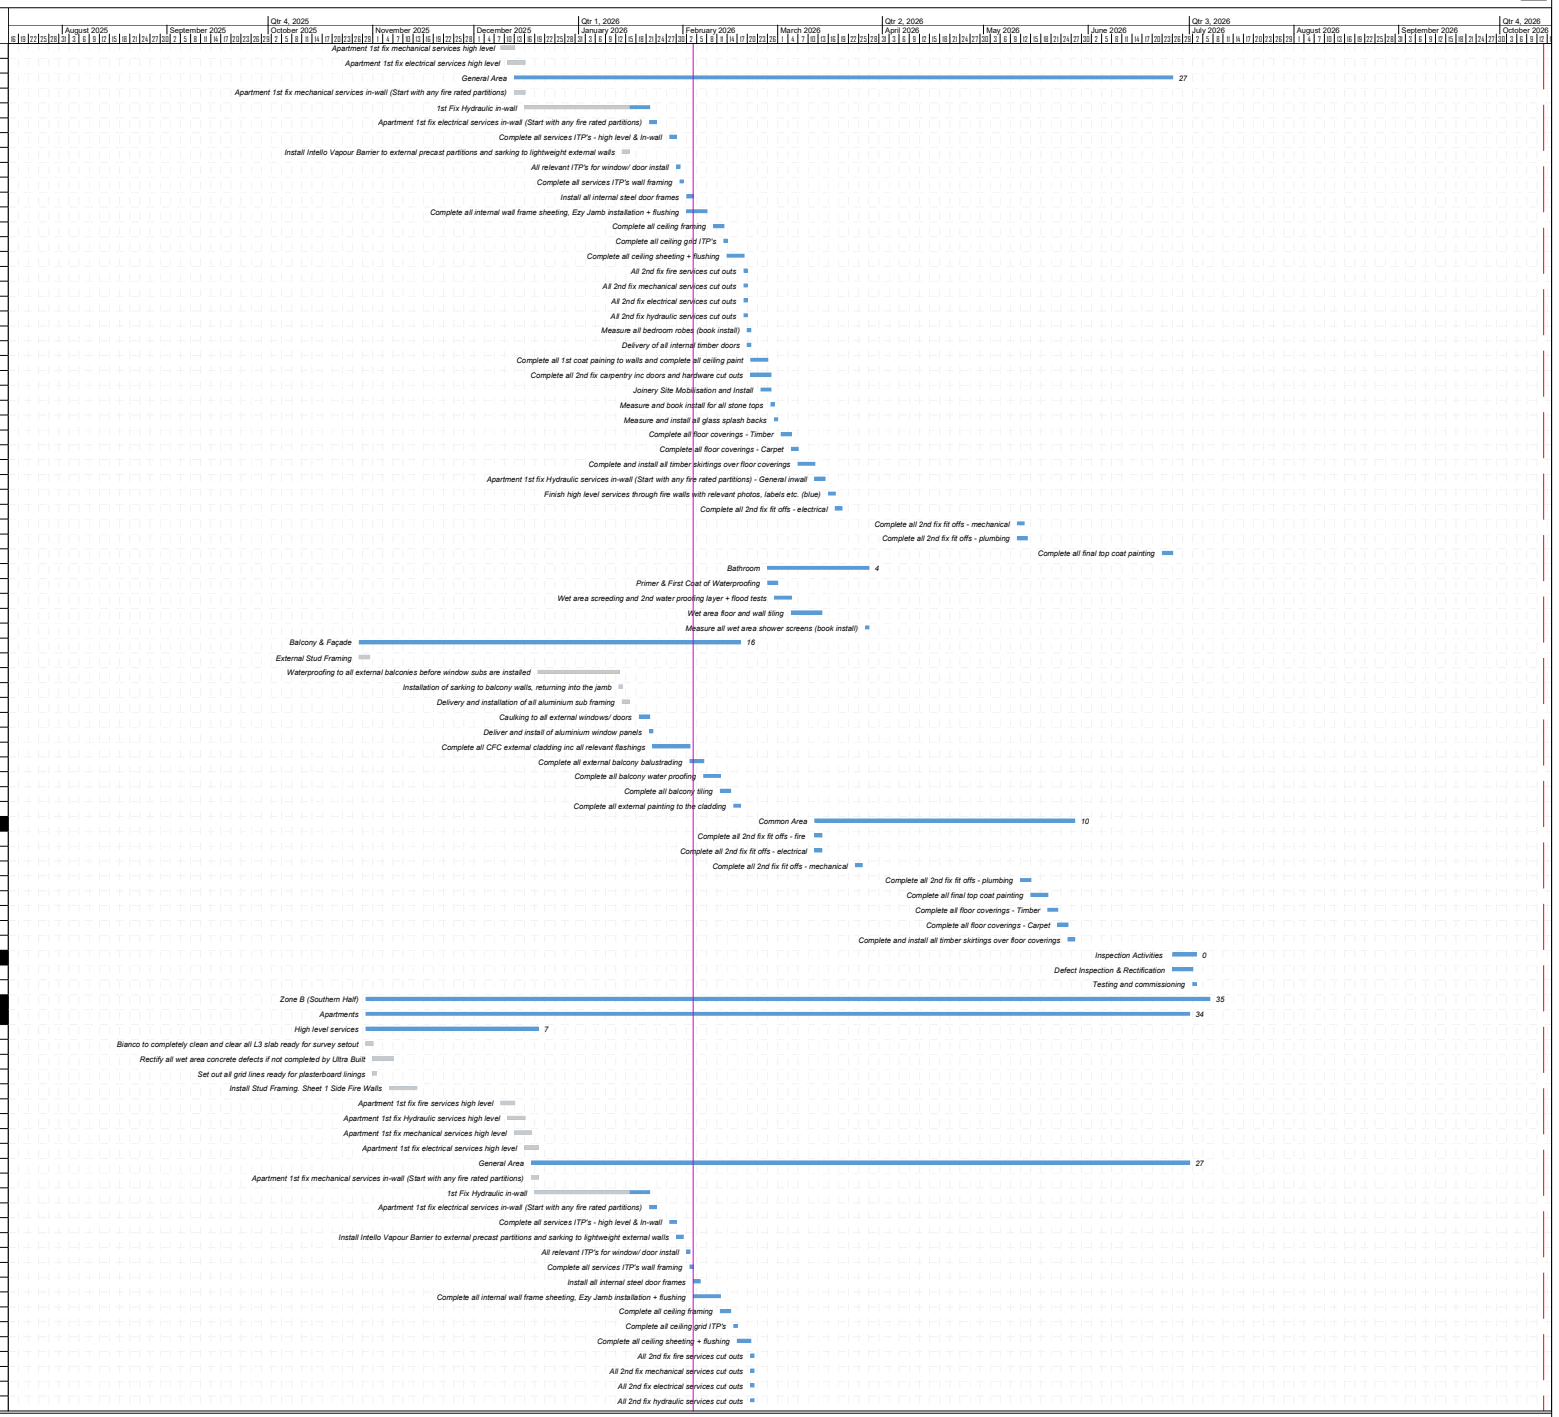

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1775	Measure all bedroom robes (book install)	0%	1 day	Tue 24/02/26	Tue 24/02/26
1776	Delivery of all internal timber doors	0%	1 day	Tue 24/02/26	Tue 24/02/26
1777	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Wed 25/02/26	Fri 27/02/26
1778	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Wed 25/02/26	Sat 28/02/26
1779	Joinery Site Mobilisation and Install	0%	3 days	Thu 26/02/26	Sat 28/02/26
1780	Measure and book install for all stone tops	0%	1 day	Mon 2/03/26	Mon 2/03/26
1781	Measure and install all glass splash backs	0%	1 day	Tue 3/03/26	Tue 3/03/26
1782	Complete all floor coverings - Timber	0%	3 days	Wed 4/03/26	Fri 6/03/26
1783	Complete all floor coverings - Carpet	0%	2 days	Sat 7/03/26	Wed 11/03/26
1784	Complete and install all timber skirtings over floor coverings	0%	2 days	Thu 12/03/26	Fri 13/03/26
1785	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Sat 14/03/26	Tue 17/03/26
1786	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Wed 18/03/26	Thu 19/03/26
1787	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 20/03/26	Sat 21/03/26
1788	Complete all 2nd fix fit offs - mechanical	0%	2 days	Fri 20/03/26	Sat 21/03/26
1789	Complete all 2nd fix fit offs - plumbing	0%	3 days	Thu 14/05/26	Sat 16/05/26
1790	Complete all final top coat painting	0%	3 days	Fri 26/06/26	Tue 30/06/26
1791	**Bathroom**	**0%**	**22 days**	**Sat 28/02/26**	**Sat 28/03/26**
1792	Primer & First Coat of Waterproofing	0%	3 days	Sat 28/02/26	Tue 3/03/26
1793	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Tue 3/03/26	Fri 6/03/26
1794	Wet area floor and wall tiling	0%	6 days	Sat 7/03/26	Mon 16/03/26
1795	Measure all wet area shower screens (book install)	0%	1 day	Sat 28/03/26	Sat 28/03/26
1796	**Balcony & Façade**	**19%**	**31 days**	**Sat 20/12/25**	**Thu 19/02/26**
1797	Waterproofing to all external balconies before window subs are installed	100%	2 days	Sat 20/12/25	Mon 12/01/26
1798	Installation of sarking to balcony walls, returning into the jamb	100%	1 day	Tue 13/01/26	Tue 13/01/26
1799	Delivery and installation of all aluminium sub framing	100%	2 days	Wed 14/01/26	Thu 15/01/26
1800	Caulking to all external windows/ doors	0%	3 days	Fri 16/01/26	Mon 19/01/26
1801	Deliver and install of aluminium window panels	0%	1 day	Fri 23/01/26	Fri 23/01/26
1802	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Wed 28/01/26	Tue 3/02/26
1803	Complete all external balcony balustrading	0%	4 days	Wed 4/02/26	Sat 7/02/26
1804	Complete all balcony water proofing	0%	3 days	Tue 10/02/26	Thu 12/02/26
1805	Complete all balcony tiling	0%	3 days	Fri 13/02/26	Mon 16/02/26
1806	Complete all external painting to the cladding	0%	2 days	Wed 18/02/26	Thu 19/02/26
1807	**Common Area**	**0%**	**58 days**	**Sat 14/03/26**	**Sat 30/05/26**
1808	Complete all 2nd fix fit offs - fire	0%	2 days	Sat 14/03/26	Mon 16/03/26
1809	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 14/03/26	Mon 16/03/26
1810	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 24/03/26	Wed 25/03/26
1811	Complete all 2nd fix fit offs - plumbing	0%	3 days	Fri 15/05/26	Tue 19/05/26
1812	Complete all final top coat painting	0%	3 days	Wed 20/05/26	Fri 22/05/26
1813	Complete all floor coverings - Timber	0%	3 days	Sat 23/05/26	Tue 26/05/26
1814	Complete all floor coverings - Carpet	0%	2 days	Wed 27/05/26	Thu 28/05/26
1815	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 29/05/26	Sat 30/05/26
1816	**Inspection Activities**	**0%**	**5 days**	**Wed 1/07/26**	**Mon 6/07/26**
1817	Defect Inspection & Rectification	0%	4 days	Wed 1/07/26	Sat 4/07/26
1818	Testing and commissioning to all L3	0%	1 day	Mon 6/07/26	Mon 6/07/26
1819	**Car Park**	**25%**	**439 days**	**Tue 19/11/24**	**Wed 5/08/26**
1820	Strip carpark props from pour 1	100%	2 days	Wed 5/11/25	Thu 6/11/25
1821	Strip carpark props from pour 2	100%	2 days	Fri 7/11/25	Sat 8/11/25
1822	Carpark 1st fix fire services high level	100%	4 days	Mon 10/11/25	Thu 13/11/25
1823	Carpark 1st fix mechanical services	100%	4 days	Thu 13/11/25	Tue 18/11/25
1824	Carpark 1st fix electrical services	100%	4 days	Tue 18/11/25	Fri 21/11/25
1825	Carpark 1st fix hydraulic services	100%	4 days	Fri 21/11/25	Tue 25/11/25
1826	Complete all carpark external cladding	100%	6 days	Tue 19/11/24	Mon 25/11/24
1827	Recycle props to upper levels	100%	1 day	Mon 10/11/25	Mon 10/11/25
1828	Area Used as lay down area	15%	165 days	Wed 26/11/25	Thu 23/07/26
1829	Services 2nd Fix	0%	3 days	Fri 24/07/26	Tue 28/07/26
1830	Car Park FF&E	0%	1 day	Thu 30/07/26	Thu 30/07/26
1831	Line Marking	0%	1 day	Wed 29/07/26	Wed 29/07/26
1832	Inspection + sign off	0%	1 day	Fri 31/07/26	Fri 31/07/26
1833	Commission + trade clean	0%	2 days	Sat 1/08/26	Mon 3/08/26
1834	10% Final clean	0%	**2 days**	Tue 4/08/26	Wed 5/08/26
1835	**FITOUT LEVEL 2- CARPARK**	**23%**	**440 days**	**Tue 19/11/24**	**Thu 6/08/26**
1836	**High Level Services**	**76%**	**35 days**	**Thu 27/11/25**	**Mon 2/02/26**
1837	Hydraulic - High level services	100%	5 days	Thu 27/11/25	Thu 4/12/25
1838	Fire - High level services	72%	25 days	Fri 5/12/25	Fri 23/01/26
1839	Mechanical - High level services	0%	5 days	Wed 28/01/26	Mon 2/02/26
1840	Electrical + Com + Security - High level services	100%	**15 days**	Wed 17/12/25	Fri 23/01/26
1841	**Zone A (Northern Half)**	**20%**	**169 days**	**Fri 7/11/25**	**Thu 9/07/26**
1842	**Apartments**	**23%**	**164 days**	**Fri 7/11/25**	**Fri 3/07/26**
1843	**High level services**	**86%**	**50 days**	**Fri 7/11/25**	**Sat 31/01/26**
1844	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Fri 7/11/25	Sat 8/11/25
1845	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Fri 28/11/25	Wed 3/12/25
1846	Set out all grid lines ready for plasterboard linings	100%	1 day	Fri 28/11/25	Fri 28/11/25
1847	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Wed 3/12/25	Wed 10/12/25
1848	Apartment 1st fix fire services high level	100%	4 days	Thu 11/12/25	Mon 15/12/25
1849	Apartment 1st fix Hydraulic services high level	100%	4 days	Sat 13/12/25	Wed 17/12/25
1850	Apartment 1st fix mechanical services high level	100%	3 days	Wed 17/12/25	Fri 19/12/25
1851	Apartment 1st fix electrical services high level	0%	4 days	Wed 28/01/26	Sat 31/01/26
1852	**General Area**	**7%**	**130 days**	**Sat 20/12/25**	**Fri 3/07/26**
1853	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	100%	2 days	Sat 20/12/25	Mon 12/01/26
1854	1st Fix Hydraulic in-wall	43%	7 days	Tue 13/01/26	Tue 20/01/26
1855	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 21/01/26	Thu 22/01/26
1856	Complete all services ITP's - high level & In-wall	0%	2 days	Mon 2/02/26	Tue 3/02/26
1857	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	0%	2 days	Wed 4/02/26	Thu 5/02/26
1858	All relevant ITP's for window/ door install	0%	1 day	Fri 6/02/26	Fri 6/02/26
1859	Complete all services ITP's wall framing	0%	1 day	Sat 7/02/26	Sat 7/02/26
1860	Install all internal steel door frames	0%	2 days	Tue 10/02/26	Wed 11/02/26
1861	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Tue 10/02/26	Mon 16/02/26
1862	Complete all ceiling framing	0%	3 days	Tue 17/02/26	Thu 19/02/26
1863	Complete all ceiling grid ITP's	0%	1 day	Fri 20/02/26	Fri 20/02/26
1864	Complete all ceiling sheeting + flushing	0%	4 days	Sat 21/02/26	Thu 26/02/26
1865	All 2nd fix fire services cut outs	0%	1 day	Fri 27/02/26	Fri 27/02/26
1866	All 2nd fix mechanical services cut outs	0%	1 day	Fri 27/02/26	Fri 27/02/26

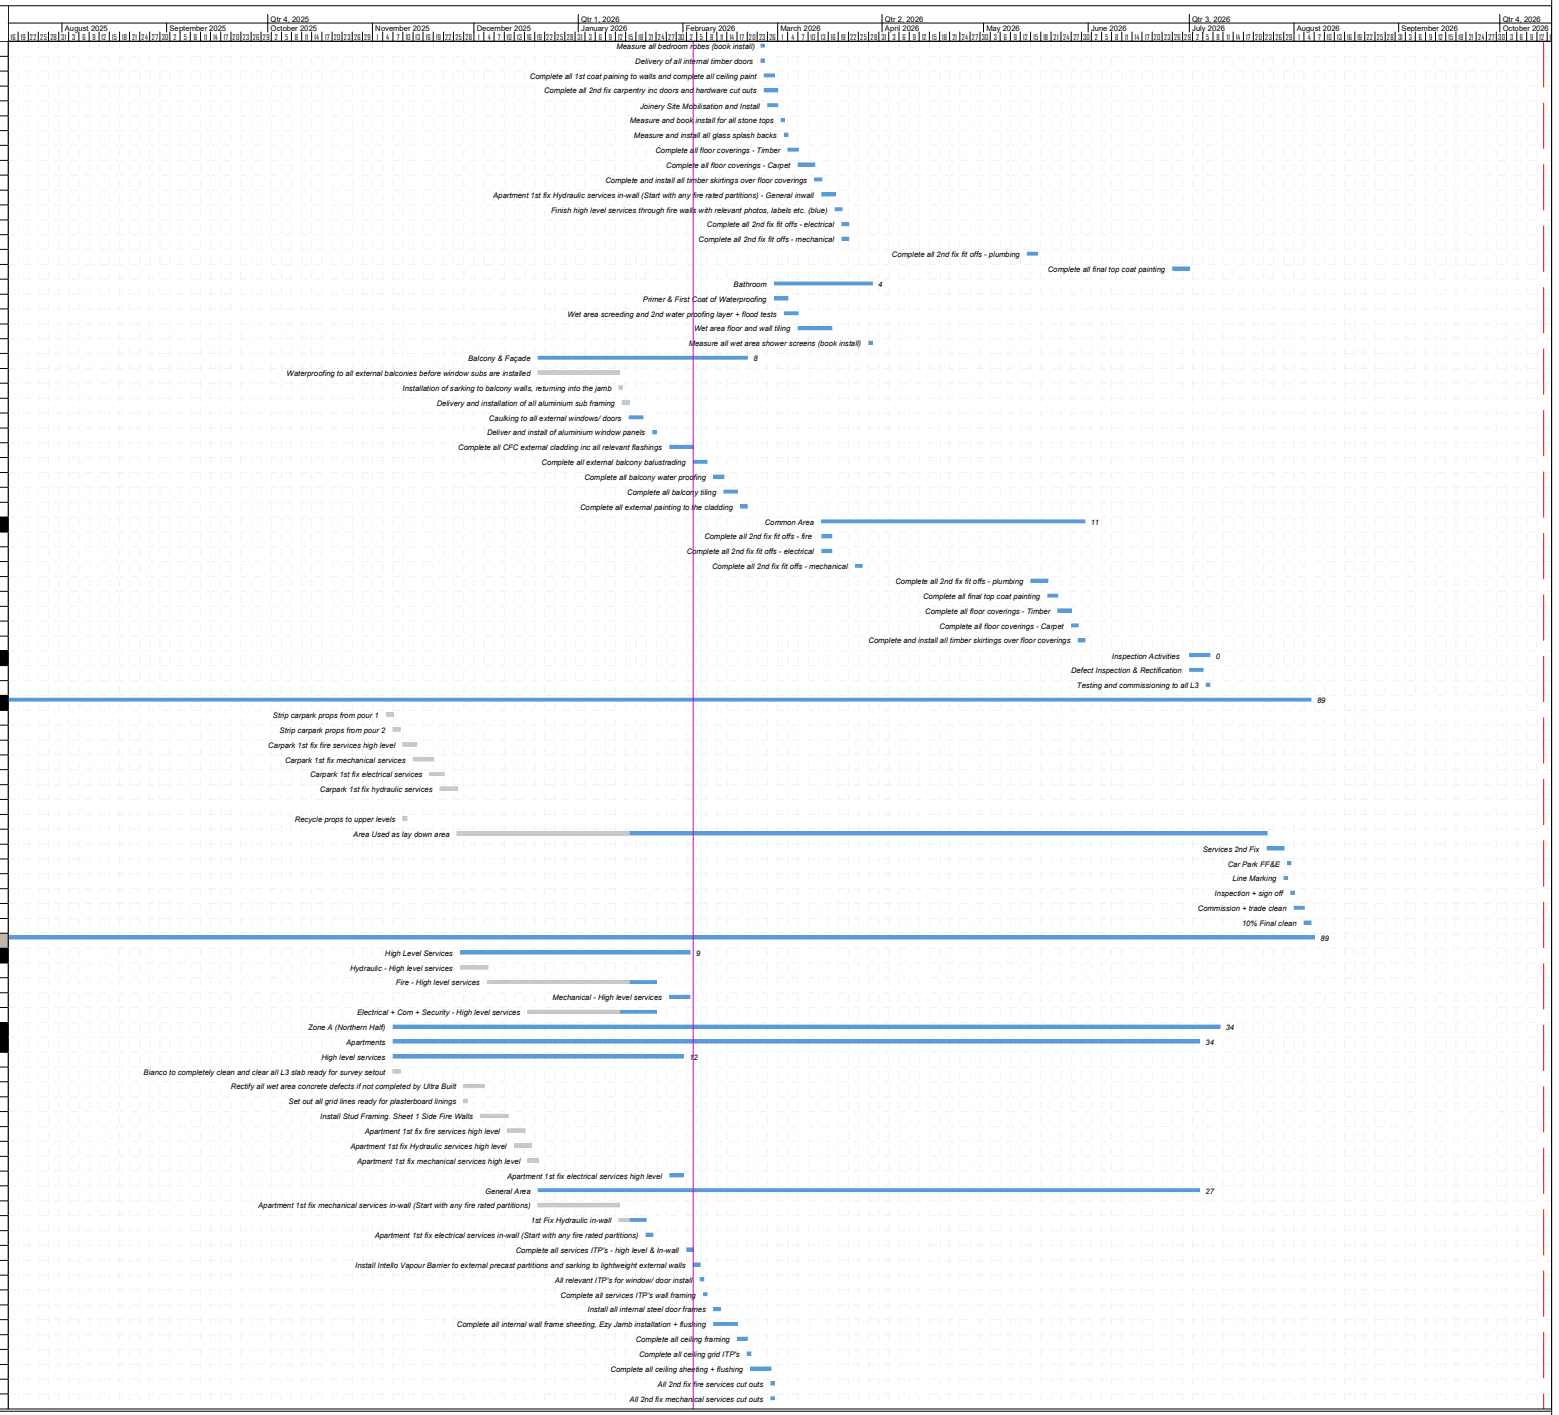

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Milestone | Summary | Critical | Critical Milestone | Client Tasks | Client Milestones | Baseline | Baseline Milestone | Baseline Summary | Progress | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
1867	All 2nd fix electrical services cut outs	0%	1 day	Fri 27/02/26	Fri 27/02/26
1868	All 2nd fix hydraulic services cut outs	0%	1 day	Fri 27/02/26	Fri 27/02/26
1869	Measure all bedroom robes (book install)	0%	1 day	Sat 28/02/26	Sat 28/02/26
1870	Delivery of all internal timber doors	0%	1 day	Sat 28/02/26	Sat 28/02/26
1871	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Mon 2/03/26	Wed 4/03/26
1872	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Mon 2/03/26	Thu 5/03/26
1873	Joinery Site Mobilisation and Install	0%	3 days	Tue 3/03/26	Thu 5/03/26
1874	Measure and book install for all stone tops	0%	1 day	Fri 6/03/26	Fri 6/03/26
1875	Measure and install all glass splash backs	0%	1 day	Sat 7/03/26	Sat 7/03/26
1876	Complete all floor coverings - Timber	0%	3 days	Wed 11/03/26	Fri 13/03/26
1877	Complete all floor coverings - Carpet	0%	2 days	Sat 14/03/26	Mon 16/03/26
1878	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 17/03/26	Wed 18/03/26
1879	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Thu 19/03/26	Sat 21/03/26
1880	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Tue 24/03/26	Wed 25/03/26
1881	Complete all 2nd fix fit offs - electrical	0%	2 days	Thu 26/03/26	Fri 27/03/26
1882	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 13/05/26	Thu 14/05/26
1883	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 13/05/26	Fri 15/05/26
1884	Complete all final top coat painting	0%	3 days	Wed 1/07/26	Fri 3/07/26
1885	**Bathroom**	**0%**	**19 days**	**Thu 5/03/26**	**Mon 30/03/26**
1886	Primer & First Coat of Waterproofing	0%	3 days	Thu 5/03/26	Sat 7/03/26
1887	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Sat 7/03/26	Fri 13/03/26
1888	Wet area floor and wall tiling	0%	6 days	Sat 14/03/26	Fri 20/03/26
1889	Measure all wet area shower screens (book install)	0%	1 day	Mon 30/03/26	Mon 30/03/26
1890	**Balcony & Façade**	**16%**	**33 days**	**Sat 20/12/25**	**Sat 21/02/26**
1891	Waterproofing to all external balconies before window subs are installed	56%	9 days	Sat 20/12/25	Tue 20/01/26
1892	Installation of sarking to balcony walls, returning into the jamb	0%	2 days	Wed 21/01/26	Thu 22/01/26
1893	Delivery and installation of all aluminium sub framing	0%	1 day	Fri 23/01/26	Fri 23/01/26
1894	Caulking to all external windows/ doors	0%	1 day	Wed 28/01/26	Wed 28/01/26
1895	Deliver and install of aluminium window panels	0%	1 day	Wed 28/01/26	Wed 28/01/26
1896	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Thu 29/01/26	Wed 4/02/26
1897	Complete all external balcony balustrading	0%	4 days	Thu 5/02/26	Tue 10/02/26
1898	Complete all balcony water proofing	0%	3 days	Wed 11/02/26	Fri 13/02/26
1899	Complete all balcony tiling	0%	3 days	Sat 14/02/26	Tue 17/02/26
1900	Complete all external painting to the cladding	0%	2 days	Fri 20/02/26	Sat 21/02/26
1901	**Common Area**	**0%**	**60 days**	**Thu 19/03/26**	**Wed 10/06/26**
1902	Complete all 2nd fix fit offs - fire	0%	2 days	Thu 19/03/26	Fri 20/03/26
1903	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 20/03/26	Sat 21/03/26
1904	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 19/05/26	Wed 20/05/26
1905	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 23/05/26	Tue 26/05/26
1906	Complete all final top coat painting	0%	3 days	Wed 27/05/26	Fri 29/05/26
1907	Complete all floor coverings - Timber	0%	3 days	Sat 30/05/26	Tue 2/06/26
1908	Complete all floor coverings - Carpet	0%	2 days	Wed 3/06/26	Thu 4/06/26
1909	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 5/06/26	Wed 10/06/26
1910	**Inspection Activities**	**0%**	**5 days**	**Sat 4/07/26**	**Thu 9/07/26**
1911	Defect Inspection & Rectification	0%	4 days	Sat 4/07/26	Wed 8/07/26
1912	Testing and commissioning to all L3	0%	1 day	Thu 9/07/26	Thu 9/07/26
1913	**Zone B (Southern Half)**	**18%**	**168 days**	**Thu 13/11/25**	**Wed 15/07/26**
1914	**Apartments**	**21%**	**162 days**	**Thu 13/11/25**	**Tue 7/07/26**
1915	**High level services**	**63%**	**49 days**	**Thu 13/11/25**	**Thu 5/02/26**
1916	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Thu 13/11/25	Fri 14/11/25
1917	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Sat 15/11/25	Wed 19/11/25
1918	Set out all grid lines ready for plasterboard linings	100%	1 day	Sat 15/11/25	Sat 15/11/25
1919	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Wed 19/11/25	Wed 26/11/25
1920	Apartment 1st fix fire services high level	60%	15 days	Tue 16/12/25	Thu 22/01/26
1921	Apartment 1st fix Hydraulic services high level	54%	13 days	Thu 18/12/25	Thu 22/01/26
1922	Apartment 1st fix mechanical services high level	0%	1 day	Thu 22/01/26	Thu 22/01/26
1923	Apartment 1st fix electrical services high level	0%	4 days	Mon 2/02/26	Thu 5/02/26
1924	**General Area**	**0%**	**122 days**	**Fri 23/01/26**	**Tue 7/07/26**
1925	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Fri 23/01/26	Wed 28/01/26
1926	1st Fix Hydraulic in-wall	0%	5 days	Thu 29/01/26	Tue 3/02/26
1927	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 4/02/26	Thu 5/02/26
1928	Complete all services ITP's - high level & In-wall	0%	2 days	Fri 6/02/26	Sat 7/02/26
1929	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	0%	2 days	Tue 10/02/26	Wed 11/02/26
1930	All relevant ITP's for window/ door install	0%	1 day	Thu 12/02/26	Thu 12/02/26
1931	Complete all services ITP's wall framing	0%	1 day	Fri 13/02/26	Fri 13/02/26
1932	Install all internal steel door frames	0%	2 days	Sat 14/02/26	Mon 16/02/26
1933	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Sat 14/02/26	Fri 20/02/26
1934	Complete all ceiling framing	0%	3 days	Sat 21/02/26	Wed 25/02/26
1935	Complete all ceiling grid ITP's	0%	1 day	Thu 26/02/26	Thu 26/02/26
1936	Complete all ceiling sheeting + flushing	0%	4 days	Fri 27/02/26	Tue 3/03/26
1937	All 2nd fix fire services cut outs	0%	1 day	Wed 4/03/26	Wed 4/03/26
1938	All 2nd fix mechanical services cut outs	0%	1 day	Wed 4/03/26	Wed 4/03/26
1939	All 2nd fix electrical services cut outs	0%	1 day	Wed 4/03/26	Wed 4/03/26
1940	All 2nd fix hydraulic services cut outs	0%	1 day	Wed 4/03/26	Wed 4/03/26
1941	Measure all bedroom robes (book install)	0%	1 day	Thu 5/03/26	Thu 5/03/26
1942	Delivery of all internal timber doors	0%	1 day	Thu 5/03/26	Thu 5/03/26
1943	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Fri 6/03/26	Wed 11/03/26
1944	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Fri 6/03/26	Thu 12/03/26
1945	Joinery Site Mobilisation and Install	0%	3 days	Sat 7/03/26	Thu 12/03/26
1946	Measure and book install for all stone tops	0%	1 day	Fri 13/03/26	Fri 13/03/26
1947	Measure and install all glass splash backs	0%	1 day	Sat 14/03/26	Sat 14/03/26
1948	Complete all floor coverings - Timber	0%	3 days	Mon 16/03/26	Wed 18/03/26
1949	Complete all floor coverings - Carpet	0%	2 days	Thu 19/03/26	Fri 20/03/26
1950	Complete and install all timber skirtings over floor coverings	0%	2 days	Sat 21/03/26	Tue 24/03/26
1951	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Wed 25/03/26	Fri 27/03/26
1952	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Sat 28/03/26	Mon 30/03/26
1953	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 31/03/26	Wed 1/04/26
1954	Complete all 2nd fix fit offs - mechanical	0%	2 days	Fri 15/05/26	Sat 16/05/26
1955	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 20/05/26	Fri 22/05/26
1956	Complete all final top coat painting	0%	3 days	Sat 4/07/26	Tue 7/07/26
1957	**Bathroom**	**0%**	**16 days**	**Thu 12/03/26**	**Tue 31/03/26**
1958	Primer & First Coat of Waterproofing	0%	3 days	Thu 12/03/26	Sat 14/03/26

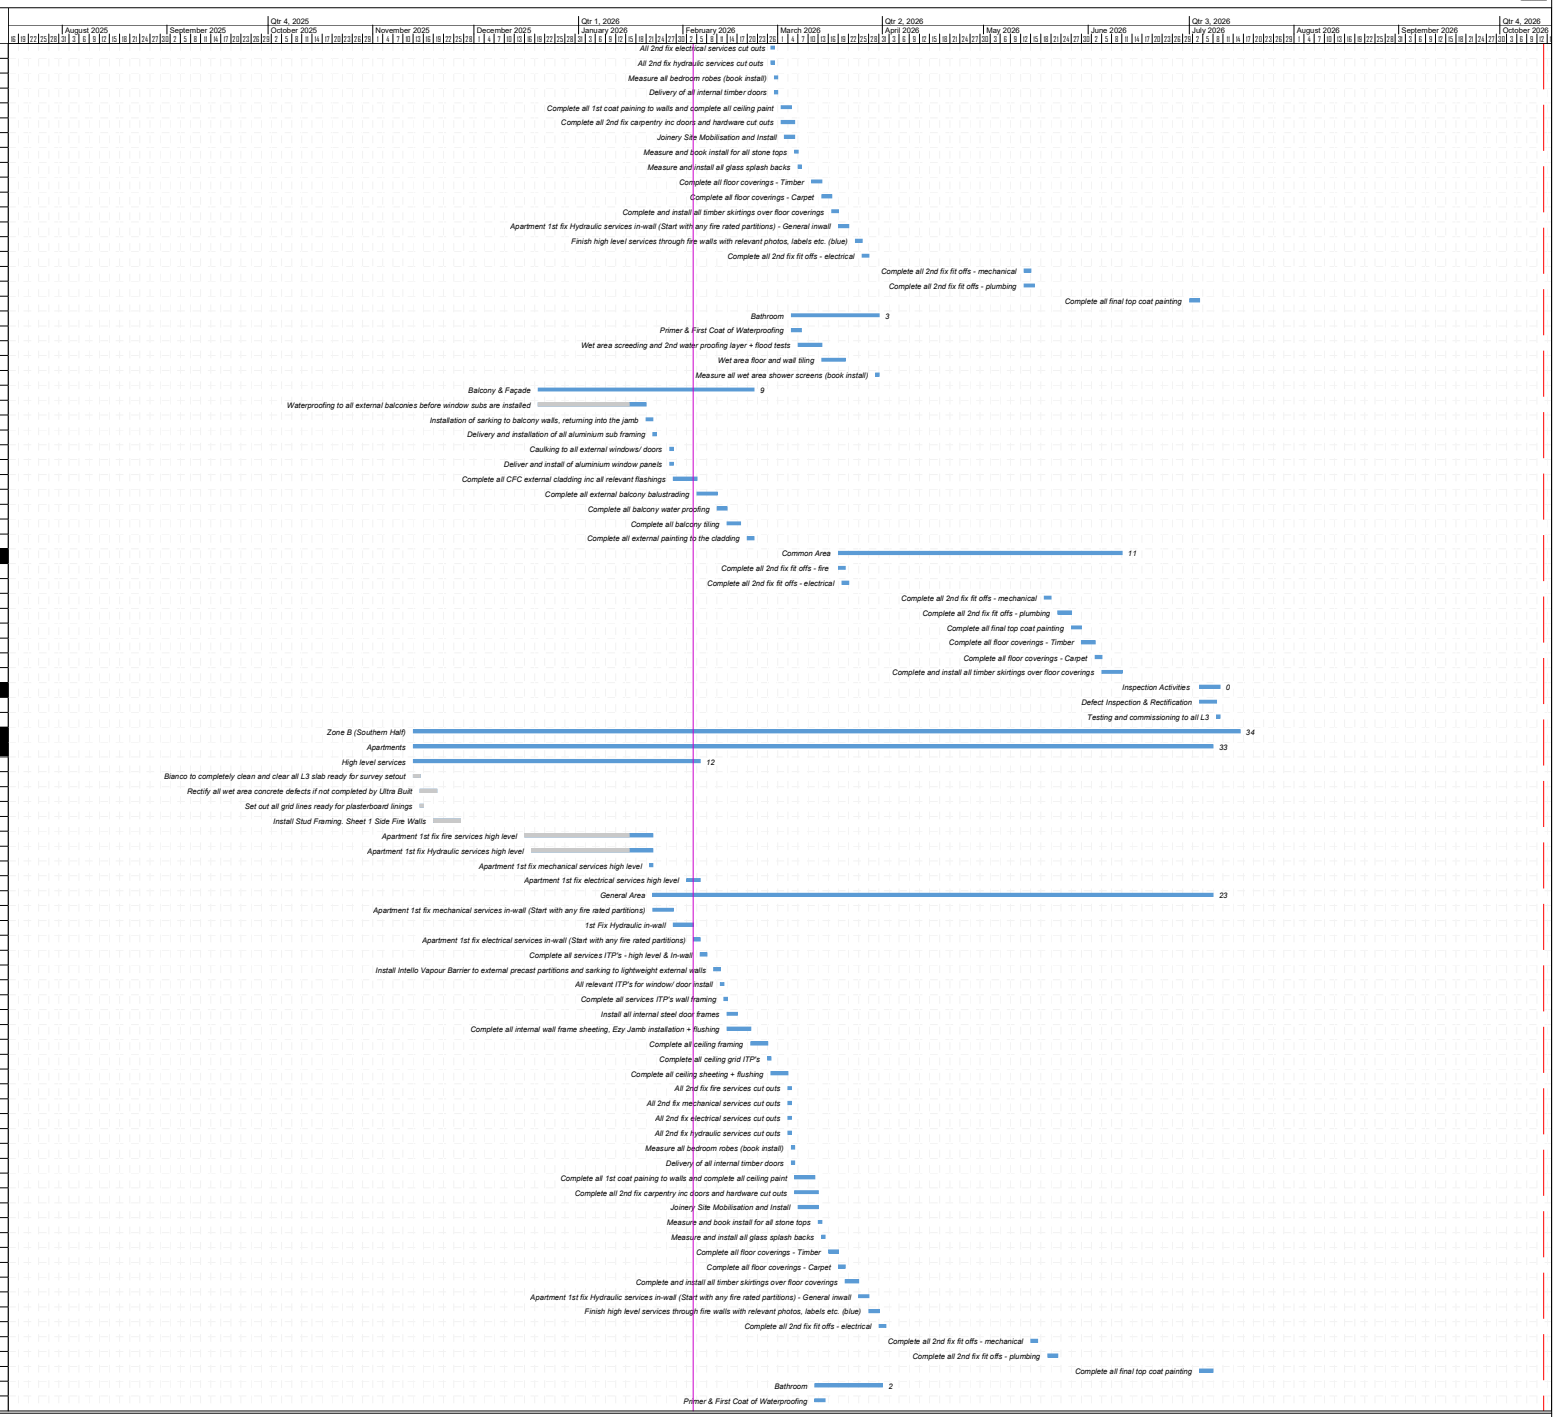

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
1959	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Sat 14/03/26	Wed 18/03/26
1960	Wet area floor and wall tiling	0%	6 days	Thu 19/03/26	Thu 26/03/26
1961	Measure all wet area shower screens (book install)	0%	1 day	Tue 31/03/26	Tue 31/03/26
1962	**Balcony & Façade**	**16%**	**35 days**	**Sat 20/12/25**	**Wed 25/02/26**
1963	Waterproofing to all external balconies before window subs are installed	56%	9 days	Sat 20/12/25	Tue 20/01/26
1964	Installation of sarking to balcony walls, returning into the jamb	0%	2 days	Wed 21/01/26	Thu 22/01/26
1965	Delivery and installation of all aluminium sub framing	0%	1 day	Fri 23/01/26	Fri 23/01/26
1966	Caulking to all external windows/ doors	0%	1 day	Wed 28/01/26	Wed 28/01/26
1967	Deliver and install of aluminium window panels	0%	1 day	Thu 29/01/26	Thu 29/01/26
1968	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 30/01/26	Thu 5/02/26
1969	Complete all external balcony balustrading	0%	4 days	Fri 6/02/26	Wed 11/02/26
1970	Complete all balcony water proofing	0%	3 days	Thu 12/02/26	Sat 14/02/26
1971	Complete all balcony tiling	0%	3 days	Mon 16/02/26	Wed 18/02/26
1972	Complete all external painting to the cladding	0%	2 days	Tue 24/02/26	Wed 25/02/26
1973	**Common Area**	**0%**	**59 days**	**Wed 25/03/26**	**Sat 13/06/26**
1974	Complete all 2nd fix fit offs - fire	0%	2 days	Wed 25/03/26	Thu 26/03/26
1975	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 25/03/26	Thu 26/03/26
1976	Complete all 2nd fix fit offs - mechanical	0%	2 days	Thu 21/05/26	Fri 22/05/26
1977	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 27/05/26	Fri 29/05/26
1978	Complete all final top coat painting	0%	3 days	Sat 30/05/26	Tue 2/06/26
1979	Complete all floor coverings - Timber	0%	3 days	Wed 3/06/26	Fri 5/06/26
1980	Complete all floor coverings - Carpet	0%	2 days	Wed 10/06/26	Thu 11/06/26
1981	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 12/06/26	Sat 13/06/26
1982	**Inspection Activities**	**0%**	**5 days**	**Thu 9/07/26**	**Wed 15/07/26**
1983	Defect Inspection & Rectification	0%	4 days	Thu 9/07/26	Tue 14/07/26
1984	Testing and commissioning to all L3	0%	1 day	Wed 15/07/26	Wed 15/07/26
1985	**Car Park**	**16%**	**440 days**	**Tue 19/11/24**	**Thu 6/08/26**
1986	Strip carpark props from pour 1	100%	2 days	Wed 5/11/25	Thu 6/11/25
1987	Strip carpark props from pour 2	100%	2 days	Fri 7/11/25	Sat 8/11/25
1988	Carpark 1st fix fire services high level	100%	4 days	Mon 10/11/25	Thu 13/11/25
1989	Carpark 1st fix mechanical services	100%	4 days	Thu 13/11/25	Tue 18/11/25
1990	Carpark 1st fix electrical services	100%	4 days	Tue 18/11/25	Fri 21/11/25
1991	Carpark 1st fix hydraulic services	100%	4 days	Fri 21/11/25	Tue 25/11/25
1992	Complete all carpark external cladding	100%	6 days	Tue 19/11/24	Mon 25/11/24
1993	Recycle props to upper levels	100%	1 day	Mon 10/11/25	Mon 10/11/25
1994	Area Used as lay down area	0%	135 days	Wed 28/01/26	Fri 24/07/26
1995	Services 2nd Fix	0%	3 days	Sat 25/07/26	Wed 29/07/26
1996	Car Park FF&E	0%	1 day	Fri 31/07/26	Fri 31/07/26
1997	Line Marking	0%	1 day	Thu 30/07/26	Thu 30/07/26
1998	Inspection + sign off	0%	1 day	Sat 1/08/26	Sat 1/08/26
1999	Commission + trade clean	0%	2 days	Mon 3/08/26	Tue 4/08/26
2000	10% Final clean	0%	2 days	Wed 5/08/26	Thu 6/08/26
2001	**FITOUT LEVEL 3**	**13%**	**162 days**	**Fri 28/11/25**	**Wed 22/07/26**
2002	**Zone A (Northern Half)**	**12%**	**158 days**	**Fri 28/11/25**	**Fri 17/07/26**
2003	**Apartments**	**14%**	**153 days**	**Fri 28/11/25**	**Fri 10/07/26**
2004	**High level services**	**53%**	**41 days**	**Fri 28/11/25**	**Wed 11/02/26**
2005	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Fri 28/11/25	Tue 2/12/25
2006	Rectify all wet area concrete defects if not completed by Ultra Built	100%	5 days	Wed 3/12/25	Mon 8/12/25
2007	Set out all grid lines ready for plasterboard linings	100%	1 day	Wed 3/12/25	Wed 3/12/25
2008	Install Stud Framing. Sheet 1 Side Fire Walls	100%	7 days	Thu 4/12/25	Thu 11/12/25
2009	Apartment 1st fix fire services high level	46%	13 days	Fri 19/12/25	Fri 23/01/26
2010	Apartment 1st fix Hydraulic services high level	0%	4 days	Fri 23/01/26	Fri 30/01/26
2011	Apartment 1st fix mechanical services high level	0%	4 days	Tue 3/02/26	Fri 6/02/26
2012	Apartment 1st fix electrical services high level	0%	4 days	Fri 6/02/26	Wed 11/02/26
2013	**General Area**	**0%**	**115 days**	**Sat 7/02/26**	**Fri 10/07/26**
2014	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 7/02/26	Tue 10/02/26
2015	1st Fix Hydraulic in-wall	0%	5 days	Wed 11/02/26	Mon 16/02/26
2016	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 17/02/26	Wed 18/02/26
2017	Complete all services ITP's - high level & In-wall	0%	2 days	Thu 19/02/26	Fri 20/02/26
2018	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	0%	2 days	Sat 21/02/26	Tue 24/02/26
2019	All relevant ITP's for window/ door install	0%	1 day	Wed 25/02/26	Wed 25/02/26
2020	Complete all services ITP's wall framing	0%	1 day	Thu 26/02/26	Thu 26/02/26
2021	Install all internal steel door frames	0%	2 days	Fri 27/02/26	Sat 28/02/26
2022	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Fri 27/02/26	Thu 5/03/26
2023	Complete all ceiling framing	0%	3 days	Fri 6/03/26	Wed 11/03/26
2024	Complete all ceiling grid ITP's	0%	1 day	Thu 12/03/26	Thu 12/03/26
2025	Complete all ceiling sheeting + flushing	0%	4 days	Fri 13/03/26	Tue 17/03/26
2026	All 2nd fix fire services cut outs	0%	1 day	Wed 18/03/26	Wed 18/03/26
2027	All 2nd fix mechanical services cut outs	0%	1 day	Wed 18/03/26	Wed 18/03/26
2028	All 2nd fix electrical services cut outs	0%	1 day	Wed 18/03/26	Wed 18/03/26
2029	All 2nd fix hydraulic services cut outs	0%	1 day	Wed 18/03/26	Wed 18/03/26
2030	Measure all bedroom robes (book install)	0%	1 day	Thu 19/03/26	Thu 19/03/26
2031	Delivery of all internal timber doors	0%	1 day	Thu 19/03/26	Thu 19/03/26
2032	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Fri 20/03/26	Tue 24/03/26
2033	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Fri 20/03/26	Wed 25/03/26
2034	Joinery Site Mobilisation and Install	0%	3 days	Sat 21/03/26	Wed 25/03/26
2035	Measure and book install for all stone tops	0%	1 day	Thu 26/03/26	Thu 26/03/26
2036	Measure and install all glass splash backs	0%	1 day	Fri 27/03/26	Fri 27/03/26
2037	Complete all floor coverings - Timber	0%	3 days	Sat 28/03/26	Tue 31/03/26
2038	Complete all floor coverings - Carpet	0%	2 days	Wed 1/04/26	Thu 2/04/26
2039	Complete and install all timber skirtings over floor coverings	0%	2 days	Wed 8/04/26	Thu 9/04/26
2040	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Fri 10/04/26	Mon 13/04/26
2041	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Tue 14/04/26	Wed 15/04/26
2042	Complete all 2nd fix fit offs - electrical	0%	2 days	Thu 16/04/26	Fri 17/04/26
2043	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 23/05/26	Mon 25/05/26
2044	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 23/05/26	Tue 26/05/26
2045	Complete all final top coat painting	0%	3 days	Wed 8/07/26	Fri 10/07/26
2046	**Bathroom**	**0%**	**13 days**	**Wed 25/03/26**	**Mon 13/04/26**
2047	Primer & First Coat of Waterproofing	0%	3 days	Wed 25/03/26	Fri 27/03/26
2048	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Fri 27/03/26	Tue 31/03/26
2049	Wet area floor and wall tiling	0%	6 days	Wed 1/04/26	Sat 11/04/26
2050	Measure all wet area shower screens (book install)	0%	1 day	Mon 13/04/26	Mon 13/04/26

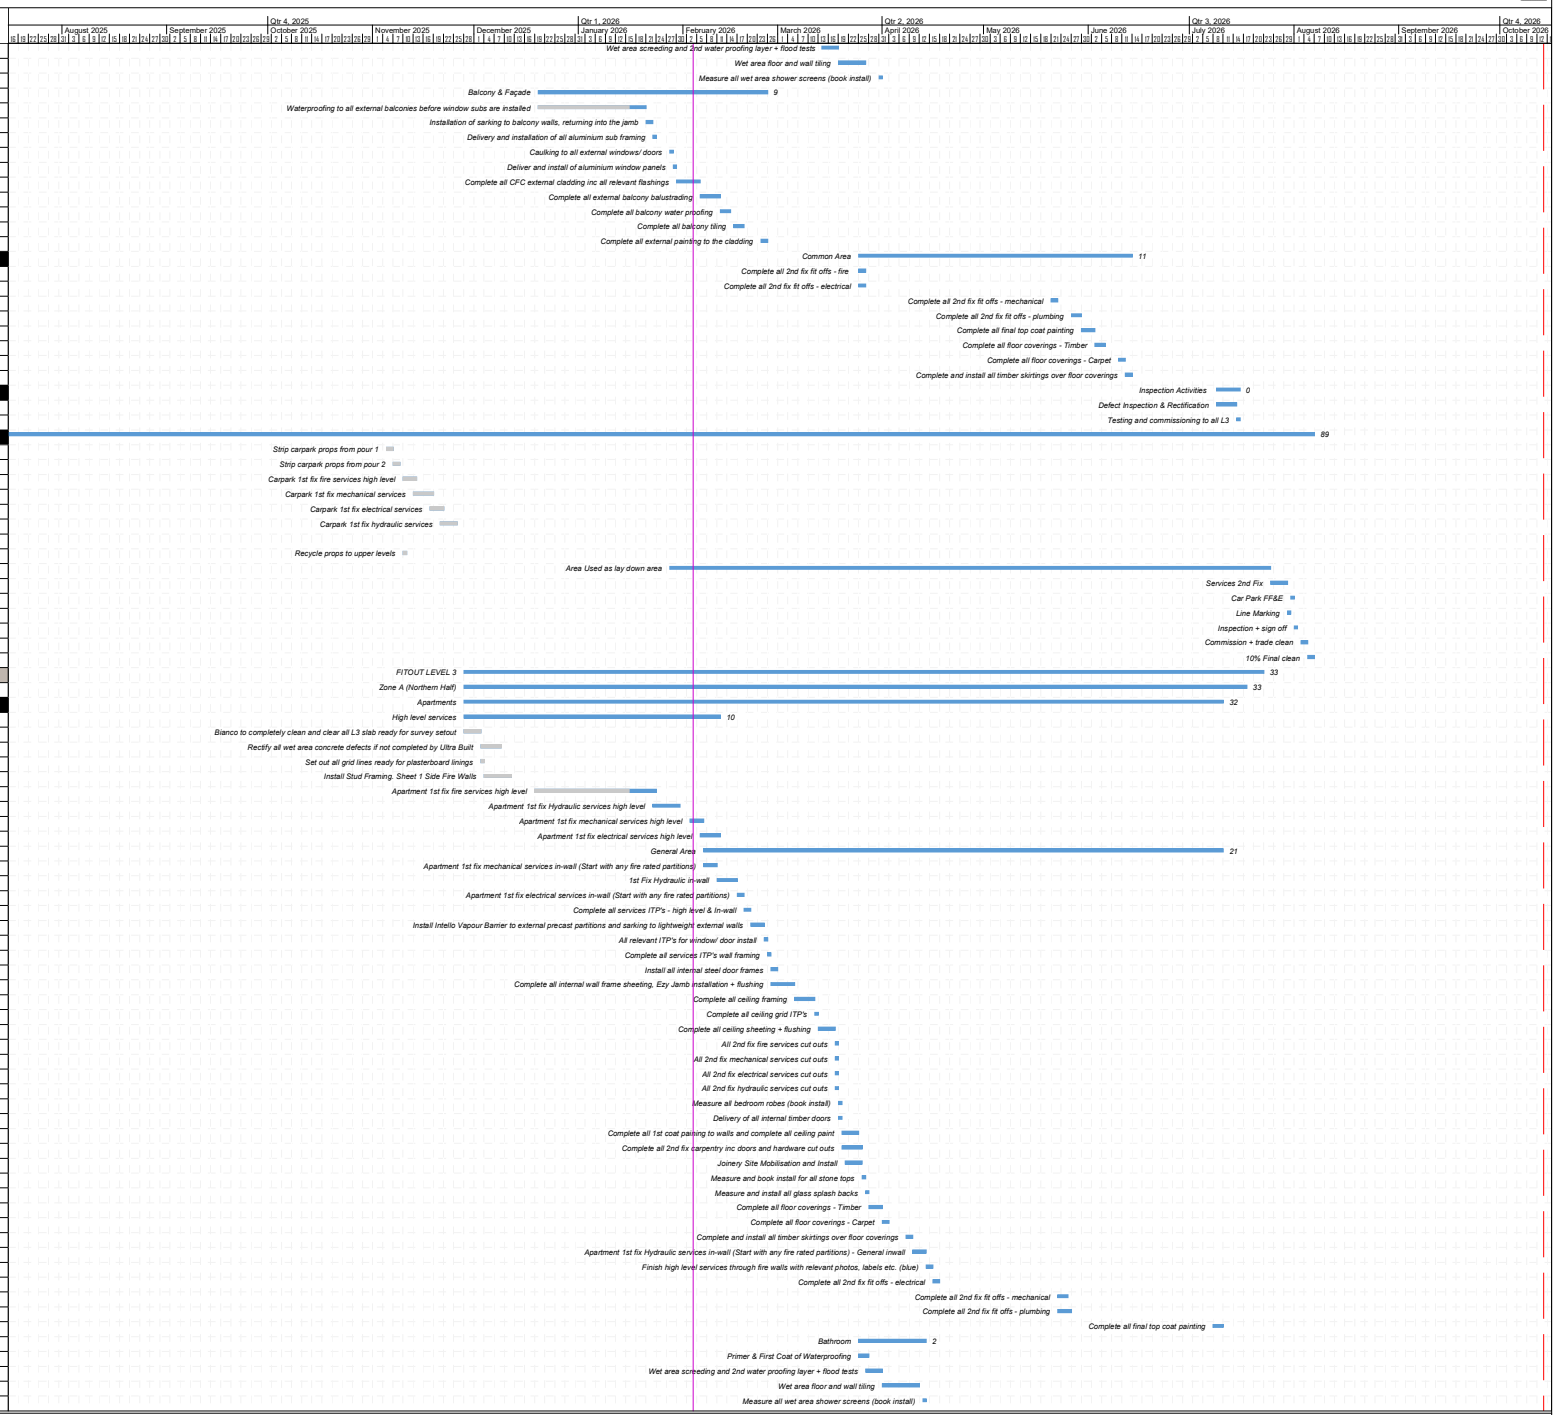

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2051	**Balcony & Façade**	**0%**	**28 days**	**Wed 21/01/26**	**Fri 27/02/26**
2052	Waterproofing to all external balconies before window subs are installed	0%	3 days	Wed 21/01/26	Fri 23/01/26
2053	Installation of sarking to balcony walls, returning into the jamb	0%	1 day	Fri 23/01/26	Fri 23/01/26
2054	Delivery and installation of all aluminium sub framing	0%	2 days	Wed 28/01/26	Thu 29/01/26
2055	Caulking to all external windows/ doors	0%	1 day	Fri 30/01/26	Fri 30/01/26
2056	Deliver and install of aluminium window panels	0%	1 day	Sat 31/01/26	Sat 31/01/26
2057	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Mon 2/02/26	Sat 7/02/26
2058	Complete all external balcony balustrading	0%	4 days	Tue 10/02/26	Fri 13/02/26
2059	Complete all balcony water proofing	0%	3 days	Sat 14/02/26	Tue 17/02/26
2060	Complete all balcony tiling	0%	3 days	Wed 18/02/26	Fri 20/02/26
2061	Complete all external painting to the cladding	0%	2 days	Thu 26/02/26	Fri 27/02/26
2062	**Common Area**	**0%**	**52 days**	**Fri 10/04/26**	**Wed 17/06/26**
2063	Complete all 2nd fix fit offs - fire	0%	2 days	Fri 10/04/26	Sat 11/04/26
2064	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 10/04/26	Sat 11/04/26
2065	Complete all 2nd fix fit offs - mechanical	0%	2 days	Thu 28/05/26	Fri 29/05/26
2066	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 30/05/26	Tue 2/06/26
2067	Complete all final top coat painting	0%	3 days	Wed 3/06/26	Fri 5/06/26
2068	Complete all floor coverings - Timber	0%	3 days	Wed 10/06/26	Fri 12/06/26
2069	Complete all floor coverings - Carpet	0%	2 days	Sat 13/06/26	Mon 15/06/26
2070	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 16/06/26	Wed 17/06/26
2071	**Inspection Activities**	**0%**	**5 days**	**Sat 11/07/26**	**Fri 17/07/26**
2072	Defect Inspection & Rectification	0%	4 days	Sat 11/07/26	Thu 16/07/26
2073	Testing and commissioning to all L3	0%	1 day	Fri 17/07/26	Fri 17/07/26
2074	**Zone B (Southern Half)**	**13%**	**159 days**	**Thu 4/12/25**	**Wed 22/07/26**
2075	**Apartments**	**15%**	**153 days**	**Thu 4/12/25**	**Wed 15/07/26**
2076	**High level services**	**58%**	**42 days**	**Thu 4/12/25**	**Mon 16/02/26**
2077	Bianco to completely clean and clear all L3 slab ready for survey setout	100%	2 days	Thu 4/12/25	Fri 5/12/25
2078	Rectify all wet area concrete defects if not completed by Ultra Built	100%	3 days	Sat 6/12/25	Tue 9/12/25
2079	Set out all grid lines ready for plasterboard linings	100%	1 day	Sat 6/12/25	Sat 6/12/25
2080	Install Stud Framing. Sheet 1 Side Fire Walls	100%	12 days	Tue 9/12/25	Mon 12/01/26
2081	Apartment 1st fix fire services high level	0%	1 day	Wed 28/01/26	Wed 28/01/26
2082	Apartment 1st fix Hydraulic services high level	0%	4 days	Sat 31/01/26	Wed 4/02/26
2083	Apartment 1st fix mechanical services high level	0%	4 days	Sat 7/02/26	Thu 12/02/26
2084	Apartment 1st fix electrical services high level	0%	4 days	Thu 12/02/26	Mon 16/02/26
2085	**General Area**	**0%**	**114 days**	**Fri 13/02/26**	**Wed 15/07/26**
2086	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Fri 13/02/26	Sat 14/02/26
2087	1st Fix Hydraulic in-wall	0%	5 days	Mon 16/02/26	Fri 20/02/26
2088	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 21/02/26	Tue 24/02/26
2089	Complete all services ITP's - high level & In-wall	0%	2 days	Wed 25/02/26	Thu 26/02/26
2090	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight exter	0%	2 days	Fri 27/02/26	Sat 28/02/26
2091	All relevant ITP's for window/ door install	0%	1 day	Mon 2/03/26	Mon 2/03/26
2092	Complete all services ITP's wall framing	0%	1 day	Tue 3/03/26	Tue 3/03/26
2093	Install all internal steel door frames	0%	2 days	Wed 4/03/26	Thu 5/03/26
2094	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	6 days	Wed 4/03/26	Thu 12/03/26
2095	Complete all ceiling framing	0%	3 days	Fri 13/03/26	Mon 16/03/26
2096	Complete all ceiling grid ITP's	0%	1 day	Tue 17/03/26	Tue 17/03/26
2097	Complete all ceiling sheeting + flushing	0%	4 days	Wed 18/03/26	Sat 21/03/26
2098	All 2nd fix fire services cut outs	0%	1 day	Tue 24/03/26	Tue 24/03/26
2099	All 2nd fix mechanical services cut outs	0%	1 day	Tue 24/03/26	Tue 24/03/26
2100	All 2nd fix electrical services cut outs	0%	1 day	Tue 24/03/26	Tue 24/03/26
2101	All 2nd fix hydraulic services cut outs	0%	1 day	Tue 24/03/26	Tue 24/03/26
2102	Measure all bedroom robes (book install)	0%	1 day	Wed 25/03/26	Wed 25/03/26
2103	Delivery of all internal timber doors	0%	1 day	Wed 25/03/26	Wed 25/03/26
2104	Complete all 1st coat paining to walls and complete all ceiling paint	0%	3 days	Thu 26/03/26	Sat 28/03/26
2105	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	4 days	Thu 26/03/26	Mon 30/03/26
2106	Joinery Site Mobilisation and Install	0%	3 days	Fri 27/03/26	Mon 30/03/26
2107	Measure and book install for all stone tops	0%	1 day	Tue 31/03/26	Tue 31/03/26
2108	Measure and install all glass splash backs	0%	1 day	Wed 1/04/26	Wed 1/04/26
2109	Complete all floor coverings - Timber	0%	3 days	Thu 2/04/26	Thu 9/04/26
2110	Complete all floor coverings - Carpet	0%	2 days	Fri 10/04/26	Sat 11/04/26
2111	Complete and install all timber skirtings over floor coverings	0%	2 days	Mon 13/04/26	Tue 14/04/26
2112	Apartment 1st fix Hydraulic services in-wall (Start with any fire rated partitions) - General	0%	3 days	Wed 15/04/26	Fri 17/04/26
2113	Finish high level services through fire walls with relevant photos, labels etc. (blue)	0%	2 days	Sat 18/04/26	Mon 20/04/26
2114	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 21/04/26	Wed 22/04/26
2115	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 26/05/26	Wed 27/05/26
2116	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 27/05/26	Fri 29/05/26
2117	Complete all final top coat painting	0%	3 days	Sat 11/07/26	Wed 15/07/26
2118	**Bathroom**	**0%**	**13 days**	**Mon 30/03/26**	**Fri 17/04/26**
2119	Primer & First Coat of Waterproofing	0%	3 days	Mon 30/03/26	Wed 1/04/26
2120	Wet area screeding and 2nd water proofing layer + flood tests	0%	4 days	Wed 1/04/26	Thu 9/04/26
2121	Wet area floor and wall tiling	0%	6 days	Fri 10/04/26	Thu 16/04/26
2122	Measure all wet area shower screens (book install)	0%	1 day	Fri 17/04/26	Fri 17/04/26
2123	**Balcony & Façade**	**14%**	**39 days**	**Sat 20/12/25**	**Mon 2/03/26**
2124	Waterproofing to all external balconies before window subs are installed	42%	12 days	Sat 20/12/25	Fri 23/01/26
2125	Installation of sarking to balcony walls, returning into the jamb	0%	1 day	Wed 28/01/26	Wed 28/01/26
2126	Delivery and installation of all aluminium sub framing	0%	2 days	Fri 30/01/26	Sat 31/01/26
2127	Caulking to all external windows/ doors	0%	1 day	Mon 2/02/26	Mon 2/02/26
2128	Deliver and install of aluminium window panels	0%	1 day	Tue 3/02/26	Tue 3/02/26
2129	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Wed 4/02/26	Wed 11/02/26
2130	Complete all external balcony balustrading	0%	4 days	Thu 12/02/26	Mon 16/02/26
2131	Complete all balcony water proofing	0%	3 days	Tue 17/02/26	Thu 19/02/26
2132	Complete all balcony tiling	0%	3 days	Fri 20/02/26	Tue 24/02/26
2133	Complete all external painting to the cladding	0%	2 days	Sat 28/02/26	Mon 2/03/26
2134	**Common Area**	**0%**	**51 days**	**Wed 15/04/26**	**Sat 20/06/26**
2135	Complete all 2nd fix fit offs - fire	0%	2 days	Wed 15/04/26	Thu 16/04/26
2136	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 15/04/26	Thu 16/04/26
2137	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 30/05/26	Mon 1/06/26
2138	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 3/06/26	Fri 5/06/26
2139	Complete all final top coat painting	0%	3 days	Wed 10/06/26	Fri 12/06/26
2140	Complete all floor coverings - Timber	0%	3 days	Sat 13/06/26	Tue 16/06/26
2141	Complete all floor coverings - Carpet	0%	2 days	Wed 17/06/26	Thu 18/06/26
2142	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 19/06/26	Sat 20/06/26

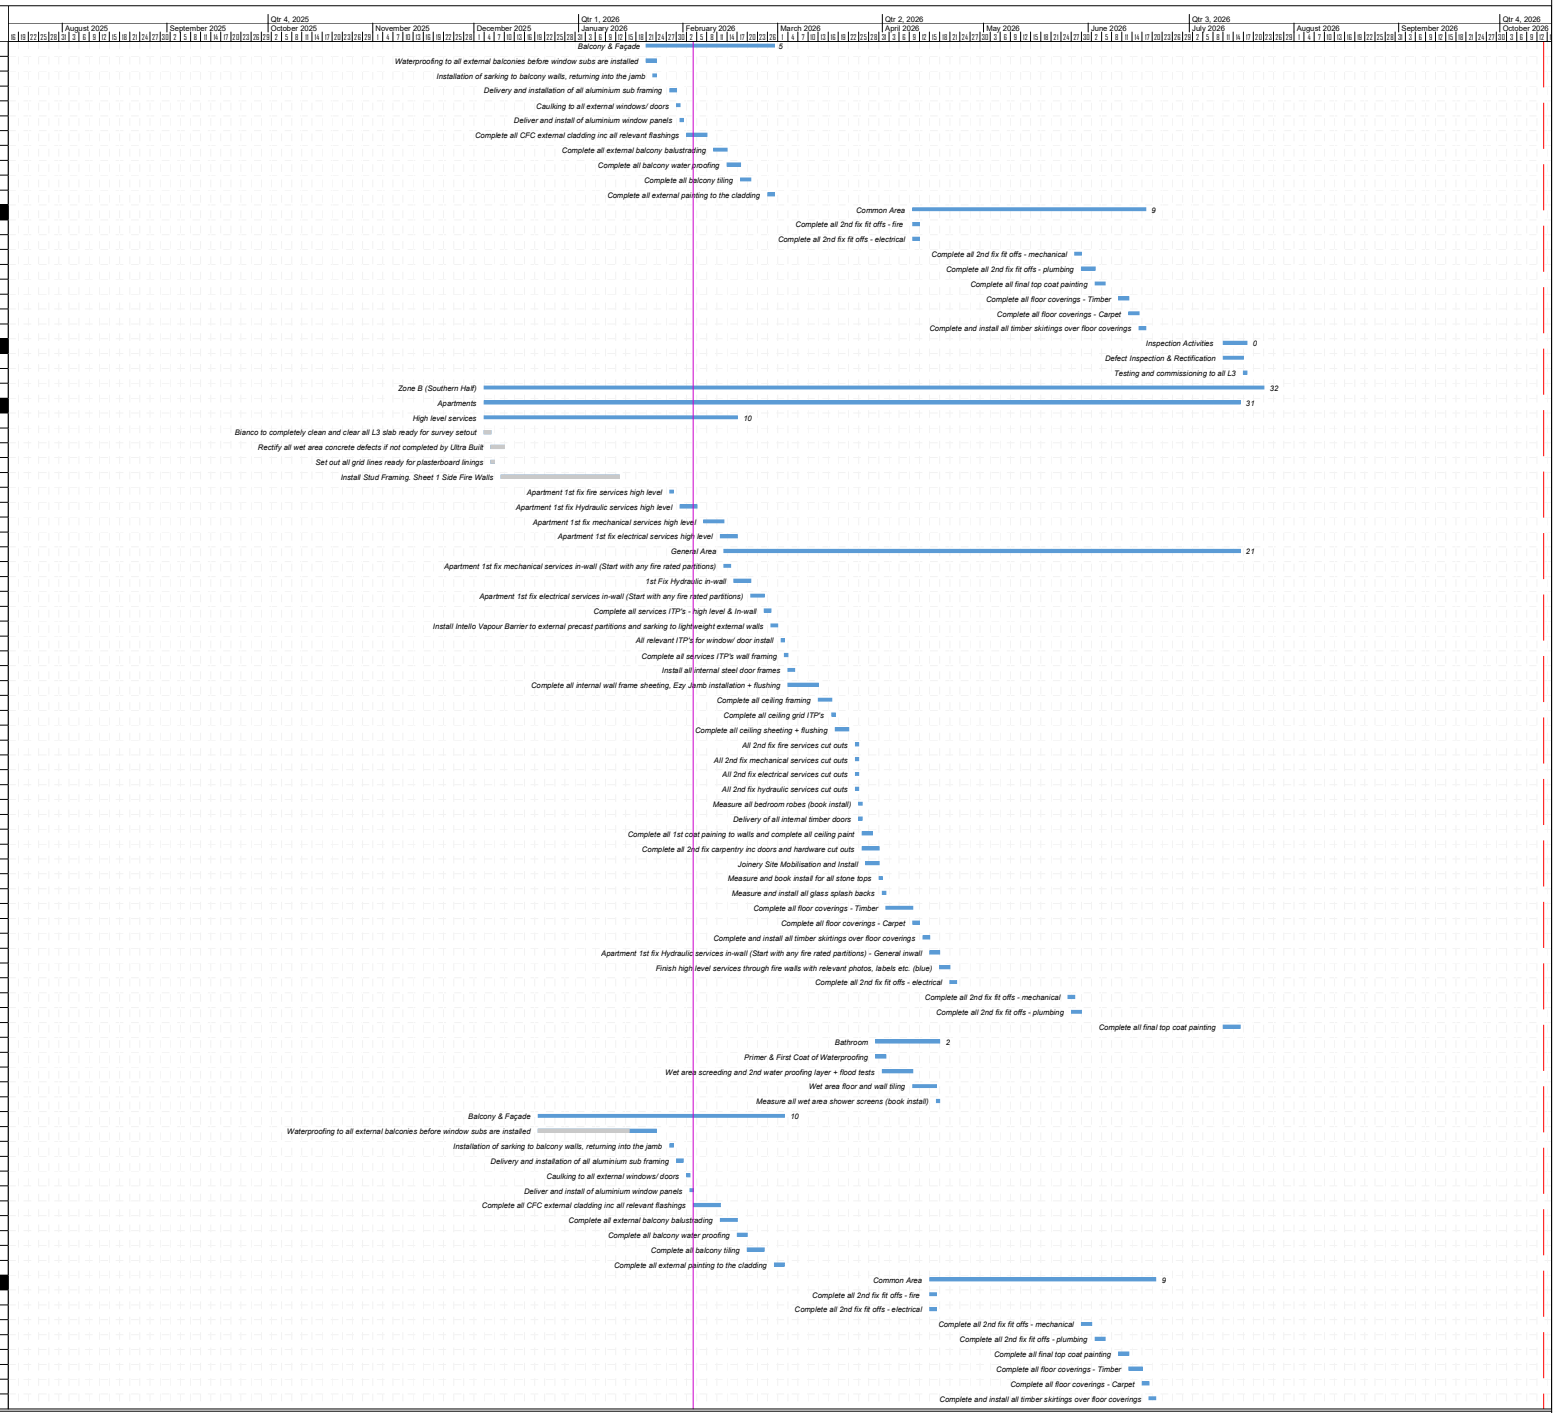

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

Planner: **Steve Church** Review: **Marcus Anderson**

ID	Name	% Complete	Duration	Start	Finish
2143	**Inspection Activities**	**0%**	**5 days**	**Fri 17/07/26**	**Wed 22/07/26**
2144	Defect Inspection & Rectification	0%	4 days	Fri 17/07/26	Tue 21/07/26
2145	Testing and commissioning to all L3	0%	1 day	Wed 22/07/26	Wed 22/07/26
2146	FITOUT LEVEL 4	0%	102.5 days	Sat 20/12/25	Thu 28/05/26
2147	**Overall Floor**	**0%**	**27 days**	**Sat 20/12/25**	**Sat 14/02/26**
2148	**High level services**	**0%**	**11 days**	**Sat 20/12/25**	**Thu 22/01/26**
2149	Bianco to clear slab (Acrow Props only)	0%	2 days	Sat 20/12/25	Mon 12/01/26
2150	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Tue 13/01/26	Thu 15/01/26
2151	Precast Caulking/ Grout complete	0%	0 days	Thu 15/01/26	Thu 15/01/26
2152	Set out Wall frames	0%	1 day	Thu 22/01/26	Thu 22/01/26
2153	Apartment 1st fix fire services high level	0%	4 days	Tue 13/01/26	Fri 16/01/26
2154	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Thu 15/01/26	Mon 19/01/26
2155	Apartment 1st fix mechanical services high level	0%	4 days	Sat 17/01/26	Wed 21/01/26
2156	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**24 days**	**Tue 13/01/26**	**Sat 14/02/26**
2157	Delivery of stud works + Entry door frames	0%	0 days	Tue 13/01/26	Tue 13/01/26
2158	Install external/balcony stud framing +Sheet moisture resistant plasterboard externally + over	0%	3 days	Fri 23/01/26	Thu 29/01/26
2159	Intello wrap install	0%	1 day	Fri 30/01/26	Fri 30/01/26
2160	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Fri 30/01/26	Mon 2/02/26
2161	Install F channel for Balustrade	0%	4 days	Tue 10/02/26	Fri 13/02/26
2162	Delivery of all windows	0%	0 days	Wed 28/01/26	Wed 28/01/26
2163	Delivery of plasterboard	0%	0 days	Sat 31/01/26	Sat 31/01/26
2164	Delivery of Door frame ready on site	0%	0 days	Fri 30/01/26	Fri 30/01/26
2165	Install window subframes (start with precast)	0%	4 days	Tue 3/02/26	Fri 6/02/26
2166	Subframe flood test sign off	0%	1 day	Sat 7/02/26	Sat 7/02/26
2167	Install window panels	0%	2 days	Tue 10/02/26	Wed 11/02/26
2168	Install Subsil/head for Sliding doors	0%	2 days	Thu 5/02/26	Fri 6/02/26
2169	Subsil flood test sign off	0%	1 day	Sat 7/02/26	Sat 7/02/26
2170	Install sliding door panels	0%	2 days	Thu 12/02/26	Fri 13/02/26
2171	All relevant ITP's for window	0%	1 day	Sat 14/02/26	Sat 14/02/26
2172	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Fri 30/01/26	Tue 3/02/26
2173	**Northern Apartments**	**0%**	**61.5 days**	**Thu 5/02/26**	**Thu 30/04/26**
2174	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 5/02/26	Fri 6/02/26
2175	1st Fix Hydraulic in-wall	0%	4 days	Thu 5/02/26	Tue 10/02/26
2176	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 5/02/26	Fri 6/02/26
2177	Nogging (Trimmers) install	0%	1 day	Tue 10/02/26	Tue 10/02/26
2178	Complete all presheeting ITP	0%	2 days	Wed 11/02/26	Thu 12/02/26
2179	Complete all internal wall sheeting, Ezy Jamb installation + flushing+ J track	0%	6 days	Fri 13/02/26	Thu 19/02/26
2180	Measure all bedroom robes (book install)	0%	0 days	Thu 19/02/26	Thu 19/02/26
2181	Complete all ceiling framing	0%	3 days	Fri 20/02/26	Tue 24/02/26
2182	Measure Kitchens and fabricate	0%	3.5 wks	Fri 20/02/26	Mon 16/03/26
2183	Complete all ceiling grid ITP's	0%	1 day	Wed 25/02/26	Wed 25/02/26
2184	Complete all ceiling sheeting + flushing	0%	4 days	Thu 26/02/26	Mon 2/03/26
2185	Flush corridor walls	0%	4 days	Fri 13/02/26	Tue 17/02/26
2186	All 2nd fix fire services cut outs	0%	2 days	Tue 3/03/26	Wed 4/03/26
2187	All 2nd fix mechanical services cut outs	0%	2 days	Tue 3/03/26	Wed 4/03/26
2188	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Tue 3/03/26	Wed 4/03/26
2189	All 2nd fix hydraulic services cut outs	0%	2 days	Tue 3/03/26	Wed 4/03/26
2190	Delivery of all internal timber doors	0%	1 day	Tue 3/03/26	Tue 3/03/26
2191	Complete all 1st coat paining to walls and ceiling	0%	2 days	Tue 3/03/26	Wed 4/03/26
2192	Hang doors and hardware cut outs	0%	4 days	Wed 4/03/26	Sat 7/03/26
2193	Plasterboard defects	0%	1 day	Thu 5/03/26	Thu 5/03/26
2194	Finish coat ceiling	0%	2 days	Fri 6/03/26	Sat 7/03/26
2195	Services trades fit off ceiling	0%	3 days	Wed 11/03/26	Fri 13/03/26
2196	Joinery Site Mobilisation and Install	0%	3 days	Mon 16/03/26	Thu 19/03/26
2197	Measure and book install for all stone tops	0%	2 wks	Thu 19/03/26	Wed 1/04/26
2198	Install Bench tops	0%	1 day	Wed 1/04/26	Thu 2/04/26
2199	Measure and install all glass splash backs	0%	2 wks	Thu 2/04/26	Sat 18/04/26
2200	Install splashback	0%	1 day	Sat 18/04/26	Mon 20/04/26
2201	Floor prep	0%	3 days	Wed 18/03/26	Sat 21/03/26
2202	2nd Coat wall	0%	2 days	Sat 21/03/26	Wed 25/03/26
2203	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 25/03/26	Fri 27/03/26
2204	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 25/03/26	Fri 27/03/26
2205	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 25/03/26	Sat 28/03/26
2206	Complete timber floor	0%	3 days	Sat 28/03/26	Wed 1/04/26
2207	Complete and install all timber skirtings	0%	2 days	Wed 22/04/26	Fri 24/04/26
2208	Complete all final top coat painting	0%	3 days	Sat 18/04/26	Wed 22/04/26
2209	Final Clean	0%	1 day	Fri 24/04/26	Tue 28/04/26
2210	Complete all floor coverings - Carpet	0%	2 days	Tue 28/04/26	Thu 30/04/26
2211	**Bathroom**	**0%**	**27 days**	**Sat 21/02/26**	**Sat 28/03/26**
2212	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Sat 21/02/26	Wed 25/02/26
2213	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Thu 26/02/26	Mon 2/03/26
2214	Wet area floor and wall tiling	0%	6 days	Tue 3/03/26	Wed 11/03/26
2215	Measure all wet area shower screens (book install)	0%	10 days	Thu 12/03/26	Tue 24/03/26
2216	Initial clean	0%	1 day	Thu 12/03/26	Thu 12/03/26
2217	Fit off ceiling	0%	1 day	Fri 13/03/26	Fri 13/03/26
2218	PC item fit off	0%	3 days	Sat 14/03/26	Tue 17/03/26
2219	Shaving cabinets	0%	2 days	Wed 18/03/26	Thu 19/03/26
2220	Shower screens	0%	2 days	Wed 25/03/26	Thu 26/03/26
2221	FF&E Fit off	0%	2 days	Fri 27/03/26	Sat 28/03/26
2222	**Balcony & Façade**	**0%**	**19 days**	**Sat 14/02/26**	**Wed 11/03/26**
2223	Caulking to all external windows/ doors	0%	1 day	Sat 14/02/26	Sat 14/02/26
2224	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Mon 16/02/26	Sat 21/02/26
2225	Complete all external balcony balustrading	0%	4 days	Tue 24/02/26	Fri 27/02/26
2226	Complete all balcony water proofing	0%	3 days	Sat 28/02/26	Tue 3/03/26
2227	Complete all balcony tiling	0%	3 days	Wed 4/03/26	Fri 6/03/26
2228	Complete all external painting to the cladding	0%	2 days	Sat 7/03/26	Wed 11/03/26
2229	**Southern Apartments**	**0%**	**62.5 days**	**Sat 7/02/26**	**Tue 5/05/26**
2230	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 7/02/26	Tue 10/02/26
2231	1st Fix Hydraulic in-wall	0%	4 days	Wed 11/02/26	Sat 14/02/26
2232	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 7/02/26	Tue 10/02/26
2233	Nogging (Trimmers) install	0%	1 day	Sat 14/02/26	Sat 14/02/26
2234	Complete all presheeting ITP	0%	2 days	Mon 16/02/26	Tue 17/02/26

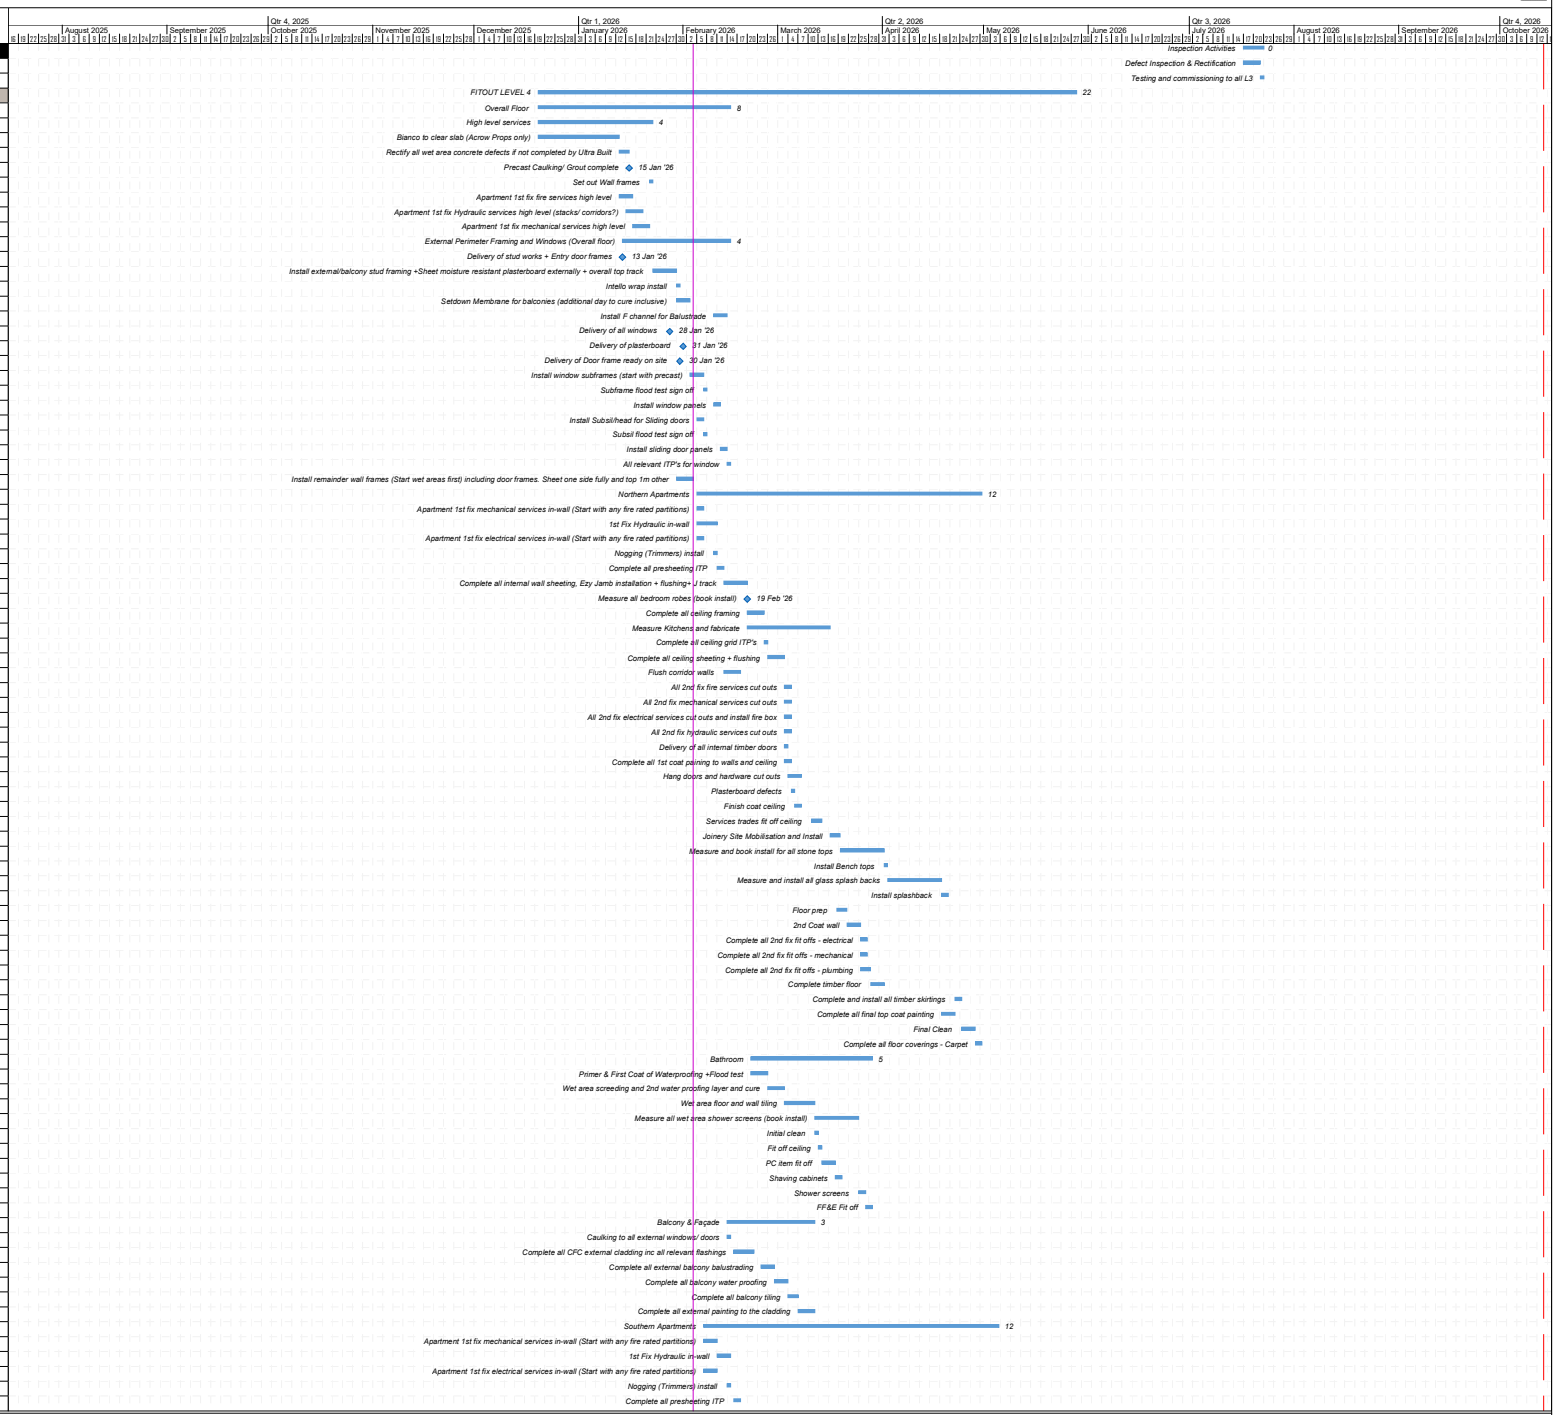

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2235	Complete all internal wall sheeting, Ezy Jamb installation + flushing	0%	6 days	Wed 18/02/26	Wed 25/02/26
2236	Measure all bedroom robes (book install)	0%	0 days	Wed 25/02/26	Wed 25/02/26
2237	Complete all ceiling framing	0%	3 days	Thu 26/02/26	Sat 28/02/26
2238	Measure Kitchens and fabricate	0%	3.5 wks	Mon 2/03/26	Wed 25/03/26
2239	Complete all ceiling grid ITP's	0%	1 day	Mon 2/03/26	Mon 2/03/26
2240	Complete all ceiling sheeting + flushing	0%	4 days	Tue 3/03/26	Fri 6/03/26
2241	Flush corridor walls	0%	4 days	Wed 18/02/26	Sat 21/02/26
2242	All 2nd fix fire services cut outs	0%	2 days	Sat 7/03/26	Wed 11/03/26
2243	All 2nd fix mechanical services cut outs	0%	2 days	Sat 7/03/26	Wed 11/03/26
2244	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Sat 7/03/26	Wed 11/03/26
2245	All 2nd fix hydraulic services cut outs	0%	2 days	Sat 7/03/26	Wed 11/03/26
2246	Delivery of all internal timber doors	0%	1 day	Sat 7/03/26	Sat 7/03/26
2247	Complete all 1st coat paining to walls and ceiling	0%	2 days	Sat 7/03/26	Wed 11/03/26
2248	Hang doors and hardware cut outs	0%	4 days	Wed 11/03/26	Sat 14/03/26
2249	Plasterboard defects	0%	1 day	Thu 12/03/26	Thu 12/03/26
2250	Finish coat ceiling	0%	2 days	Fri 13/03/26	Sat 14/03/26
2251	Services trades fit off ceiling	0%	3 days	Mon 16/03/26	Wed 18/03/26
2252	Joinery Site Mobilisation and Install	0%	3 days	Wed 25/03/26	Sat 28/03/26
2253	Measure and book install for all stone tops	0%	2 wks	Sat 28/03/26	Tue 14/04/26
2254	Install Bench tops	0%	1 day	Tue 14/04/26	Wed 15/04/26
2255	Measure and install all glass splash backs	0%	2 wks	Wed 15/04/26	Wed 29/04/26
2256	Install splashback	0%	1 day	Wed 29/04/26	Thu 30/04/26
2257	Floor prep	0%	3 days	Fri 27/03/26	Tue 31/03/26
2258	2nd Coat wall	0%	2 days	Tue 31/03/26	Thu 2/04/26
2259	Complete all 2nd fix fit offs - electrical	0%	2 days	Thu 2/04/26	Thu 9/04/26
2260	Complete all 2nd fix fit offs - mechanical	0%	2 days	Thu 2/04/26	Thu 9/04/26
2261	Complete all 2nd fix fit offs - plumbing	0%	3 days	Thu 2/04/26	Fri 10/04/26
2262	Complete Timber Flooring	0%	3 days	Fri 10/04/26	Tue 14/04/26
2263	Complete and install all timber skirtings	0%	2 days	Fri 17/04/26	Mon 20/04/26
2264	Complete all final top coat painting	0%	3 days	Tue 14/04/26	Fri 17/04/26
2265	Final Clean	0%	1 day	Thu 30/04/26	Fri 1/05/26
2266	Complete all floor coverings - Carpet	0%	2 days	Fri 1/05/26	Tue 5/05/26
2267	**Bathroom**	**0%**	**27 days**	**Fri 27/02/26**	**Thu 2/04/26**
2268	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Fri 27/02/26	Mon 2/03/26
2269	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Tue 3/03/26	Fri 6/03/26
2270	Wet area floor and wall tiling	0%	6 days	Sat 7/03/26	Mon 16/03/26
2271	Measure all wet area shower screens (book install)	0%	2 wks	Tue 17/03/26	Sat 28/03/26
2272	Initial clean	0%	1 day	Tue 17/03/26	Tue 17/03/26
2273	Fit off ceiling	0%	1 day	Wed 18/03/26	Wed 18/03/26
2274	PC item fit off	0%	3 days	Thu 19/03/26	Sat 21/03/26
2275	Shaving cabinets	0%	2 days	Tue 24/03/26	Wed 25/03/26
2276	Shower screens	0%	2 days	Mon 30/03/26	Tue 31/03/26
2277	FF&E Fit off	0%	2 days	Wed 1/04/26	Thu 2/04/26
2278	**Balcony & Façade**	**0%**	**19 days**	**Sat 14/02/26**	**Wed 11/03/26**
2279	Caulking to all external windows/ doors	0%	1 day	Sat 14/02/26	Sat 14/02/26
2280	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Mon 16/02/26	Sat 21/02/26
2281	Complete all external balcony balustrading	0%	4 days	Tue 24/02/26	Fri 27/02/26
2282	Complete all balcony water proofing	0%	3 days	Sat 28/02/26	Tue 3/03/26
2283	Complete all balcony tiling	0%	3 days	Wed 4/03/26	Fri 6/03/26
2284	Complete all external painting to the cladding	0%	2 days	Sat 7/03/26	Wed 11/03/26
2285	**Common Area (Corridors)**	**0%**	**69.5 days**	**Tue 24/02/26**	**Thu 28/05/26**
2286	Prime walls	0%	1 day	Tue 24/02/26	Tue 24/02/26
2287	Ceiling framing	0%	2 days	Sat 28/03/26	Tue 31/03/26
2288	Services and Ceiling Closeout ITP	0%	1 day	Tue 31/03/26	Wed 1/04/26
2289	Sheet and Flush Ceiling	0%	4 days	Wed 1/04/26	Fri 10/04/26
2290	Cut out ceilign services	0%	1 day	Fri 10/04/26	Sat 11/04/26
2291	2nd Coat wall and Finish coat ceiling	0%	3 days	Sat 11/04/26	Wed 15/04/26
2292	Complete all 2nd fix fit offs - fire	0%	2 days	Wed 15/04/26	Fri 17/04/26
2293	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 15/04/26	Fri 17/04/26
2294	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 15/04/26	Fri 17/04/26
2295	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 15/04/26	Sat 18/04/26
2296	Complete all final top coat painting	0%	3 days	Sat 18/04/26	Wed 22/04/26
2297	Complete all floor coverings - Timber	0%	3 days	Wed 22/04/26	Tue 28/04/26
2298	Complete all floor coverings - Carpet	0%	2 days	Tue 5/05/26	Thu 7/05/26
2299	Complete and install all timber skirtings over floor coverings	0%	2 days	Thu 7/05/26	Sat 9/05/26
2300	**Inspection Activities**	**0%**	**15 days**	**Sat 9/05/26**	**Thu 28/05/26**
2301	Defect Inspection & Rectification	0%	4 days	Sat 9/05/26	Thu 14/05/26
2302	Testing and commissioning to all L4	0%	1 day	Thu 14/05/26	Fri 15/05/26
2303	Contingency	0%	10 days	Fri 15/05/26	Thu 28/05/26
2304	FITOUT LEVEL 5	0%	98.5 days	Thu 22/01/26	Thu 4/06/26
2305	**Overall Floor**	**0%**	**24 days**	**Thu 22/01/26**	**Tue 24/02/26**
2306	**High level services**	**0%**	**15 days**	**Thu 22/01/26**	**Thu 12/02/26**
2307	Bianco to clear slab (Acrow Props only)	0%	2 days	Thu 22/01/26	Fri 23/01/26
2308	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Wed 28/01/26	Fri 30/01/26
2309	Precast Caulking/ Grout complete	0%	0 days	Fri 30/01/26	Fri 30/01/26
2310	Delivery of stud works + Entry door frames	0%	0 days	Tue 3/02/26	Tue 3/02/26
2311	Set out Wall frames +install top track	0%	4 days	Tue 3/02/26	Fri 6/02/26
2312	Delivery of all windows	0%	0 days	Wed 4/02/26	Wed 4/02/26
2313	Apartment 1st fix fire services high level	0%	4 days	Tue 3/02/26	Fri 6/02/26
2314	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Thu 5/02/26	Tue 10/02/26
2315	Apartment 1st fix mechanical services high level	0%	4 days	Sat 7/02/26	Thu 12/02/26
2316	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**14 days**	**Fri 6/02/26**	**Tue 24/02/26**
2317	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Fri 6/02/26	Tue 10/02/26
2318	Intello wrap install	0%	1 day	Wed 11/02/26	Wed 11/02/26
2319	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Wed 11/02/26	Fri 13/02/26
2320	Install F channel for Balustrade	0%	4 days	Sat 14/02/26	Wed 18/02/26
2321	Delivery of plasterboard	0%	0 days	Thu 12/02/26	Thu 12/02/26
2322	Delivery of Door frame ready on site	0%	0 days	Wed 11/02/26	Wed 11/02/26
2323	Install window subframes (start with precast)	0%	4 days	Thu 12/02/26	Mon 16/02/26
2324	Subframe flood test sign off	0%	1 day	Tue 17/02/26	Tue 17/02/26
2325	Install window panels	0%	2 days	Wed 18/02/26	Thu 19/02/26

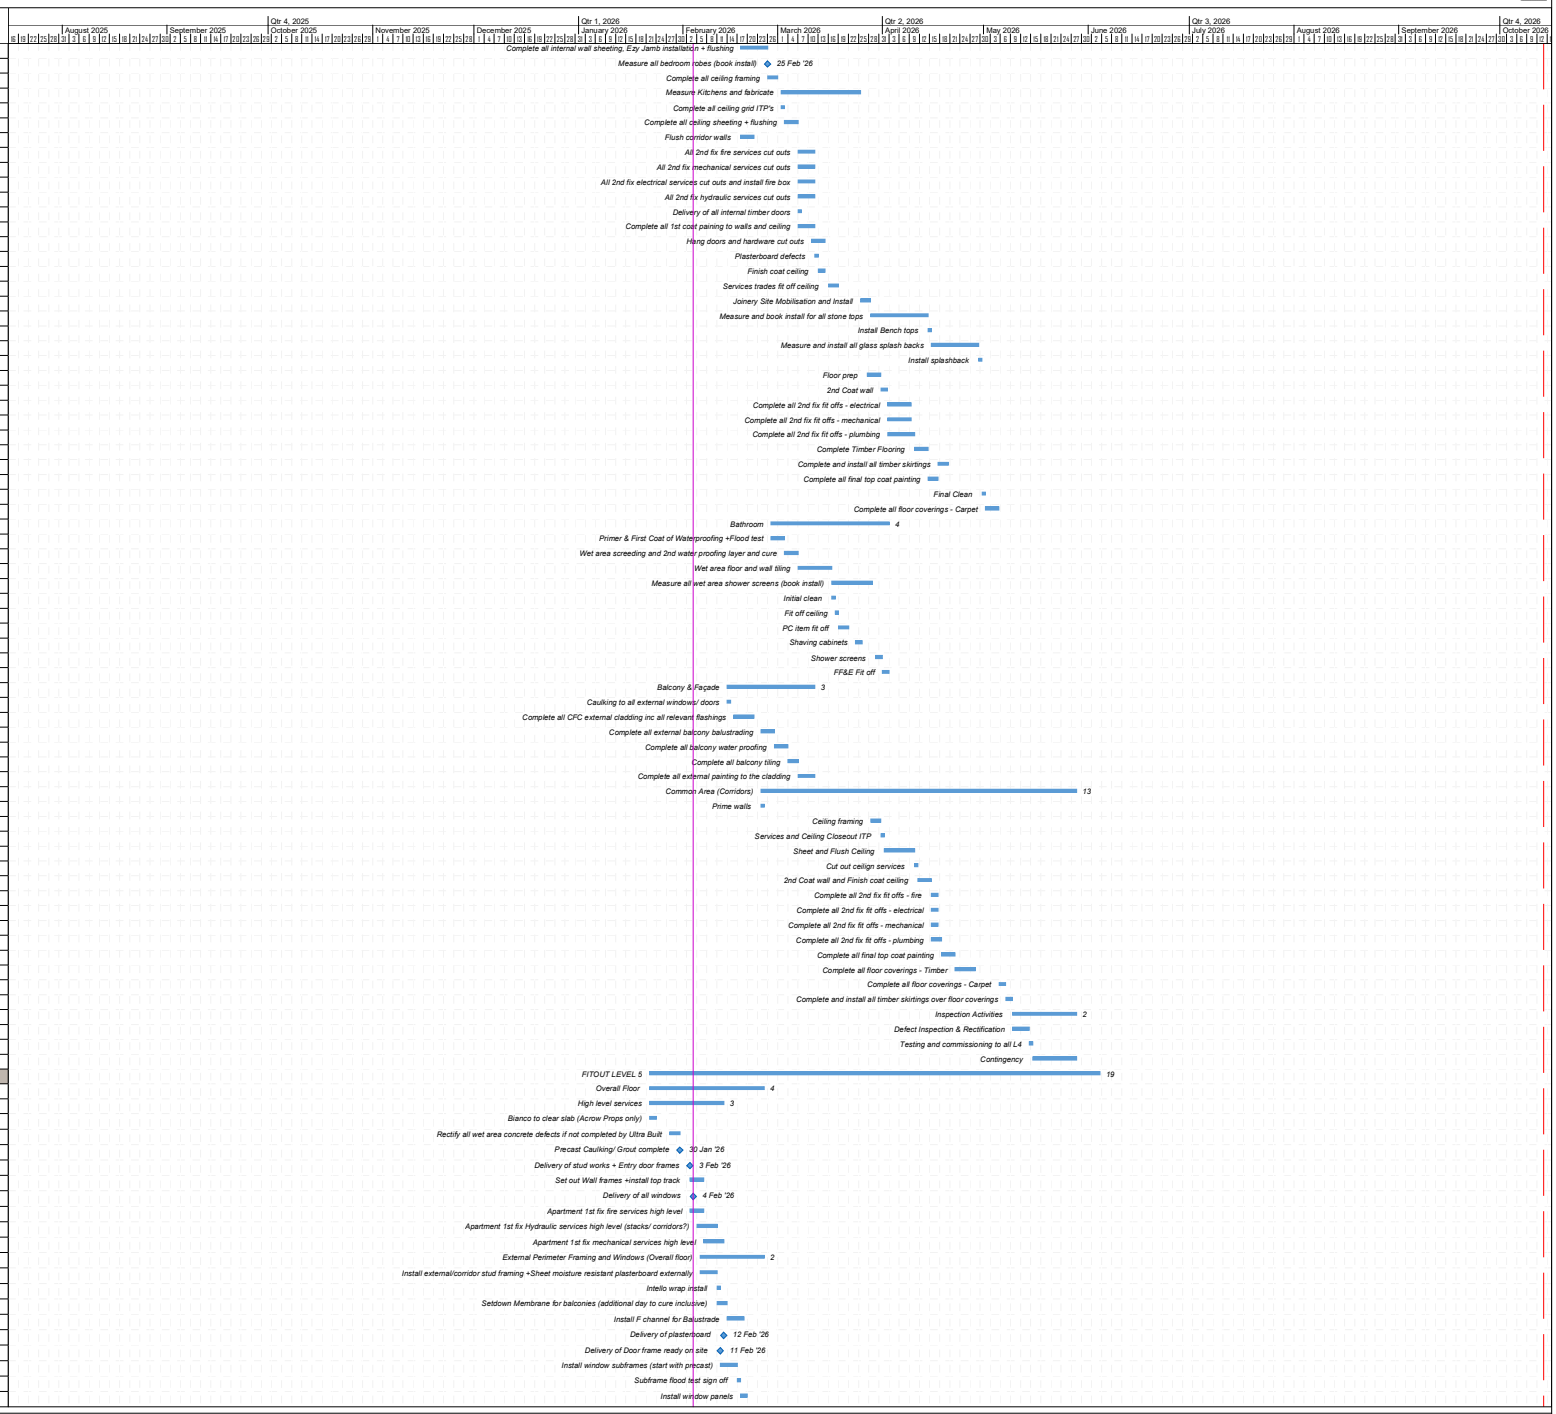

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2326	Install Subsil/head for Sliding doors	0%	2 days	Sat 14/02/26	Mon 16/02/26
2327	Subsil flood test sign off	0%	1 day	Tue 17/02/26	Tue 17/02/26
2328	Install sliding door panels	0%	2 days	Fri 20/02/26	Sat 21/02/26
2329	All relevant ITP's for window	0%	1 day	Tue 24/02/26	Tue 24/02/26
2330	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Wed 11/02/26	Sat 14/02/26
2331	**Northern Apartments**	**0%**	**61.5 days**	**Fri 13/02/26**	**Fri 8/05/26**
2332	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Fri 13/02/26	Sat 14/02/26
2333	1st Fix Hydraulic in-wall	0%	4 days	Fri 13/02/26	Tue 17/02/26
2334	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Fri 13/02/26	Sat 14/02/26
2335	Nogging (Trimmers) install	0%	1 day	Tue 17/02/26	Tue 17/02/26
2336	Complete all presheeting ITP	0%	2 days	Wed 18/02/26	Thu 19/02/26
2337	Complete all internal wall sheeting, Ezy Jamb installation + flushing+ Ceiling J Track	0%	6 days	Fri 20/02/26	Fri 27/02/26
2338	Measure all bedroom robes (book install)	0%	0 days	Fri 27/02/26	Fri 27/02/26
2339	Complete all ceiling framing	0%	3 days	Sat 28/02/26	Tue 3/03/26
2340	Measure Kitchens and fabricate	0%	3.5 wks	Sat 28/02/26	Tue 24/03/26
2341	Complete all ceiling grid ITP's	0%	1 day	Wed 4/03/26	Wed 4/03/26
2342	Complete all ceiling sheeting + flushing	0%	4 days	Thu 5/03/26	Wed 11/03/26
2343	Flush corridor walls	0%	4 days	Fri 20/02/26	Wed 25/02/26
2344	All 2nd fix fire services cut outs	0%	2 days	Thu 12/03/26	Fri 13/03/26
2345	All 2nd fix mechanical services cut outs	0%	2 days	Thu 12/03/26	Fri 13/03/26
2346	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Thu 12/03/26	Fri 13/03/26
2347	All 2nd fix hydraulic services cut outs	0%	2 days	Thu 12/03/26	Fri 13/03/26
2348	Delivery of all internal timber doors	0%	1 day	Thu 12/03/26	Thu 12/03/26
2349	Complete all 1st coat paining to walls and ceiling	0%	2 days	Thu 12/03/26	Fri 13/03/26
2350	Hang doors and hardware cut outs	0%	4 days	Fri 13/03/26	Tue 17/03/26
2351	Plasterboard defects	0%	1 day	Sat 14/03/26	Sat 14/03/26
2352	Finish coat ceiling	0%	2 days	Mon 16/03/26	Tue 17/03/26
2353	Services trades fit off ceiling	0%	3 days	Wed 18/03/26	Fri 20/03/26
2354	Joinery Site Mobilisation and Install	0%	3 days	Tue 24/03/26	Fri 27/03/26
2355	Measure and book install for all stone tops	0%	2 wks	Fri 27/03/26	Mon 13/04/26
2356	Install Bench tops	0%	1 day	Mon 13/04/26	Tue 14/04/26
2357	Measure and install all glass splash backs	0%	2 wks	Tue 14/04/26	Tue 28/04/26
2358	Install splashback	0%	1 day	Tue 28/04/26	Wed 29/04/26
2359	Floor prep	0%	3 days	Thu 26/03/26	Mon 30/03/26
2360	2nd Coat wall	0%	2 days	Mon 30/03/26	Wed 1/04/26
2361	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 1/04/26	Wed 8/04/26
2362	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 1/04/26	Wed 8/04/26
2363	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 1/04/26	Thu 9/04/26
2364	Complete timber floor	0%	3 days	Thu 9/04/26	Mon 13/04/26
2365	Complete and install all timber skirtings	0%	2 days	Fri 1/05/26	Tue 5/05/26
2366	Complete all final top coat painting	0%	3 days	Tue 28/04/26	Fri 1/05/26
2367	Final Clean	0%	1 day	Tue 5/05/26	Wed 6/05/26
2368	Complete all floor coverings - Carpet	0%	2 days	Wed 6/05/26	Fri 8/05/26
2369	**Bathroom**	**0%**	**27 days**	**Mon 2/03/26**	**Thu 9/04/26**
2370	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Mon 2/03/26	Wed 4/03/26
2371	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Thu 5/03/26	Wed 11/03/26
2372	Wet area floor and wall tiling	0%	6 days	Thu 12/03/26	Wed 18/03/26
2373	Measure all wet area shower screens (book install)	0%	10 days	Thu 19/03/26	Tue 31/03/26
2374	Initial clean	0%	1 day	Thu 19/03/26	Thu 19/03/26
2375	Fit off ceiling	0%	1 day	Fri 20/03/26	Fri 20/03/26
2376	PC item fit off	0%	3 days	Sat 21/03/26	Wed 25/03/26
2377	Shaving cabinets	0%	2 days	Thu 26/03/26	Fri 27/03/26
2378	Shower screens	0%	2 days	Wed 1/04/26	Thu 2/04/26
2379	FF&E Fit off	0%	2 days	Wed 8/04/26	Thu 9/04/26
2380	**Balcony & Façade**	**0%**	**19 days**	**Tue 24/02/26**	**Thu 19/03/26**
2381	Caulking to all external windows/ doors	0%	1 day	Tue 24/02/26	Tue 24/02/26
2382	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Wed 25/02/26	Tue 3/03/26
2383	Complete all external balcony balustrading	0%	4 days	Wed 4/03/26	Sat 7/03/26
2384	Complete all balcony water proofing	0%	3 days	Wed 11/03/26	Fri 13/03/26
2385	Complete all balcony tiling	0%	3 days	Sat 14/03/26	Tue 17/03/26
2386	Complete all external painting to the cladding	0%	2 days	Wed 18/03/26	Thu 19/03/26
2387	**Southern Apartments**	**0%**	**62.5 days**	**Mon 16/02/26**	**Tue 12/05/26**
2388	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 16/02/26	Tue 17/02/26
2389	1st Fix Hydraulic in-wall	0%	4 days	Wed 18/02/26	Sat 21/02/26
2390	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 16/02/26	Tue 17/02/26
2391	Nogging (Trimmers) install	0%	1 day	Sat 21/02/26	Sat 21/02/26
2392	Complete all presheeting ITP	0%	2 days	Tue 24/02/26	Wed 25/02/26
2393	Complete all internal wall sheeting, Ezy Jamb installation + flushing + J tack	0%	6 days	Thu 26/02/26	Wed 4/03/26
2394	Measure all bedroom robes (book install)	0%	0 days	Wed 4/03/26	Wed 4/03/26
2395	Complete all ceiling framing	0%	3 days	Thu 5/03/26	Sat 7/03/26
2396	Measure Kitchens and fabricate	0%	3.5 wks	Wed 11/03/26	Wed 1/04/26
2397	Complete all ceiling grid ITP's	0%	1 day	Wed 11/03/26	Wed 11/03/26
2398	Complete all ceiling sheeting + flushing	0%	4 days	Thu 12/03/26	Mon 16/03/26
2399	Flush corridor walls	0%	4 days	Thu 26/02/26	Mon 2/03/26
2400	All 2nd fix fire services cut outs	0%	2 days	Tue 17/03/26	Wed 18/03/26
2401	All 2nd fix mechanical services cut outs	0%	2 days	Tue 17/03/26	Wed 18/03/26
2402	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Tue 17/03/26	Wed 18/03/26
2403	All 2nd fix hydraulic services cut outs	0%	2 days	Tue 17/03/26	Wed 18/03/26
2404	Delivery of all internal timber doors	0%	1 day	Tue 17/03/26	Tue 17/03/26
2405	Complete all 1st coat paining to walls and ceiling	0%	2 days	Tue 17/03/26	Wed 18/03/26
2406	Hang doors and hardware cut outs	0%	4 days	Wed 18/03/26	Sat 21/03/26
2407	Plasterboard defects	0%	1 day	Thu 19/03/26	Thu 19/03/26
2408	Finish coat ceiling	0%	2 days	Fri 20/03/26	Sat 21/03/26
2409	Services trades fit off ceiling	0%	3 days	Tue 24/03/26	Thu 26/03/26
2410	Joinery Site Mobilisation and Install	0%	3 days	Wed 1/04/26	Thu 9/04/26
2411	Measure and book install for all stone tops	0%	2 wks	Thu 9/04/26	Tue 21/04/26
2412	Install Bench tops	0%	1 day	Tue 21/04/26	Wed 22/04/26
2413	Measure and install all glass splash backs	0%	2 wks	Wed 22/04/26	Thu 7/05/26

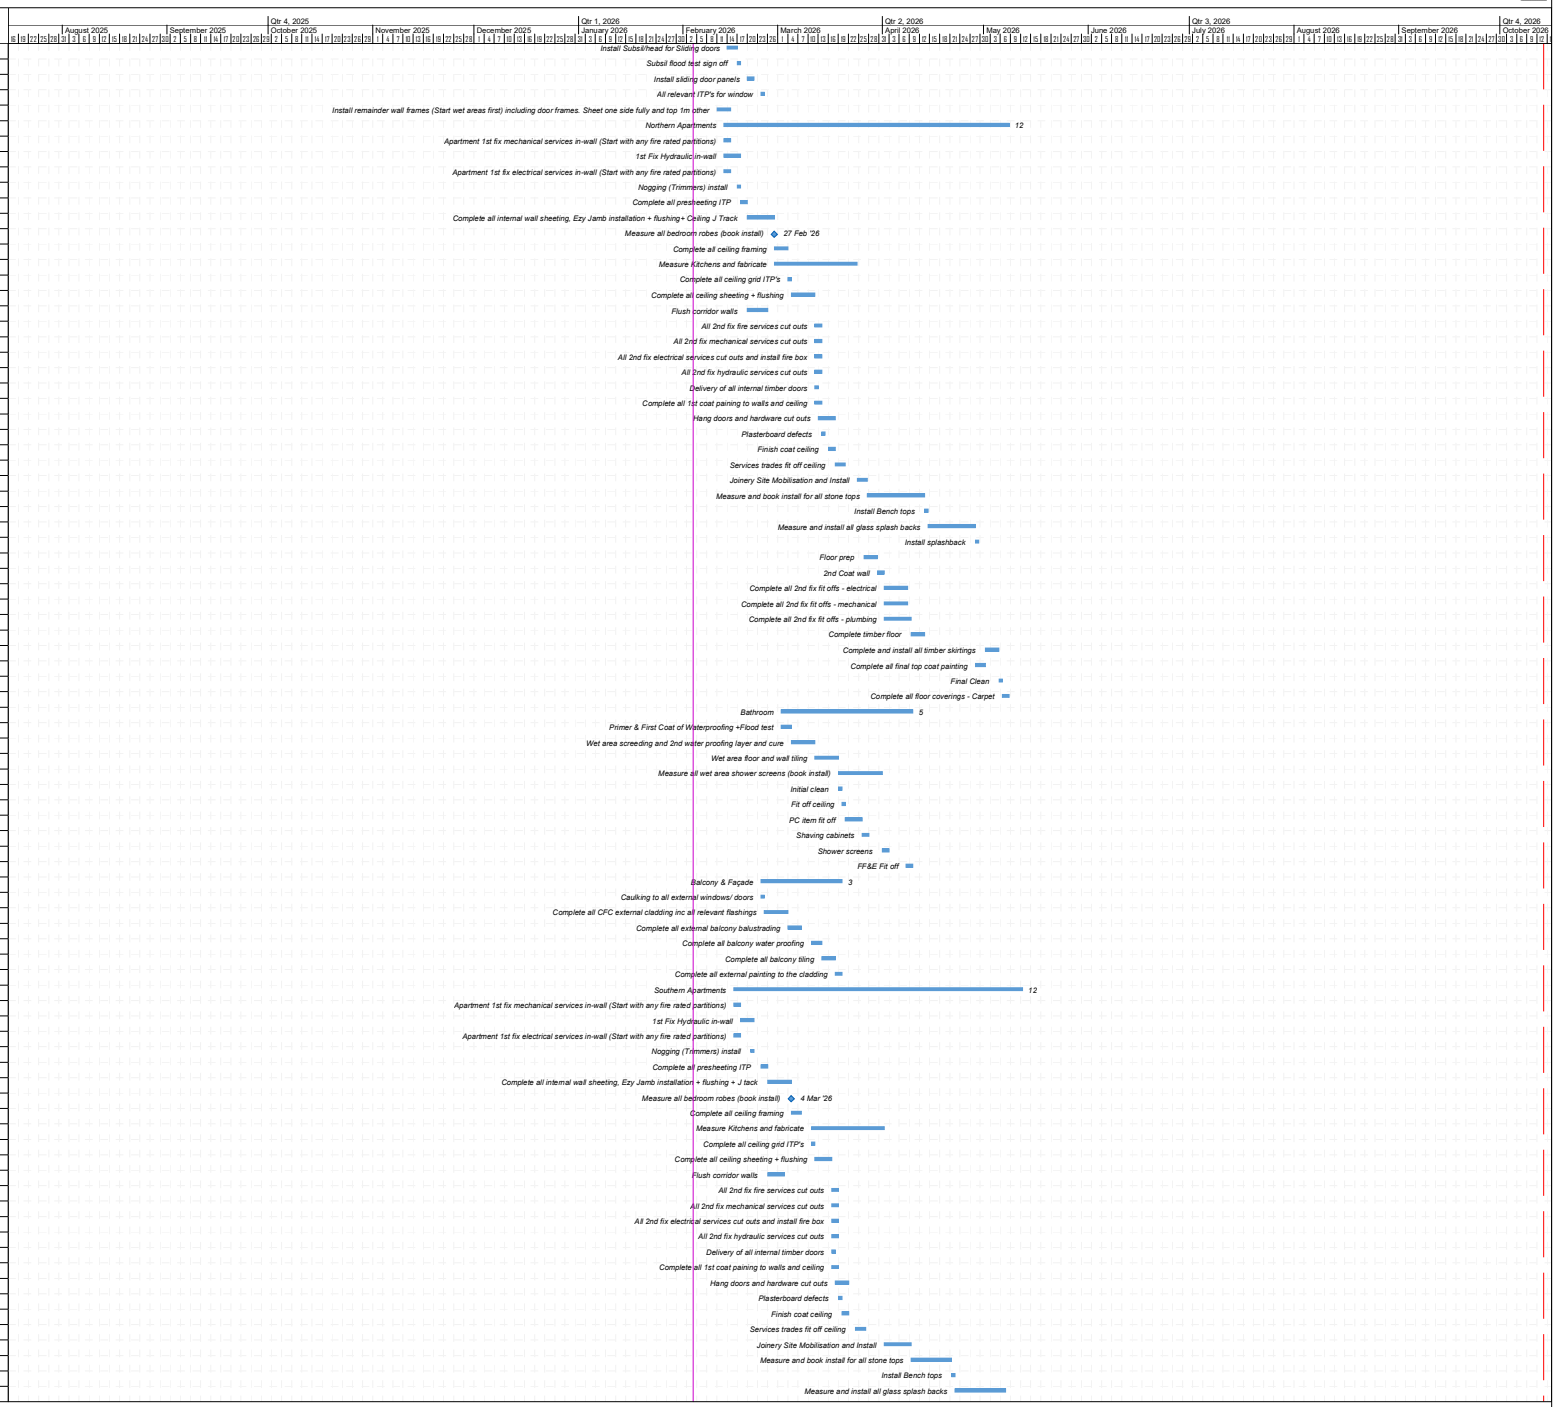

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
2414	Install splashback	0%	1 day	Thu 7/05/26	Fri 8/05/26
2415	Floor prep	0%	3 days	Wed 8/04/26	Sat 11/04/26
2416	2nd Coat wall	0%	2 days	Sat 11/04/26	Tue 14/04/26
2417	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 14/04/26	Thu 16/04/26
2418	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 14/04/26	Thu 16/04/26
2419	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 14/04/26	Fri 17/04/26
2420	Complete Timber Flooring	0%	3 days	Fri 17/04/26	Tue 21/04/26
2421	Complete and install all timber skirtings	0%	2 days	Fri 24/04/26	Wed 29/04/26
2422	Complete all final top coat painting	0%	3 days	Tue 21/04/26	Fri 24/04/26
2423	Final Clean	0%	1 day	Fri 8/05/26	Sat 9/05/26
2424	Complete all floor coverings - Carpet	0%	2 days	Sat 9/05/26	Tue 12/05/26
2425	**Bathroom**	**0%**	**27 days**	**Fri 6/03/26**	**Tue 14/04/26**
2426	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Fri 6/03/26	Wed 11/03/26
2427	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Thu 12/03/26	Mon 16/03/26
2428	Wet area floor and wall tiling	0%	6 days	Tue 17/03/26	Tue 24/03/26
2429	Measure all wet area shower screens (book install)	0%	2 wks	Wed 25/03/26	Thu 9/04/26
2430	Initial clean	0%	1 day	Wed 25/03/26	Wed 25/03/26
2431	Fit off ceiling	0%	1 day	Thu 26/03/26	Thu 26/03/26
2432	PC item fit off	0%	3 days	Fri 27/03/26	Mon 30/03/26
2433	Shaving cabinets	0%	2 days	Tue 31/03/26	Wed 1/04/26
2434	Shower screens	0%	2 days	Fri 10/04/26	Sat 11/04/26
2435	FF&E Fit off	0%	2 days	Mon 13/04/26	Tue 14/04/26
2436	**Balcony & Façade**	**0%**	**19 days**	**Tue 24/02/26**	**Thu 19/03/26**
2437	Caulking to all external windows/ doors	0%	1 day	Tue 24/02/26	Tue 24/02/26
2438	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Wed 25/02/26	Tue 3/03/26
2439	Complete all external balcony balustrading	0%	4 days	Wed 4/03/26	Sat 7/03/26
2440	Complete all balcony water proofing	0%	3 days	Wed 11/03/26	Fri 13/03/26
2441	Complete all balcony tiling	0%	3 days	Sat 14/03/26	Tue 17/03/26
2442	Complete all external painting to the cladding	0%	2 days	Wed 18/03/26	Thu 19/03/26
2443	**Common Area (Corridors)**	**0%**	**69.5 days**	**Tue 3/03/26**	**Thu 4/06/26**
2444	Prime walls	0%	1 day	Tue 3/03/26	Tue 3/03/26
2445	Ceiling framing	0%	2 days	Thu 9/04/26	Sat 11/04/26
2446	Services and Ceiling Closeout ITP	0%	1 day	Sat 11/04/26	Mon 13/04/26
2447	Sheet and Flush Ceiling	0%	4 days	Mon 13/04/26	Fri 17/04/26
2448	Cut out ceilign services	0%	1 day	Fri 17/04/26	Sat 18/04/26
2449	2nd Coat wall and Finish coat ceiling	0%	3 days	Sat 18/04/26	Wed 22/04/26
2450	Complete all 2nd fix fit offs - fire	0%	2 days	Wed 22/04/26	Fri 24/04/26
2451	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 22/04/26	Fri 24/04/26
2452	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 22/04/26	Fri 24/04/26
2453	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 22/04/26	Tue 28/04/26
2454	Complete all final top coat painting	0%	3 days	Tue 28/04/26	Fri 1/05/26
2455	Complete all floor coverings - Timber	0%	3 days	Fri 1/05/26	Wed 6/05/26
2456	Complete all floor coverings - Carpet	0%	2 days	Tue 12/05/26	Thu 14/05/26
2457	Complete and install all timber skirtings over floor coverings	0%	2 days	Thu 14/05/26	Sat 16/05/26
2458	**Inspection Activities**	**0%**	**15 days**	**Sat 16/05/26**	**Thu 4/06/26**
2459	Defect Inspection & Rectification	0%	4 days	Sat 16/05/26	Fri 22/05/26
2460	Testing and commissioning to all L4	0%	1 day	Fri 22/05/26	Sat 23/05/26
2461	Contingency	0%	10 days	Sat 23/05/26	Thu 4/06/26
2462	FITOUT LEVEL 6	0%	93.5 days	Thu 12/02/26	Thu 18/06/26
2463	**Overall Floor**	**0%**	**22 days**	**Thu 12/02/26**	**Thu 12/03/26**
2464	**High level services**	**0%**	**10 days**	**Thu 12/02/26**	**Tue 24/02/26**
2465	Bianco to clear slab (Acrow Props only)	0%	2 days	Thu 12/02/26	Fri 13/02/26
2466	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Sat 14/02/26	Tue 17/02/26
2467	Precast Caulking/ Grout complete	0%	0 days	Tue 17/02/26	Tue 17/02/26
2468	Delivery of stud works + Entry door frames	0%	0 days	Thu 12/02/26	Thu 12/02/26
2469	Set out Wall frames +install top track	0%	4 days	Sat 14/02/26	Wed 18/02/26
2470	Delivery of all windows	0%	0 days	Sat 14/02/26	Sat 14/02/26
2471	Apartment 1st fix fire services high level	0%	4 days	Sat 14/02/26	Wed 18/02/26
2472	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Tue 17/02/26	Fri 20/02/26
2473	Apartment 1st fix mechanical services high level	0%	4 days	Thu 19/02/26	Tue 24/02/26
2474	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Thu 19/02/26**	**Thu 12/03/26**
2475	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Thu 19/02/26	Sat 21/02/26
2476	Intello wrap install	0%	1 day	Tue 24/02/26	Tue 24/02/26
2477	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Tue 24/02/26	Thu 26/02/26
2478	Install F channel for Balustrade	0%	4 days	Fri 27/02/26	Tue 3/03/26
2479	Delivery of plasterboard	0%	0 days	Wed 25/02/26	Wed 25/02/26
2480	Delivery of Door frame ready on site	0%	0 days	Tue 24/02/26	Tue 24/02/26
2481	Install window subframes (start with precast)	0%	4 days	Fri 27/02/26	Tue 3/03/26
2482	Subframe flood test sign off	0%	1 day	Wed 4/03/26	Wed 4/03/26
2483	Install window panels	0%	2 days	Thu 5/03/26	Fri 6/03/26
2484	Install Subsill/head for Sliding doors	0%	2 days	Mon 2/03/26	Tue 3/03/26
2485	Subsil flood test sign off	0%	1 day	Wed 4/03/26	Wed 4/03/26
2486	Install sliding door panels	0%	2 days	Sat 7/03/26	Wed 11/03/26
2487	All relevant ITP's for window	0%	1 day	Thu 12/03/26	Thu 12/03/26
2488	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Tue 24/02/26	Fri 27/02/26
2489	**Northern Apartments**	**0%**	**61.5 days**	**Thu 26/02/26**	**Thu 21/05/26**
2490	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 26/02/26	Fri 27/02/26
2491	1st Fix Hydraulic in-wall	0%	4 days	Thu 26/02/26	Mon 2/03/26
2492	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 26/02/26	Fri 27/02/26
2493	Nogging (Trimmers) install	0%	1 day	Mon 2/03/26	Mon 2/03/26
2494	Complete all presheeting ITP	0%	2 days	Tue 3/03/26	Wed 4/03/26
2495	Complete all internal wall sheeting, Ezy Jamb installation + flushing+ Ceiling J Track	0%	6 days	Thu 5/03/26	Fri 13/03/26
2496	Measure all bedroom robes (book install)	0%	0 days	Fri 13/03/26	Fri 13/03/26
2497	Complete all ceiling framing	0%	3 days	Sat 14/03/26	Tue 17/03/26
2498	Measure Kitchens and fabricate	0%	3.5 wks	Sat 14/03/26	Thu 9/04/26
2499	Complete all ceiling grid ITP's	0%	1 day	Wed 18/03/26	Wed 18/03/26
2500	Complete all ceiling sheeting + flushing	0%	4 days	Thu 19/03/26	Tue 24/03/26
2501	Flush corridor walls	0%	4 days	Thu 5/03/26	Wed 11/03/26

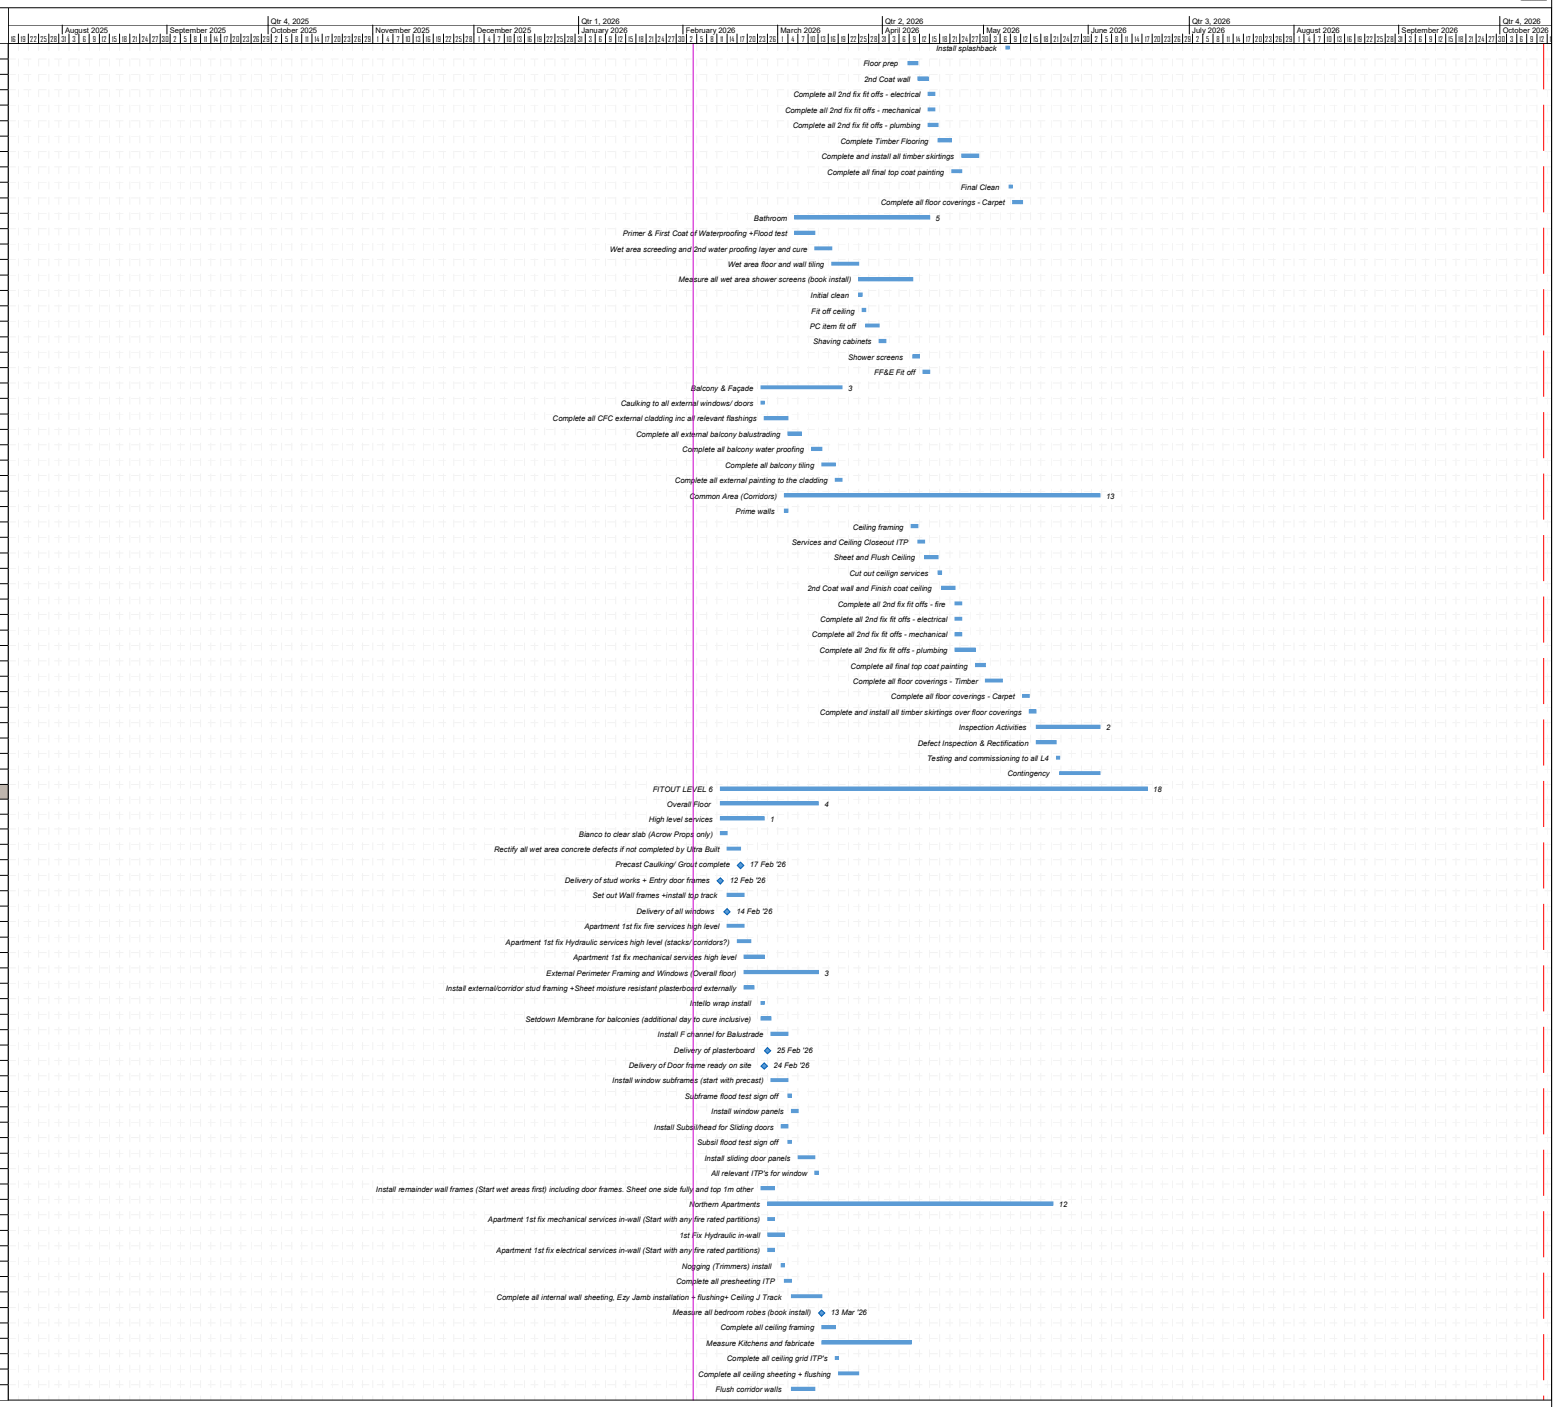

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2502	All 2nd fix fire services cut outs	0%	2 days	Wed 25/03/26	Thu 26/03/26
2503	All 2nd fix mechanical services cut outs	0%	2 days	Wed 25/03/26	Thu 26/03/26
2504	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Wed 25/03/26	Thu 26/03/26
2505	All 2nd fix hydraulic services cut outs	0%	2 days	Wed 25/03/26	Thu 26/03/26
2506	Delivery of all internal timber doors	0%	1 day	Wed 25/03/26	Wed 25/03/26
2507	Complete all 1st coat paining to walls and ceiling	0%	2 days	Wed 25/03/26	Thu 26/03/26
2508	Hang doors and hardware cut outs	0%	4 days	Thu 26/03/26	Mon 30/03/26
2509	Plasterboard defects	0%	1 day	Fri 27/03/26	Fri 27/03/26
2510	Finish coat ceiling	0%	2 days	Sat 28/03/26	Mon 30/03/26
2511	Services trades fit off ceiling	0%	3 days	Tue 31/03/26	Thu 2/04/26
2512	Joinery Site Mobilisation and Install	0%	3 days	Thu 9/04/26	Mon 13/04/26
2513	Measure and book install for all stone tops	0%	2 wks	Mon 13/04/26	Fri 24/04/26
2514	Install Bench tops	0%	1 day	Fri 24/04/26	Tue 28/04/26
2515	Measure and install all glass splash backs	0%	2 wks	Tue 28/04/26	Mon 11/05/26
2516	Install splashback	0%	1 day	Mon 11/05/26	Tue 12/05/26
2517	Floor prep	0%	3 days	Sat 11/04/26	Wed 15/04/26
2518	2nd Coat wall	0%	2 days	Wed 15/04/26	Fri 17/04/26
2519	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 17/04/26	Mon 20/04/26
2520	Complete all 2nd fix fit offs - mechanical	0%	2 days	Fri 17/04/26	Mon 20/04/26
2521	Complete all 2nd fix fit offs - plumbing	0%	3 days	Fri 17/04/26	Tue 21/04/26
2522	Complete timber floor	0%	3 days	Tue 21/04/26	Fri 24/04/26
2523	Complete and install all timber skirtings	0%	2 days	Thu 14/05/26	Sat 16/05/26
2524	Complete all final top coat painting	0%	3 days	Mon 11/05/26	Thu 14/05/26
2525	Final Clean	0%	1 day	Sat 16/05/26	Tue 19/05/26
2526	Complete all floor coverings - Carpet	0%	2 days	Tue 19/05/26	Thu 21/05/26
2527	**Bathroom**	**0%**	**27 days**	**Mon 16/03/26**	**Tue 21/04/26**
2528	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Mon 16/03/26	Wed 18/03/26
2529	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Thu 19/03/26	Tue 24/03/26
2530	Wet area floor and wall tiling	0%	6 days	Wed 25/03/26	Tue 31/03/26
2531	Measure all wet area shower screens (book install)	0%	10 days	Wed 1/04/26	Thu 16/04/26
2532	Initial clean	0%	1 day	Wed 1/04/26	Wed 1/04/26
2533	Fit off ceiling	0%	1 day	Thu 2/04/26	Thu 2/04/26
2534	PC item fit off	0%	3 days	Wed 8/04/26	Fri 10/04/26
2535	Shaving cabinets	0%	2 days	Sat 11/04/26	Mon 13/04/26
2536	Shower screens	0%	2 days	Fri 17/04/26	Sat 18/04/26
2537	FF&E Fit off	0%	2 days	Mon 20/04/26	Tue 21/04/26
2538	**Balcony & Façade**	**0%**	**19 days**	**Thu 12/03/26**	**Wed 8/04/26**
2539	Caulking to all external windows/ doors	0%	1 day	Thu 12/03/26	Thu 12/03/26
2540	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 13/03/26	Thu 19/03/26
2541	Complete all external balcony balustrading	0%	4 days	Fri 20/03/26	Wed 25/03/26
2542	Complete all balcony water proofing	0%	3 days	Thu 26/03/26	Sat 28/03/26
2543	Complete all balcony tiling	0%	3 days	Mon 30/03/26	Wed 1/04/26
2544	Complete all external painting to the cladding	0%	2 days	Thu 2/04/26	Wed 8/04/26
2545	**Southern Apartments**	**0%**	**61.5 days**	**Sat 28/02/26**	**Sat 23/05/26**
2546	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 28/02/26	Mon 2/03/26
2547	1st Fix Hydraulic in-wall	0%	4 days	Tue 3/03/26	Fri 6/03/26
2548	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 28/02/26	Mon 2/03/26
2549	Nogging (Trimmers) install	0%	1 day	Fri 6/03/26	Fri 6/03/26
2550	Complete all presheeting ITP	0%	2 days	Sat 7/03/26	Wed 11/03/26
2551	Complete all internal wall sheeting, Ezy Jamb installation + flushing + Ceiling J track	0%	6 days	Thu 12/03/26	Wed 18/03/26
2552	Measure all bedroom robes (book install)	0%	0 days	Wed 18/03/26	Wed 18/03/26
2553	Complete all ceiling framing	0%	3 days	Thu 19/03/26	Sat 21/03/26
2554	Measure Kitchens and fabricate	0%	3.5 wks	Thu 19/03/26	Tue 14/04/26
2555	Complete all ceiling grid ITP's	0%	1 day	Tue 24/03/26	Tue 24/03/26
2556	Complete all ceiling sheeting + flushing	0%	4 days	Wed 25/03/26	Sat 28/03/26
2557	Flush corridor walls	0%	4 days	Thu 12/03/26	Mon 16/03/26
2558	All 2nd fix fire services cut outs	0%	2 days	Mon 30/03/26	Tue 31/03/26
2559	All 2nd fix mechanical services cut outs	0%	2 days	Mon 30/03/26	Tue 31/03/26
2560	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Mon 30/03/26	Tue 31/03/26
2561	All 2nd fix hydraulic services cut outs	0%	2 days	Mon 30/03/26	Tue 31/03/26
2562	Delivery of all internal timber doors	0%	1 day	Mon 30/03/26	Mon 30/03/26
2563	Complete all 1st coat paining to walls and ceiling	0%	2 days	Mon 30/03/26	Tue 31/03/26
2564	Hang doors and hardware cut outs	0%	4 days	Tue 31/03/26	Wed 8/04/26
2565	Plasterboard defects	0%	1 day	Wed 1/04/26	Wed 1/04/26
2566	Finish coat ceiling	0%	2 days	Thu 2/04/26	Wed 8/04/26
2567	Services trades fit off ceiling	0%	3 days	Thu 9/04/26	Sat 11/04/26
2568	Joinery Site Mobilisation and Install	0%	3 days	Tue 14/04/26	Fri 17/04/26
2569	Measure and book install for all stone tops	0%	2 wks	Fri 17/04/26	Fri 1/05/26
2570	Install Bench tops	0%	1 day	Fri 1/05/26	Sat 2/05/26
2571	Measure and install all glass splash backs	0%	2 wks	Sat 2/05/26	Fri 15/05/26
2572	Install splashback	0%	1 day	Fri 15/05/26	Sat 16/05/26
2573	Floor prep	0%	3 days	Thu 16/04/26	Mon 20/04/26
2574	2nd Coat wall	0%	2 days	Mon 20/04/26	Wed 22/04/26
2575	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 22/04/26	Fri 24/04/26
2576	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 22/04/26	Fri 24/04/26
2577	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 22/04/26	Tue 28/04/26
2578	Complete Timber Flooring	0%	3 days	Tue 28/04/26	Fri 1/05/26
2579	Complete and install all timber skirtings	0%	2 days	Wed 6/05/26	Fri 8/05/26
2580	Complete all final top coat painting	0%	3 days	Fri 1/05/26	Wed 6/05/26
2581	Final Clean	0%	1 day	Sat 16/05/26	Tue 19/05/26
2582	Complete all floor coverings - Carpet	0%	2 days	Thu 21/05/26	Sat 23/05/26
2583	**Bathroom**	**0%**	**27 days**	**Fri 20/03/26**	**Tue 28/04/26**
2584	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Fri 20/03/26	Tue 24/03/26
2585	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Wed 25/03/26	Sat 28/03/26
2586	Wet area floor and wall tiling	0%	6 days	Mon 30/03/26	Thu 9/04/26
2587	Measure all wet area shower screens (book install)	0%	2 wks	Fri 10/04/26	Tue 21/04/26
2588	Initial clean	0%	1 day	Fri 10/04/26	Fri 10/04/26
2589	Fit off ceiling	0%	1 day	Sat 11/04/26	Sat 11/04/26

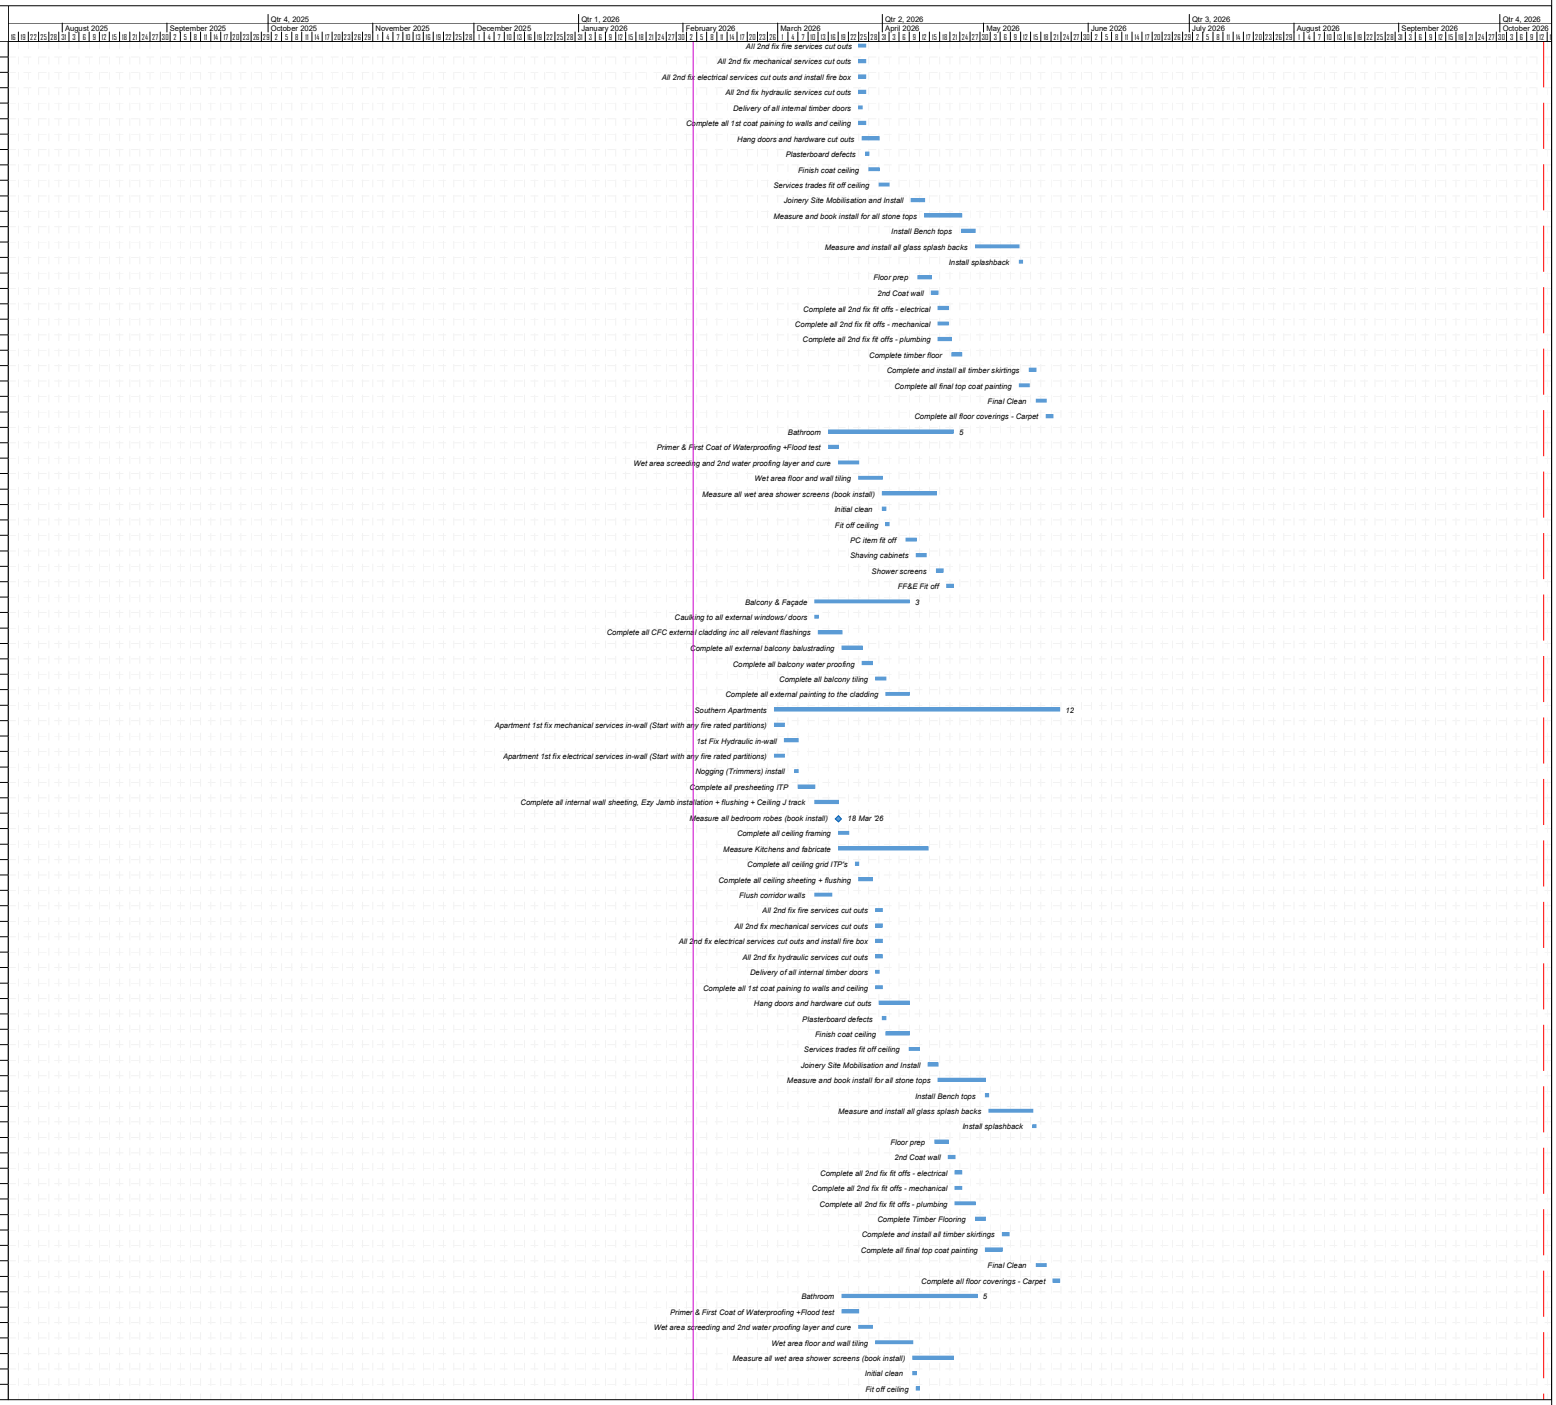

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2590	PC item fit off	0%	3 days	Mon 13/04/26	Wed 15/04/26
2591	Shaving cabinets	0%	2 days	Thu 16/04/26	Fri 17/04/26
2592	Shower screens	0%	2 days	Wed 22/04/26	Thu 23/04/26
2593	FF&E Fit off	0%	2 days	Fri 24/04/26	Tue 28/04/26
2594	**Balcony & Façade**	**0%**	**19 days**	**Thu 12/03/26**	**Wed 8/04/26**
2595	Caulking to all external windows/ doors	0%	1 day	Thu 12/03/26	Thu 12/03/26
2596	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 13/03/26	Thu 19/03/26
2597	Complete all external balcony balustrading	0%	4 days	Fri 20/03/26	Wed 25/03/26
2598	Complete all balcony water proofing	0%	3 days	Thu 26/03/26	Sat 28/03/26
2599	Complete all balcony tiling	0%	3 days	Mon 30/03/26	Wed 1/04/26
2600	Complete all external painting to the cladding	0%	2 days	Thu 2/04/26	Wed 8/04/26
2601	**Common Area (Corridors)**	**0%**	**68.5 days**	**Tue 17/03/26**	**Thu 18/06/26**
2602	Prime walls	0%	1 day	Tue 17/03/26	Tue 17/03/26
2603	Ceiling framing	0%	2 days	Fri 17/04/26	Mon 20/04/26
2604	Services and Ceiling Closeout ITP	0%	1 day	Mon 20/04/26	Tue 21/04/26
2605	Sheet and Flush Ceiling	0%	4 days	Tue 21/04/26	Tue 28/04/26
2606	Cut out ceilign services	0%	1 day	Tue 28/04/26	Wed 29/04/26
2607	2nd Coat wall and Finish coat ceiling	0%	3 days	Wed 29/04/26	Sat 2/05/26
2608	Complete all 2nd fix fit offs - fire	0%	2 days	Sat 2/05/26	Wed 6/05/26
2609	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 2/05/26	Wed 6/05/26
2610	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 2/05/26	Wed 6/05/26
2611	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 2/05/26	Thu 7/05/26
2612	Complete all final top coat painting	0%	3 days	Thu 7/05/26	Mon 11/05/26
2613	Complete all floor coverings - Timber	0%	3 days	Mon 11/05/26	Thu 14/05/26
2614	Complete all floor coverings - Carpet	0%	2 days	Sat 23/05/26	Tue 26/05/26
2615	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 26/05/26	Thu 28/05/26
2616	**Inspection Activities**	**0%**	**15 days**	**Thu 28/05/26**	**Thu 18/06/26**
2617	Defect Inspection & Rectification	0%	4 days	Thu 28/05/26	Tue 2/06/26
2618	Testing and commissioning to all L4	0%	1 day	Tue 2/06/26	Wed 3/06/26
2619	Contingency	0%	10 days	Wed 3/06/26	Thu 18/06/26
2620	FITOUT LEVEL 7	0%	92.5 days	Fri 27/02/26	Fri 3/07/26
2621	**Overall Floor**	**0%**	**22 days**	**Fri 27/02/26**	**Fri 27/03/26**
2622	**High level services**	**0%**	**12 days**	**Fri 27/02/26**	**Sat 14/03/26**
2623	Bianco to clear slab (Acrow Props only)	0%	2 days	Fri 27/02/26	Sat 28/02/26
2624	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Mon 2/03/26	Wed 4/03/26
2625	Precast Caulking/ Grout complete	0%	0 days	Wed 4/03/26	Wed 4/03/26
2626	Delivery of stud works + Entry door frames	0%	0 days	Wed 4/03/26	Wed 4/03/26
2627	Set out Wall frames + install top track	0%	4 days	Wed 4/03/26	Sat 7/03/26
2628	Delivery of all windows	0%	0 days	Sat 7/03/26	Sat 7/03/26
2629	Apartment 1st fix fire services high level	0%	4 days	Wed 4/03/26	Sat 7/03/26
2630	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Fri 6/03/26	Thu 12/03/26
2631	Apartment 1st fix mechanical services high level	0%	4 days	Wed 11/03/26	Sat 14/03/26
2632	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Fri 6/03/26**	**Fri 27/03/26**
2633	Install external/Corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Fri 6/03/26	Wed 11/03/26
2634	Intello wrap install	0%	1 day	Thu 12/03/26	Thu 12/03/26
2635	Seldown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Thu 12/03/26	Sat 14/03/26
2636	Install F channel for Balustrade	0%	4 days	Mon 16/03/26	Thu 19/03/26
2637	Delivery of plasterboard	0%	0 days	Fri 13/03/26	Fri 13/03/26
2638	Delivery of Door frame ready on site	0%	0 days	Thu 12/03/26	Thu 12/03/26
2639	Install window subframes (start with precast)	0%	4 days	Mon 16/03/26	Thu 19/03/26
2640	Subframe flood test sign off	0%	1 day	Fri 20/03/26	Fri 20/03/26
2641	Install window panels	0%	2 days	Sat 21/03/26	Tue 24/03/26
2642	Install Subsil/head for Sliding doors	0%	2 days	Wed 18/03/26	Thu 19/03/26
2643	Subsil flood test sign off	0%	1 day	Fri 20/03/26	Fri 20/03/26
2644	Install sliding door panels	0%	2 days	Wed 25/03/26	Thu 26/03/26
2645	All relevant ITP's for window	0%	1 day	Fri 27/03/26	Fri 27/03/26
2646	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Thu 12/03/26	Mon 16/03/26
2647	**Northern Apartments**	**0%**	**61.5 days**	**Sat 14/03/26**	**Thu 4/06/26**
2648	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 14/03/26	Mon 16/03/26
2649	1st Fix Hydraulic in-wall	0%	4 days	Sat 14/03/26	Wed 18/03/26
2650	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 14/03/26	Mon 16/03/26
2651	Nogging (Trimmers) install	0%	1 day	Wed 18/03/26	Wed 18/03/26
2652	Complete all presheeting ITP	0%	2 days	Thu 19/03/26	Fri 20/03/26
2653	Complete all internal wall sheeting, Ezy Jamb installation + flushing+ Ceiling J Track	0%	6 days	Sat 21/03/26	Sat 28/03/26
2654	Measure all bedroom robes (book install)	0%	0 days	Sat 28/03/26	Sat 28/03/26
2655	Complete all ceiling framing	0%	3 days	Mon 30/03/26	Wed 1/04/26
2656	Measure Kitchens and fabricate	0%	3.5 wks	Mon 30/03/26	Thu 23/04/26
2657	Complete all ceiling grid ITP's	0%	1 day	Thu 2/04/26	Thu 2/04/26
2658	Complete all ceiling sheeting + flushing	0%	4 days	Wed 8/04/26	Sat 11/04/26
2659	Flush corridor walls	0%	4 days	Sat 21/03/26	Thu 26/03/26
2660	All 2nd fix fire services cut outs	0%	2 days	Mon 13/04/26	Tue 14/04/26
2661	All 2nd fix mechanical services cut outs	0%	2 days	Mon 13/04/26	Tue 14/04/26
2662	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Mon 13/04/26	Tue 14/04/26
2663	All 2nd fix hydraulic services cut outs	0%	2 days	Mon 13/04/26	Tue 14/04/26
2664	Delivery of all internal timber doors	0%	1 day	Mon 13/04/26	Mon 13/04/26
2665	Complete all 1st coat paining to walls and ceiling	0%	2 days	Mon 13/04/26	Tue 14/04/26
2666	Hang doors and hardware cut outs	0%	4 days	Tue 14/04/26	Fri 17/04/26
2667	Plasterboard defects	0%	1 day	Wed 15/04/26	Wed 15/04/26
2668	Finish coat ceiling	0%	2 days	Thu 16/04/26	Fri 17/04/26
2669	Services trades fit off ceiling	0%	3 days	Sat 18/04/26	Tue 21/04/26
2670	Joinery Site Mobilisation and Install	0%	3 days	Thu 23/04/26	Wed 29/04/26
2671	Measure and book install for all stone tops	0%	2 wks	Wed 29/04/26	Tue 12/05/26
2672	Install Bench tops	0%	1 day	Tue 12/05/26	Wed 13/05/26
2673	Measure and install all glass splash backs	0%	2 wks	Wed 13/05/26	Tue 26/05/26
2674	Install splashback	0%	1 day	Tue 26/05/26	Wed 27/05/26
2675	Floor prep	0%	3 days	Tue 28/04/26	Fri 1/05/26
2676	2nd Coat wall	0%	2 days	Fri 1/05/26	Tue 5/05/26
2677	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 5/05/26	Thu 7/05/26

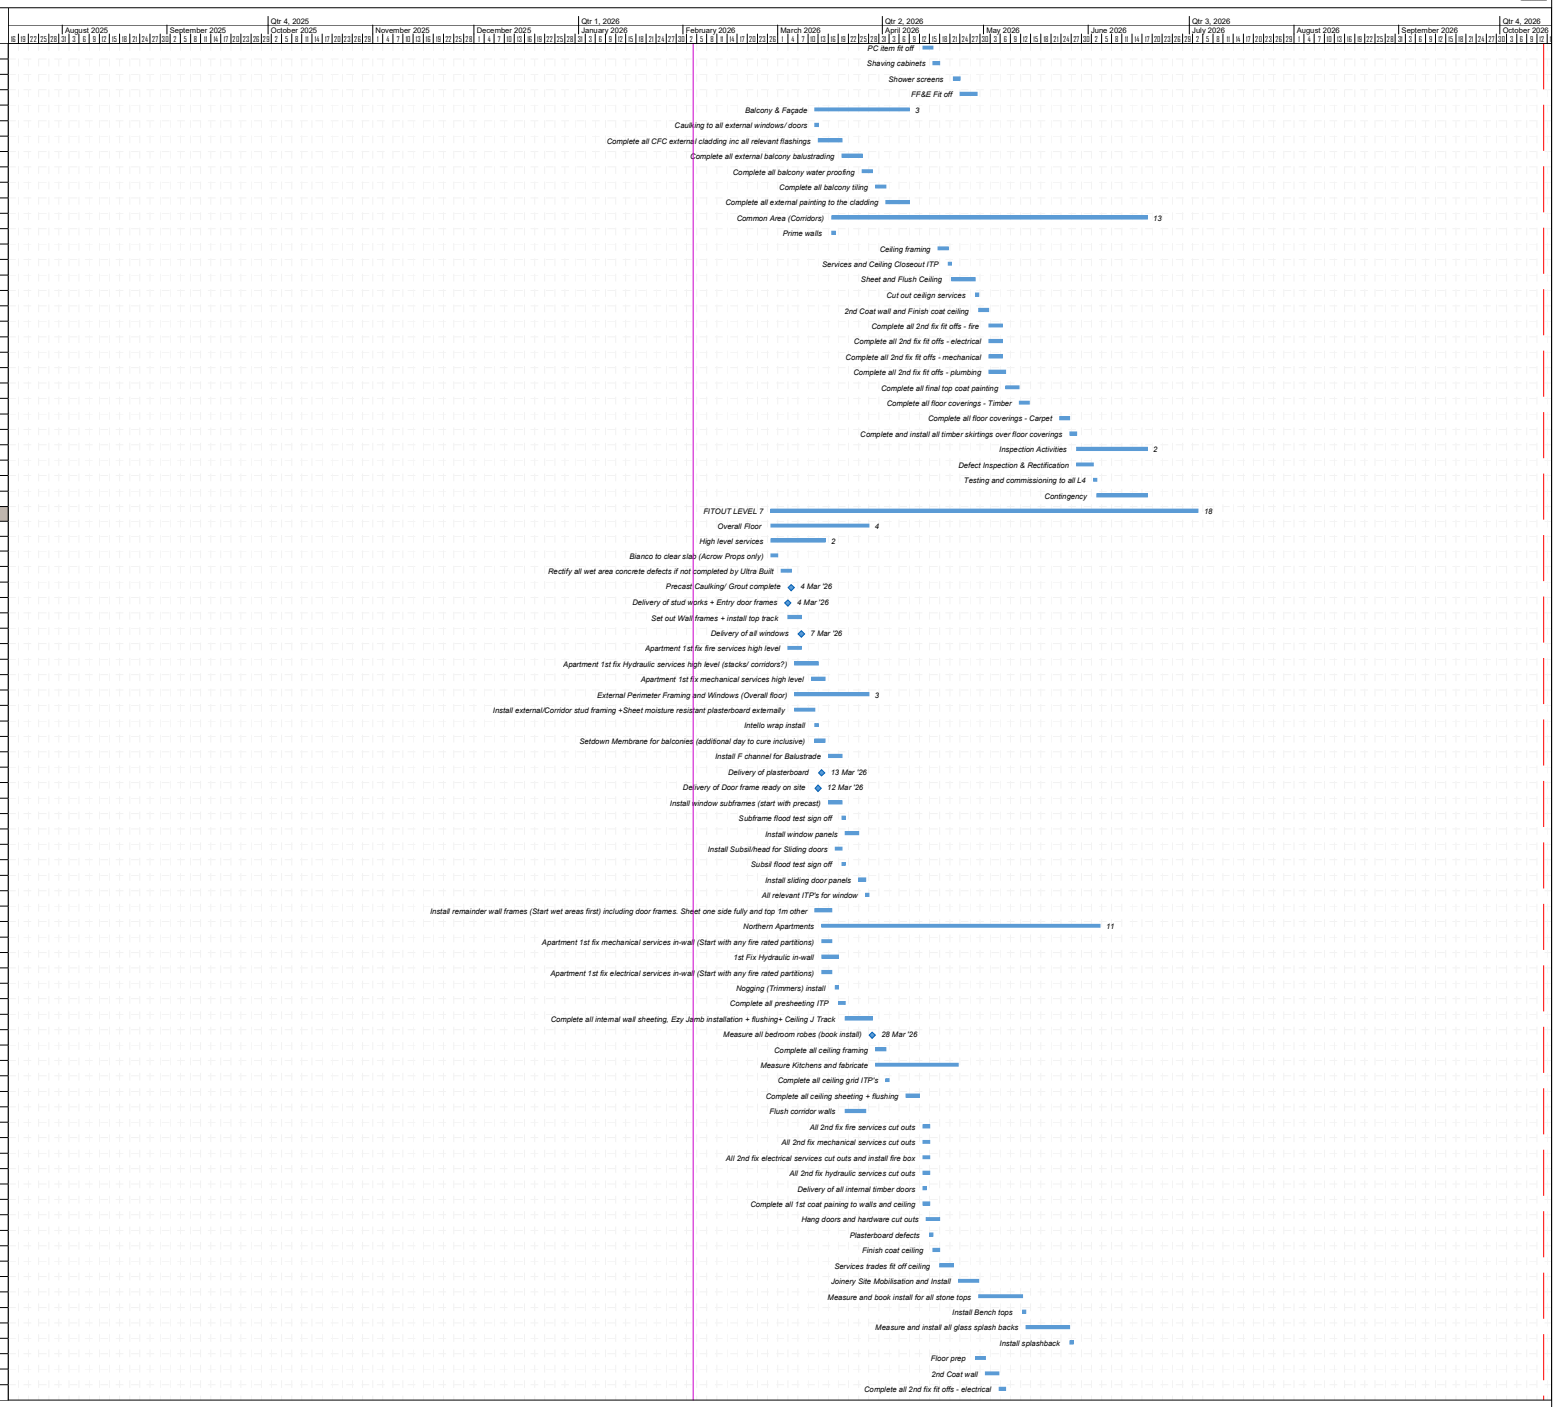

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
2678	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 5/05/26	Thu 7/05/26
2679	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 5/05/26	Fri 8/05/26
2680	Complete timber floor	0%	3 days	Fri 8/05/26	Tue 12/05/26
2681	Complete and install all timber skirtings	0%	2 days	Fri 29/05/26	Mon 1/06/26
2682	Complete all final top coat painting	0%	3 days	Tue 26/05/26	Fri 29/05/26
2683	Final Clean	0%	1 day	Mon 1/06/26	Tue 2/06/26
2684	Complete all floor coverings - Carpet	0%	2 days	Tue 2/06/26	Thu 4/06/26
2685	**Bathroom**	**0%**	**27 days**	**Tue 31/03/26**	**Fri 8/05/26**
2686	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Tue 31/03/26	Thu 2/04/26
2687	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Wed 8/04/26	Sat 11/04/26
2688	Wet area floor and wall tiling	0%	6 days	Mon 13/04/26	Sat 18/04/26
2689	Measure all wet area shower screens (book install)	0%	10 days	Mon 20/04/26	Sat 2/05/26
2690	Initial clean	0%	1 day	Mon 20/04/26	Mon 20/04/26
2691	Fit off ceiling	0%	1 day	Tue 21/04/26	Tue 21/04/26
2692	PC item fit off	0%	3 days	Wed 22/04/26	Fri 24/04/26
2693	Shaving cabinets	0%	2 days	Tue 28/04/26	Wed 29/04/26
2694	Shower screens	0%	2 days	Tue 5/05/26	Wed 6/05/26
2695	FF&E Fit off	0%	2 days	Thu 7/05/26	Fri 8/05/26
2696	**Balcony & Façade**	**0%**	**19 days**	**Fri 27/03/26**	**Wed 22/04/26**
2697	Caulking to all external windows/ doors	0%	1 day	Fri 27/03/26	Fri 27/03/26
2698	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Sat 28/03/26	Wed 8/04/26
2699	Complete all external balcony balustrading	0%	4 days	Thu 9/04/26	Mon 13/04/26
2700	Complete all balcony water proofing	0%	3 days	Tue 14/04/26	Thu 16/04/26
2701	Complete all balcony tiling	0%	3 days	Fri 17/04/26	Mon 20/04/26
2702	Complete all external painting to the cladding	0%	2 days	Tue 21/04/26	Wed 22/04/26
2703	**Southern Apartments**	**0%**	**61.5 days**	**Tue 17/03/26**	**Wed 10/06/26**
2704	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 17/03/26	Wed 18/03/26
2705	1st Fix Hydraulic in-wall	0%	4 days	Thu 19/03/26	Tue 24/03/26
2706	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 17/03/26	Wed 18/03/26
2707	Nogging (Trimmers) install	0%	1 day	Tue 24/03/26	Tue 24/03/26
2708	Complete all presheeting ITP	0%	2 days	Wed 25/03/26	Thu 26/03/26
2709	Complete all internal wall sheeting, Ezy Jamb installation + flushing + j track	0%	6 days	Fri 27/03/26	Thu 2/04/26
2710	Measure all bedroom robes (book install)	0%	0 days	Thu 2/04/26	Thu 2/04/26
2711	Complete all ceiling framing	0%	3 days	Wed 8/04/26	Fri 10/04/26
2712	Measure Kitchens and fabricate	0%	3.5 wks	Wed 8/04/26	Thu 30/04/26
2713	Complete all ceiling grid ITP's	0%	1 day	Sat 11/04/26	Sat 11/04/26
2714	Complete all ceiling sheeting + flushing	0%	4 days	Mon 13/04/26	Thu 16/04/26
2715	Flush corridor walls	0%	4 days	Fri 27/03/26	Tue 31/03/26
2716	All 2nd fix fire services cut outs	0%	2 days	Fri 17/04/26	Sat 18/04/26
2717	All 2nd fix mechanical services cut outs	0%	2 days	Fri 17/04/26	Sat 18/04/26
2718	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Fri 17/04/26	Sat 18/04/26
2719	All 2nd fix hydraulic services cut outs	0%	2 days	Fri 17/04/26	Sat 18/04/26
2720	Delivery of all internal timber doors	0%	1 day	Fri 17/04/26	Fri 17/04/26
2721	Complete all 1st coat paining to walls and ceiling	0%	2 days	Fri 17/04/26	Sat 18/04/26
2722	Hang doors and hardware cut outs	0%	4 days	Sat 18/04/26	Wed 22/04/26
2723	Plasterboard defects	0%	1 day	Mon 20/04/26	Mon 20/04/26
2724	Finish coat ceiling	0%	2 days	Tue 21/04/26	Wed 22/04/26
2725	Services trades fit off ceiling	0%	3 days	Thu 23/04/26	Tue 28/04/26
2726	Joinery Site Mobilisation and Install	0%	3 days	Thu 30/04/26	Tue 5/05/26
2727	Measure and book install for all stone tops	0%	2 wks	Tue 5/05/26	Sat 16/05/26
2728	Install Bench tops	0%	1 day	Sat 16/05/26	Tue 19/05/26
2729	Measure and install all glass splash backs	0%	2 wks	Tue 19/05/26	Sat 30/05/26
2730	Install splashback	0%	1 day	Sat 30/05/26	Mon 1/06/26
2731	Floor prep	0%	3 days	Sat 2/05/26	Thu 7/05/26
2732	2nd Coat wall	0%	2 days	Thu 7/05/26	Sat 9/05/26
2733	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 9/05/26	Tue 12/05/26
2734	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 9/05/26	Tue 12/05/26
2735	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 9/05/26	Wed 13/05/26
2736	Complete Timber Flooring	0%	3 days	Wed 13/05/26	Sat 16/05/26
2737	Complete and install all timber skirtings	0%	2 days	Thu 21/05/26	Sat 23/05/26
2738	Complete all final top coat painting	0%	3 days	Sat 16/05/26	Thu 21/05/26
2739	Final Clean	0%	1 day	Mon 1/06/26	Tue 2/06/26
2740	Complete all floor coverings - Carpet	0%	2 days	Thu 4/06/26	Wed 10/06/26
2741	**Bathroom**	**0%**	**27 days**	**Thu 9/04/26**	**Wed 13/05/26**
2742	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Thu 9/04/26	Sat 11/04/26
2743	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Mon 13/04/26	Thu 16/04/26
2744	Wet area floor and wall tiling	0%	6 days	Fri 17/04/26	Thu 23/04/26
2745	Measure all wet area shower screens (book install)	0%	2 wks	Fri 24/04/26	Fri 8/05/26
2746	Initial clean	0%	1 day	Fri 24/04/26	Fri 24/04/26
2747	Fit off ceiling	0%	1 day	Tue 28/04/26	Tue 28/04/26
2748	PC item fit off	0%	3 days	Wed 29/04/26	Fri 1/05/26
2749	Shaving cabinets	0%	2 days	Sat 2/05/26	Tue 5/05/26
2750	Shower screens	0%	2 days	Sat 9/05/26	Mon 11/05/26
2751	FF&E Fit off	0%	2 days	Tue 12/05/26	Wed 13/05/26
2752	**Balcony & Façade**	**0%**	**19 days**	**Fri 27/03/26**	**Wed 22/04/26**
2753	Caulking to all external windows/ doors	0%	1 day	Fri 27/03/26	Fri 27/03/26
2754	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Sat 28/03/26	Wed 8/04/26
2755	Complete all external balcony balustrading	0%	4 days	Thu 9/04/26	Mon 13/04/26
2756	Complete all balcony water proofing	0%	3 days	Tue 14/04/26	Thu 16/04/26
2757	Complete all balcony tiling	0%	3 days	Fri 17/04/26	Mon 20/04/26
2758	Complete all external painting to the cladding	0%	2 days	Tue 21/04/26	Wed 22/04/26
2759	**Common Area (Corridors)**	**0%**	**68.5 days**	**Wed 1/04/26**	**Fri 3/07/26**
2760	Prime walls	0%	1 day	Wed 1/04/26	Wed 1/04/26
2761	Ceiling framing	0%	2 days	Tue 5/05/26	Thu 7/05/26
2762	Services and Ceiling Closeout ITP	0%	1 day	Thu 7/05/26	Fri 8/05/26
2763	Sheet and Flush Ceiling	0%	4 days	Fri 8/05/26	Wed 13/05/26
2764	Cut out ceilign services	0%	1 day	Wed 13/05/26	Thu 14/05/26
2765	2nd Coat wall and Finish coat ceiling	0%	3 days	Thu 14/05/26	Tue 19/05/26

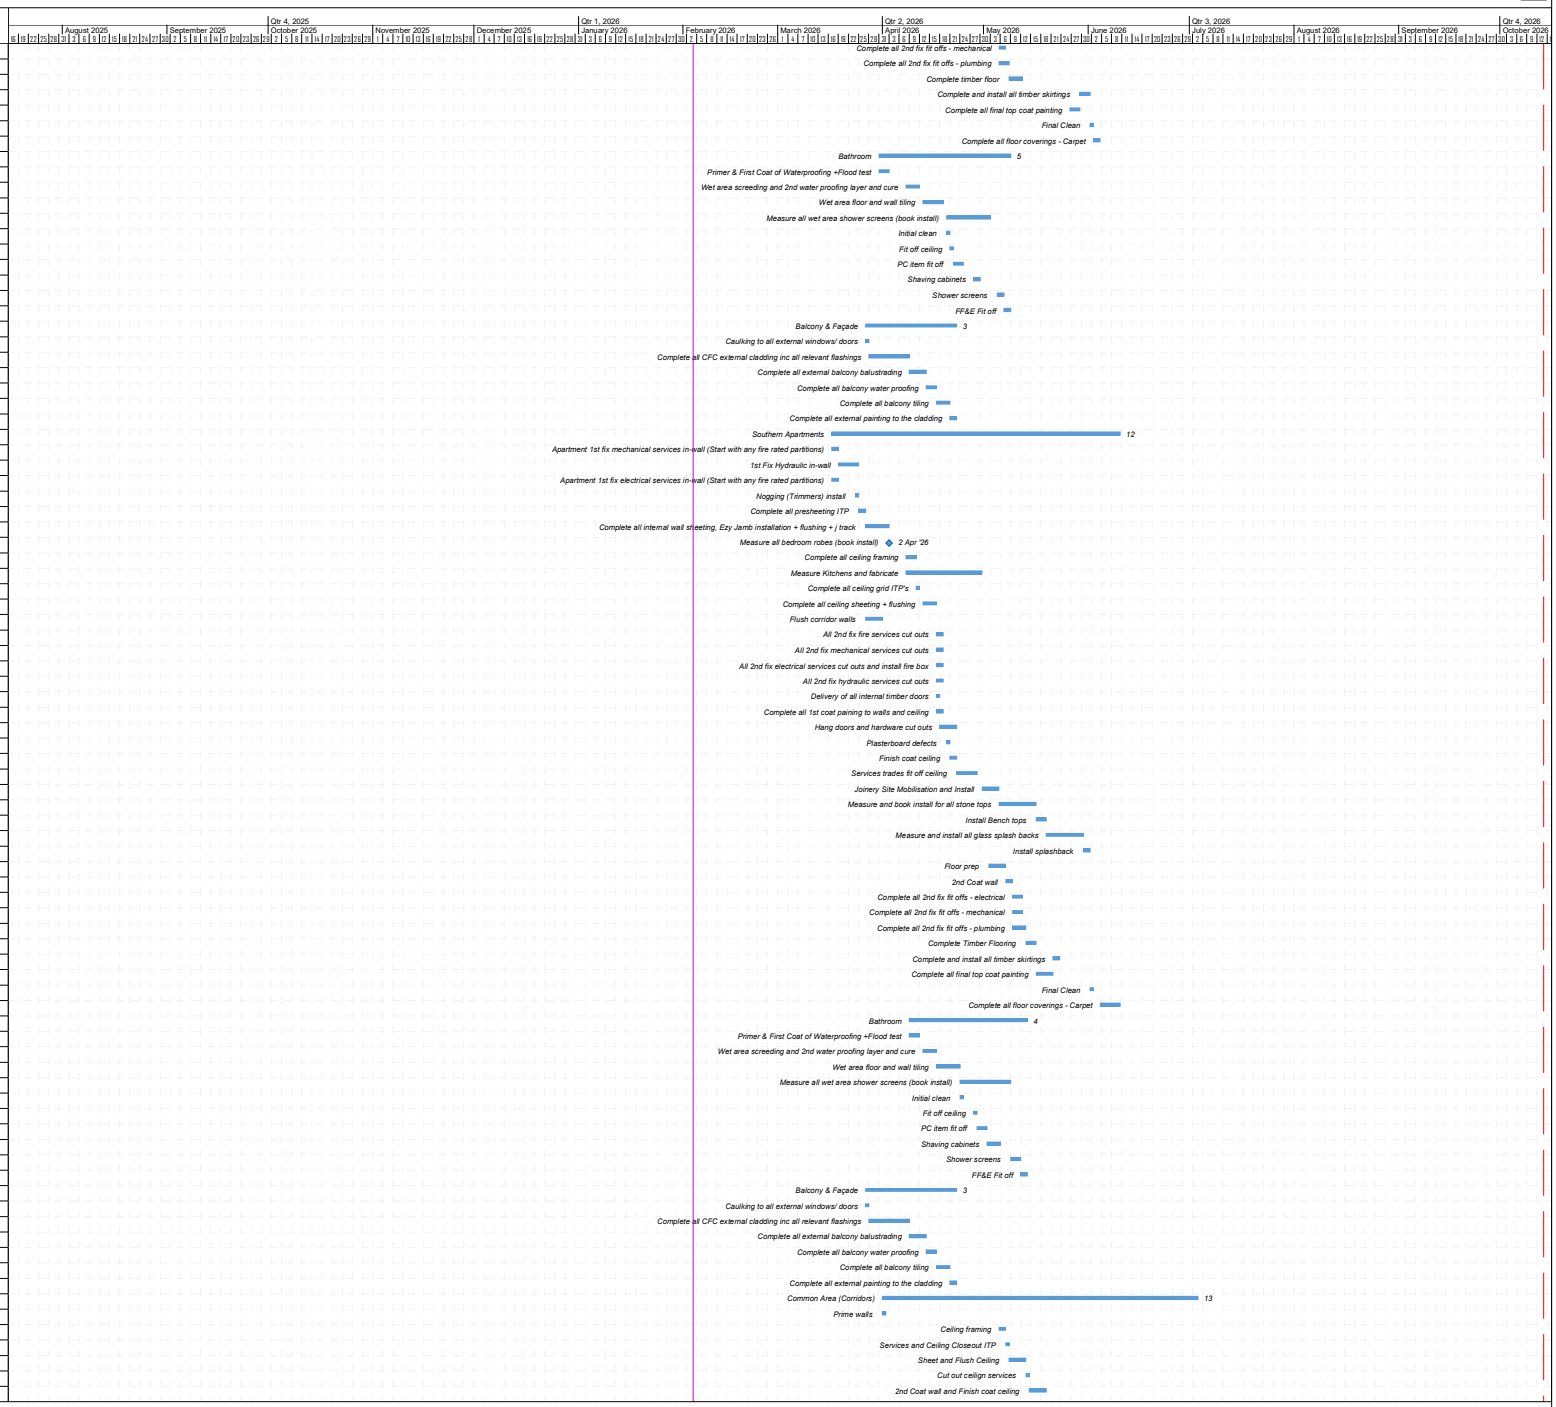

ID	Name	% Complete	Duration	Start	Finish
2766	Complete all 2nd fix fit offs - fire	0%	2 days	Tue 19/05/26	Thu 21/05/26
2767	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 19/05/26	Thu 21/05/26
2768	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 19/05/26	Thu 21/05/26
2769	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 19/05/26	Fri 22/05/26
2770	Complete all final top coat painting	0%	3 days	Fri 22/05/26	Tue 26/05/26
2771	Complete all floor coverings - Timber	0%	3 days	Tue 26/05/26	Fri 29/05/26
2772	Complete all floor coverings - Carpet	0%	2 days	Wed 10/06/26	Fri 12/06/26
2773	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 12/06/26	Mon 15/06/26
2774	**Inspection Activities**	**0%**	**15 days**	**Mon 15/06/26**	**Fri 3/07/26**
2775	Defect Inspection & Rectification	0%	4 days	Mon 15/06/26	Fri 19/06/26
2776	Testing and commissioning to all L4	0%	1 day	Fri 19/06/26	Sat 20/06/26
2777	Contingency	0%	10 days	Sat 20/06/26	Fri 3/07/26
2778	FITOUT LEVEL 8	0%	92.5 days	Mon 16/03/26	Sat 18/07/26
2779	**Overall Floor**	**0%**	**22 days**	**Mon 16/03/26**	**Wed 15/04/26**
2780	**High level services**	**0%**	**12 days**	**Mon 16/03/26**	**Mon 30/03/26**
2781	Bianco to clear slab (Acrow Props only)	0%	2 days	Mon 16/03/26	Tue 17/03/26
2782	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Wed 18/03/26	Fri 20/03/26
2783	Precast Caulking/ Grout complete	0%	0 days	Fri 20/03/26	Fri 20/03/26
2784	Delivery of stud works + Entry door frames	0%	0 days	Wed 18/03/26	Wed 18/03/26
2785	Set out Wall frames + install top track	0%	4 days	Fri 20/03/26	Wed 25/03/26
2786	Delivery of all windows	0%	0 days	Fri 20/03/26	Fri 20/03/26
2787	Apartment 1st fix fire services high level	0%	4 days	Fri 20/03/26	Wed 25/03/26
2788	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Tue 24/03/26	Fri 27/03/26
2789	Apartment 1st fix mechanical services high level	0%	4 days	Thu 26/03/26	Mon 30/03/26
2790	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Tue 24/03/26**	**Wed 15/04/26**
2791	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Tue 24/03/26	Thu 26/03/26
2792	Intello wrap install	0%	1 day	Fri 27/03/26	Fri 27/03/26
2793	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Fri 27/03/26	Mon 30/03/26
2794	Install F channel for Balustrade	0%	4 days	Tue 31/03/26	Wed 8/04/26
2795	Delivery of plasterboard	0%	0 days	Sat 28/03/26	Sat 28/03/26
2796	Delivery of Door frame ready on site	0%	0 days	Fri 27/03/26	Fri 27/03/26
2797	Install window subframes (start with precast)	0%	4 days	Tue 31/03/26	Wed 8/04/26
2798	Subframe flood test sign off	0%	1 day	Thu 9/04/26	Thu 9/04/26
2799	Install window panels	0%	2 days	Fri 10/04/26	Sat 11/04/26
2800	Install Subsil/head for Sliding doors	0%	2 days	Thu 2/04/26	Wed 8/04/26
2801	Subsil flood test sign off	0%	1 day	Thu 9/04/26	Thu 9/04/26
2802	Install sliding door panels	0%	2 days	Mon 13/04/26	Tue 14/04/26
2803	All relevant ITP's for window	0%	1 day	Wed 15/04/26	Wed 15/04/26
2804	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Fri 27/03/26	Tue 31/03/26
2805	**Northern Apartments**	**0%**	**61.5 days**	**Mon 30/03/26**	**Mon 22/06/26**
2806	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 30/03/26	Tue 31/03/26
2807	1st Fix Hydraulic in-wall	0%	4 days	Mon 30/03/26	Thu 2/04/26
2808	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 30/03/26	Tue 31/03/26
2809	Nogging (Trimmers) install	0%	1 day	Thu 2/04/26	Thu 2/04/26
2810	Complete all presheeting ITP	0%	2 days	Wed 8/04/26	Thu 9/04/26
2811	Complete all internal wall sheeting, Ezy Jamb installation + flushing + Ceiling J track	0%	6 days	Fri 10/04/26	Thu 16/04/26
2812	Measure all bedroom robes (book install)	0%	0 days	Thu 16/04/26	Thu 16/04/26
2813	Complete all ceiling framing	0%	3 days	Fri 17/04/26	Mon 20/04/26
2814	Measure Kitchens and fabricate	0%	3.5 wks	Fri 17/04/26	Mon 11/05/26
2815	Complete all ceiling grid ITP's	0%	1 day	Tue 21/04/26	Tue 21/04/26
2816	Complete all ceiling sheeting + flushing	0%	4 days	Wed 22/04/26	Tue 28/04/26
2817	Flush corridor walls	0%	4 days	Fri 10/04/26	Tue 14/04/26
2818	All 2nd fix fire services cut outs	0%	2 days	Wed 29/04/26	Thu 30/04/26
2819	All 2nd fix mechanical services cut outs	0%	2 days	Wed 29/04/26	Thu 30/04/26
2820	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Wed 29/04/26	Thu 30/04/26
2821	All 2nd fix hydraulic services cut outs	0%	2 days	Wed 29/04/26	Thu 30/04/26
2822	Delivery of all internal timber doors	0%	1 day	Wed 29/04/26	Wed 29/04/26
2823	Complete all 1st coat paining to walls and ceiling	0%	2 days	Wed 29/04/26	Thu 30/04/26
2824	Hang doors and hardware cut outs	0%	4 days	Thu 30/04/26	Tue 5/05/26
2825	Plasterboard defects	0%	1 day	Fri 1/05/26	Fri 1/05/26
2826	Finish coat ceiling	0%	2 days	Sat 2/05/26	Tue 5/05/26
2827	Services trades fit off ceiling	0%	3 days	Wed 6/05/26	Fri 8/05/26
2828	Joinery Site Mobilisation and Install	0%	3 days	Mon 11/05/26	Thu 14/05/26
2829	Measure and book install for all stone tops	0%	2 wks	Thu 14/05/26	Wed 27/05/26
2830	Install Bench tops	0%	1 day	Wed 27/05/26	Thu 28/05/26
2831	Measure and install all glass splash backs	0%	2 wks	Thu 28/05/26	Fri 12/06/26
2832	Install splashback	0%	1 day	Fri 12/06/26	Sat 13/06/26
2833	Floor prep	0%	3 days	Wed 13/05/26	Sat 16/05/26
2834	2nd Coat wall	0%	2 days	Sat 16/05/26	Wed 20/05/26
2835	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 20/05/26	Fri 22/05/26
2836	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 20/05/26	Fri 22/05/26
2837	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 20/05/26	Sat 23/05/26
2838	Complete timber floor	0%	3 days	Sat 23/05/26	Wed 27/05/26
2839	Complete and install all timber skirtings	0%	2 days	Tue 16/06/26	Thu 18/06/26
2840	Complete all final top coat painting	0%	3 days	Fri 12/06/26	Tue 16/06/26
2841	Final Clean	0%	1 day	Thu 18/06/26	Fri 19/06/26
2842	Complete all floor coverings - Carpet	0%	2 days	Fri 19/06/26	Mon 22/06/26
2843	**Bathroom**	**0%**	**27 days**	**Sat 18/04/26**	**Sat 23/05/26**
2844	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Sat 18/04/26	Tue 21/04/26
2845	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Wed 22/04/26	Tue 28/04/26
2846	Wet area floor and wall tiling	0%	6 days	Wed 29/04/26	Wed 6/05/26
2847	Measure all wet area shower screens (book install)	0%	10 days	Thu 7/05/26	Tue 19/05/26
2848	Initial clean	0%	1 day	Thu 7/05/26	Thu 7/05/26
2849	Fit off ceiling	0%	1 day	Fri 8/05/26	Fri 8/05/26
2850	PC item fit off	0%	3 days	Sat 9/05/26	Tue 12/05/26
2851	Shaving cabinets	0%	2 days	Wed 13/05/26	Thu 14/05/26
2852	Shower screens	0%	2 days	Wed 20/05/26	Thu 21/05/26
2853	FF&E Fit off	0%	2 days	Fri 22/05/26	Sat 23/05/26

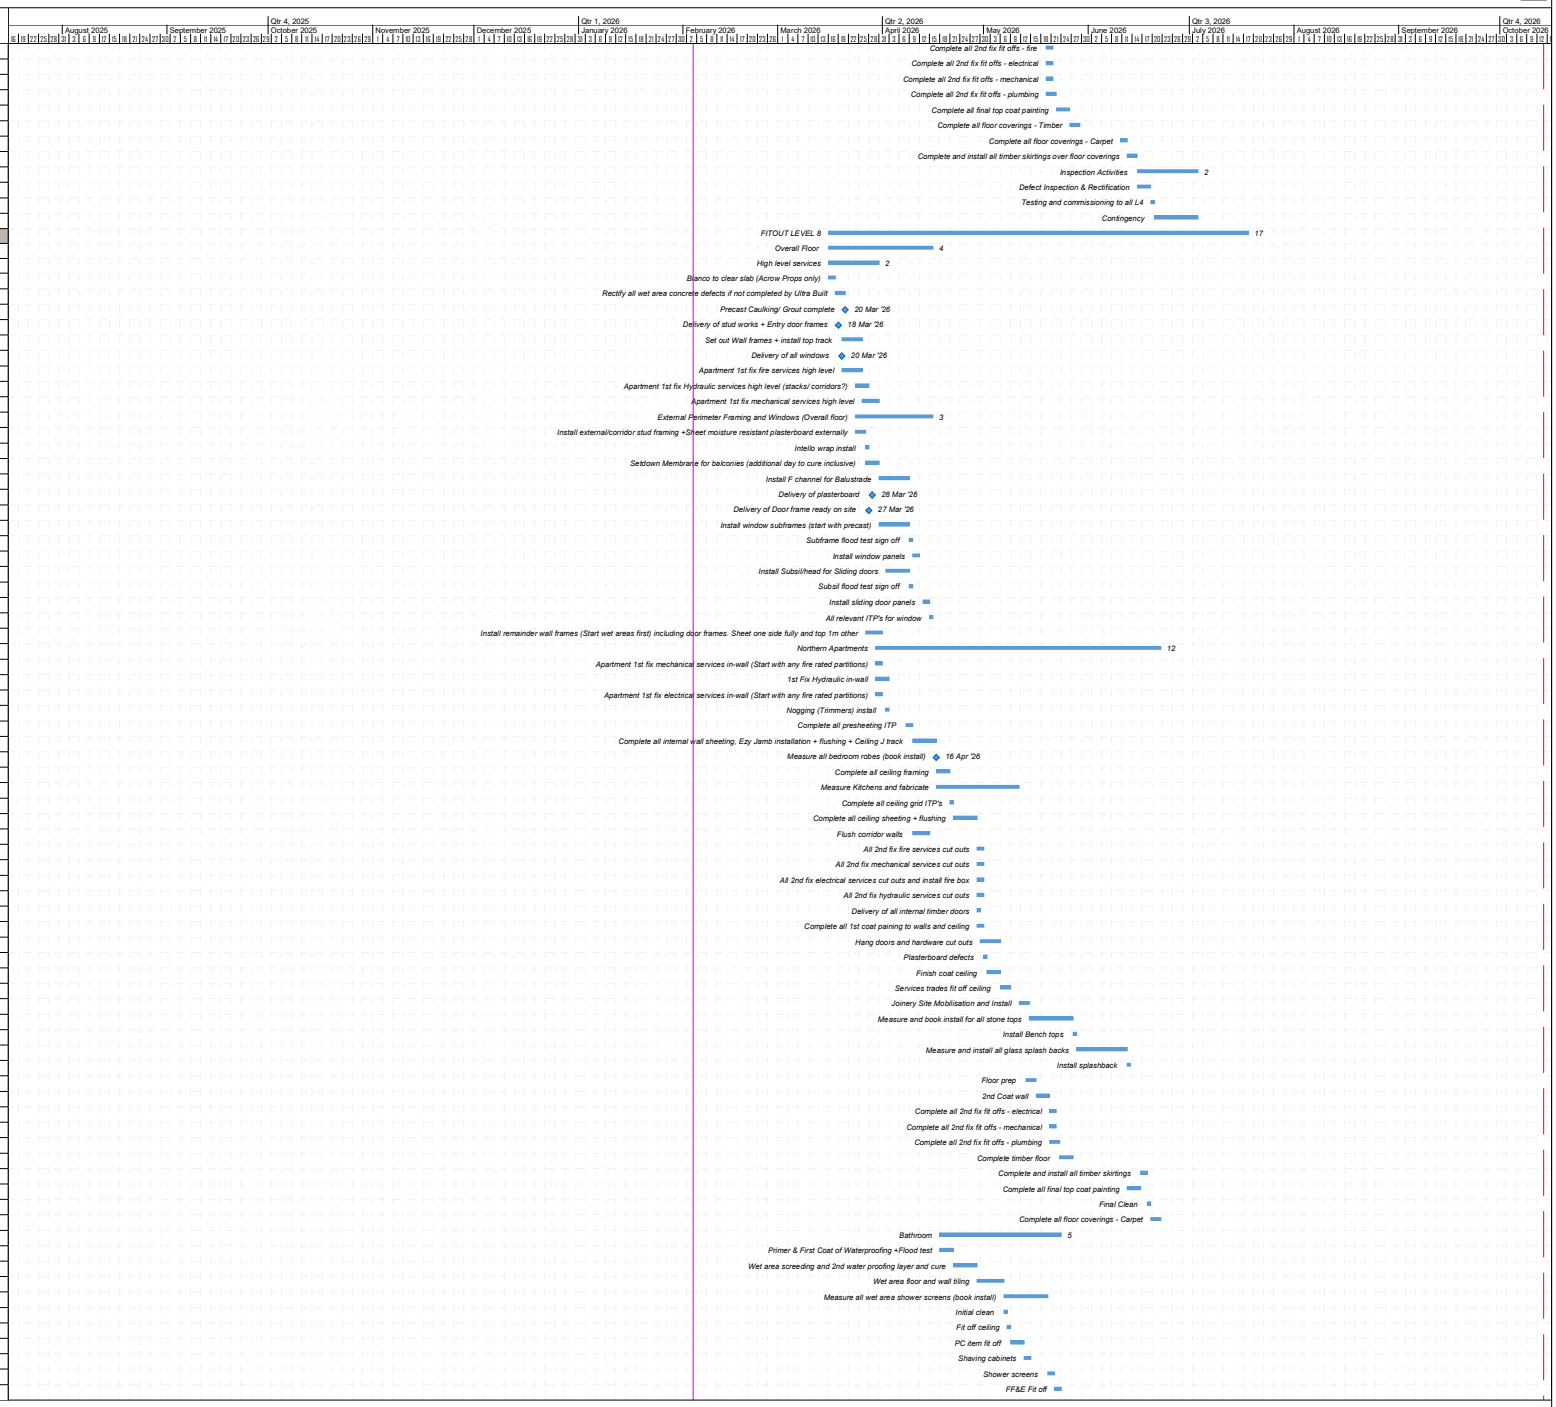

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
2854	**Balcony & Façade**	**0%**	**19 days**	**Wed 15/04/26**	**Sat 9/05/26**
2855	Caulking to all external windows/ doors	0%	1 day	Wed 15/04/26	Wed 15/04/26
2856	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Thu 16/04/26	Wed 22/04/26
2857	Complete all external balcony balustrading	0%	4 days	Thu 23/04/26	Wed 29/04/26
2858	Complete all balcony water proofing	0%	3 days	Thu 30/04/26	Sat 2/05/26
2859	Complete all balcony tiling	0%	3 days	Tue 5/05/26	Thu 7/05/26
2860	Complete all external painting to the cladding	0%	2 days	Fri 8/05/26	Sat 9/05/26
2861	**Southern Apartments**	**0%**	**61.5 days**	**Wed 1/04/26**	**Wed 24/06/26**
2862	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 1/04/26	Thu 2/04/26
2863	1st Fix Hydraulic in-wall	0%	4 days	Wed 8/04/26	Sat 11/04/26
2864	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 1/04/26	Thu 2/04/26
2865	Nogging (Trimmers) install	0%	1 day	Sat 11/04/26	Sat 11/04/26
2866	Complete all presheeting ITP	0%	2 days	Mon 13/04/26	Tue 14/04/26
2867	Complete all internal wall sheeting, Ezy Jamb installation + flushing+ Jtrack	0%	6 days	Wed 15/04/26	Tue 21/04/26
2868	Measure all bedroom robes (book install)	0%	0 days	Tue 21/04/26	Tue 21/04/26
2869	Complete all ceiling framing	0%	3 days	Wed 22/04/26	Fri 24/04/26
2870	Measure Kitchens and fabricate	0%	3.5 wks	Wed 22/04/26	Fri 15/05/26
2871	Complete all ceiling grid ITP's	0%	1 day	Tue 28/04/26	Tue 28/04/26
2872	Complete all ceiling sheeting + flushing	0%	4 days	Wed 29/04/26	Sat 2/05/26
2873	Flush corridor walls	0%	4 days	Wed 15/04/26	Sat 18/04/26
2874	All 2nd fix fire services cut outs	0%	2 days	Tue 5/05/26	Wed 6/05/26
2875	All 2nd fix mechanical services cut outs	0%	2 days	Tue 5/05/26	Wed 6/05/26
2876	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Tue 5/05/26	Wed 6/05/26
2877	All 2nd fix hydraulic services cut outs	0%	2 days	Tue 5/05/26	Wed 6/05/26
2878	Delivery of all internal timber doors	0%	1 day	Tue 5/05/26	Tue 5/05/26
2879	Complete all 1st coat paining to walls and ceiling	0%	2 days	Tue 5/05/26	Wed 6/05/26
2880	Hang doors and hardware cut outs	0%	4 days	Wed 6/05/26	Sat 9/05/26
2881	Plasterboard defects	0%	1 day	Thu 7/05/26	Thu 7/05/26
2882	Finish coat ceiling	0%	2 days	Fri 8/05/26	Sat 9/05/26
2883	Services trades fit off ceiling	0%	3 days	Mon 11/05/26	Wed 13/05/26
2884	Joinery Site Mobilisation and Install	0%	3 days	Fri 15/05/26	Wed 20/05/26
2885	Measure and book install for all stone tops	0%	2 wks	Wed 20/05/26	Mon 1/06/26
2886	Install Bench tops	0%	1 day	Mon 1/06/26	Tue 2/06/26
2887	Measure and install all glass splash backs	0%	2 wks	Tue 2/06/26	Wed 17/06/26
2888	Install splashback	0%	1 day	Wed 17/06/26	Thu 18/06/26
2889	Floor prep	0%	3 days	Tue 19/05/26	Fri 22/05/26
2890	2nd Coat wall	0%	2 days	Fri 22/05/26	Mon 25/05/26
2891	Complete all 2nd fix fit offs - electrical	0%	2 days	Mon 25/05/26	Wed 27/05/26
2892	Complete all 2nd fix fit offs - mechanical	0%	2 days	Mon 25/05/26	Wed 27/05/26
2893	Complete all 2nd fix fit offs - plumbing	0%	3 days	Mon 25/05/26	Thu 28/05/26
2894	Complete Timber Flooring	0%	3 days	Thu 28/05/26	Mon 1/06/26
2895	Complete and install all timber skirtings	0%	2 days	Thu 4/06/26	Wed 10/06/26
2896	Complete all final top coat painting	0%	3 days	Mon 1/06/26	Thu 4/06/26
2897	Final Clean	0%	1 day	Thu 18/06/26	Fri 19/06/26
2898	Complete all floor coverings - Carpet	0%	2 days	Mon 22/06/26	Wed 24/06/26
2899	**Bathroom**	**0%**	**27 days**	**Thu 23/04/26**	**Thu 28/05/26**
2900	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Thu 23/04/26	Tue 28/04/26
2901	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Wed 29/04/26	Sat 2/05/26
2902	Wet area floor and wall tiling	0%	6 days	Tue 5/05/26	Mon 11/05/26
2903	Measure all wet area shower screens (book install)	0%	2 wks	Tue 12/05/26	Sat 23/05/26
2904	Initial clean	0%	1 day	Tue 12/05/26	Tue 12/05/26
2905	Fit off ceiling	0%	1 day	Wed 13/05/26	Wed 13/05/26
2906	PC item fit off	0%	3 days	Thu 14/05/26	Sat 16/05/26
2907	Shaving cabinets	0%	2 days	Tue 19/05/26	Wed 20/05/26
2908	Shower screens	0%	2 days	Mon 25/05/26	Tue 26/05/26
2909	FF&E Fit off	0%	2 days	Wed 27/05/26	Thu 28/05/26
2910	**Balcony & Façade**	**0%**	**19 days**	**Wed 15/04/26**	**Sat 9/05/26**
2911	Caulking to all external windows/ doors	0%	1 day	Wed 15/04/26	Wed 15/04/26
2912	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Thu 16/04/26	Wed 22/04/26
2913	Complete all external balcony balustrading	0%	4 days	Thu 23/04/26	Wed 29/04/26
2914	Complete all balcony water proofing	0%	3 days	Thu 30/04/26	Sat 2/05/26
2915	Complete all balcony tiling	0%	3 days	Tue 5/05/26	Thu 7/05/26
2916	Complete all external painting to the cladding	0%	2 days	Fri 8/05/26	Sat 9/05/26
2917	**Common Area (Corridors)**	**0%**	**68.5 days**	**Mon 20/04/26**	**Sat 18/07/26**
2918	Prime walls	0%	1 day	Mon 20/04/26	Mon 20/04/26
2919	Ceiling framing	0%	2 days	Wed 20/05/26	Fri 22/05/26
2920	Services and Ceiling Closeout ITP	0%	1 day	Fri 22/05/26	Sat 23/05/26
2921	Sheet and Flush Ceiling	0%	4 days	Sat 23/05/26	Thu 28/05/26
2922	Cut out ceilign services	0%	1 day	Thu 28/05/26	Fri 29/05/26
2923	2nd Coat wall and Finish coat ceiling	0%	3 days	Fri 29/05/26	Tue 2/06/26
2924	Complete all 2nd fix fit offs - fire	0%	2 days	Tue 2/06/26	Thu 4/06/26
2925	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 2/06/26	Thu 4/06/26
2926	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 2/06/26	Thu 4/06/26
2927	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 2/06/26	Fri 5/06/26
2928	Complete all final top coat painting	0%	3 days	Fri 5/06/26	Fri 12/06/26
2929	Complete all floor coverings - Timber	0%	3 days	Fri 12/06/26	Tue 16/06/26
2930	Complete all floor coverings - Carpet	0%	2 days	Wed 24/06/26	Fri 26/06/26
2931	Complete and install all timber skirtings over floor coverings	0%	2 days	Fri 26/06/26	Tue 30/06/26
2932	**Inspection Activities**	**0%**	**15 days**	**Tue 30/06/26**	**Sat 18/07/26**
2933	Defect Inspection & Rectification	0%	4 days	Tue 30/06/26	Sat 4/07/26
2934	Testing and commissioning to all L4	0%	1 day	Sat 4/07/26	Mon 6/07/26
2935	Contingency	0%	10 days	Mon 6/07/26	Sat 18/07/26
2936	**FITOUT LEVEL 9**	**0%**	**96.5 days**	**Tue 31/03/26**	**Wed 5/08/26**
2937	**Overall Floor**	**0%**	**22 days**	**Tue 31/03/26**	**Fri 1/05/26**
2938	**High level services**	**0%**	**12 days**	**Tue 31/03/26**	**Fri 17/04/26**
2939	Bianco to clear slab (Acrow Props only)	0%	2 days	Tue 31/03/26	Wed 1/04/26
2940	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Thu 2/04/26	Thu 9/04/26
2941	Precast Caulking/ Grout complete	0%	0 days	Thu 9/04/26	Thu 9/04/26

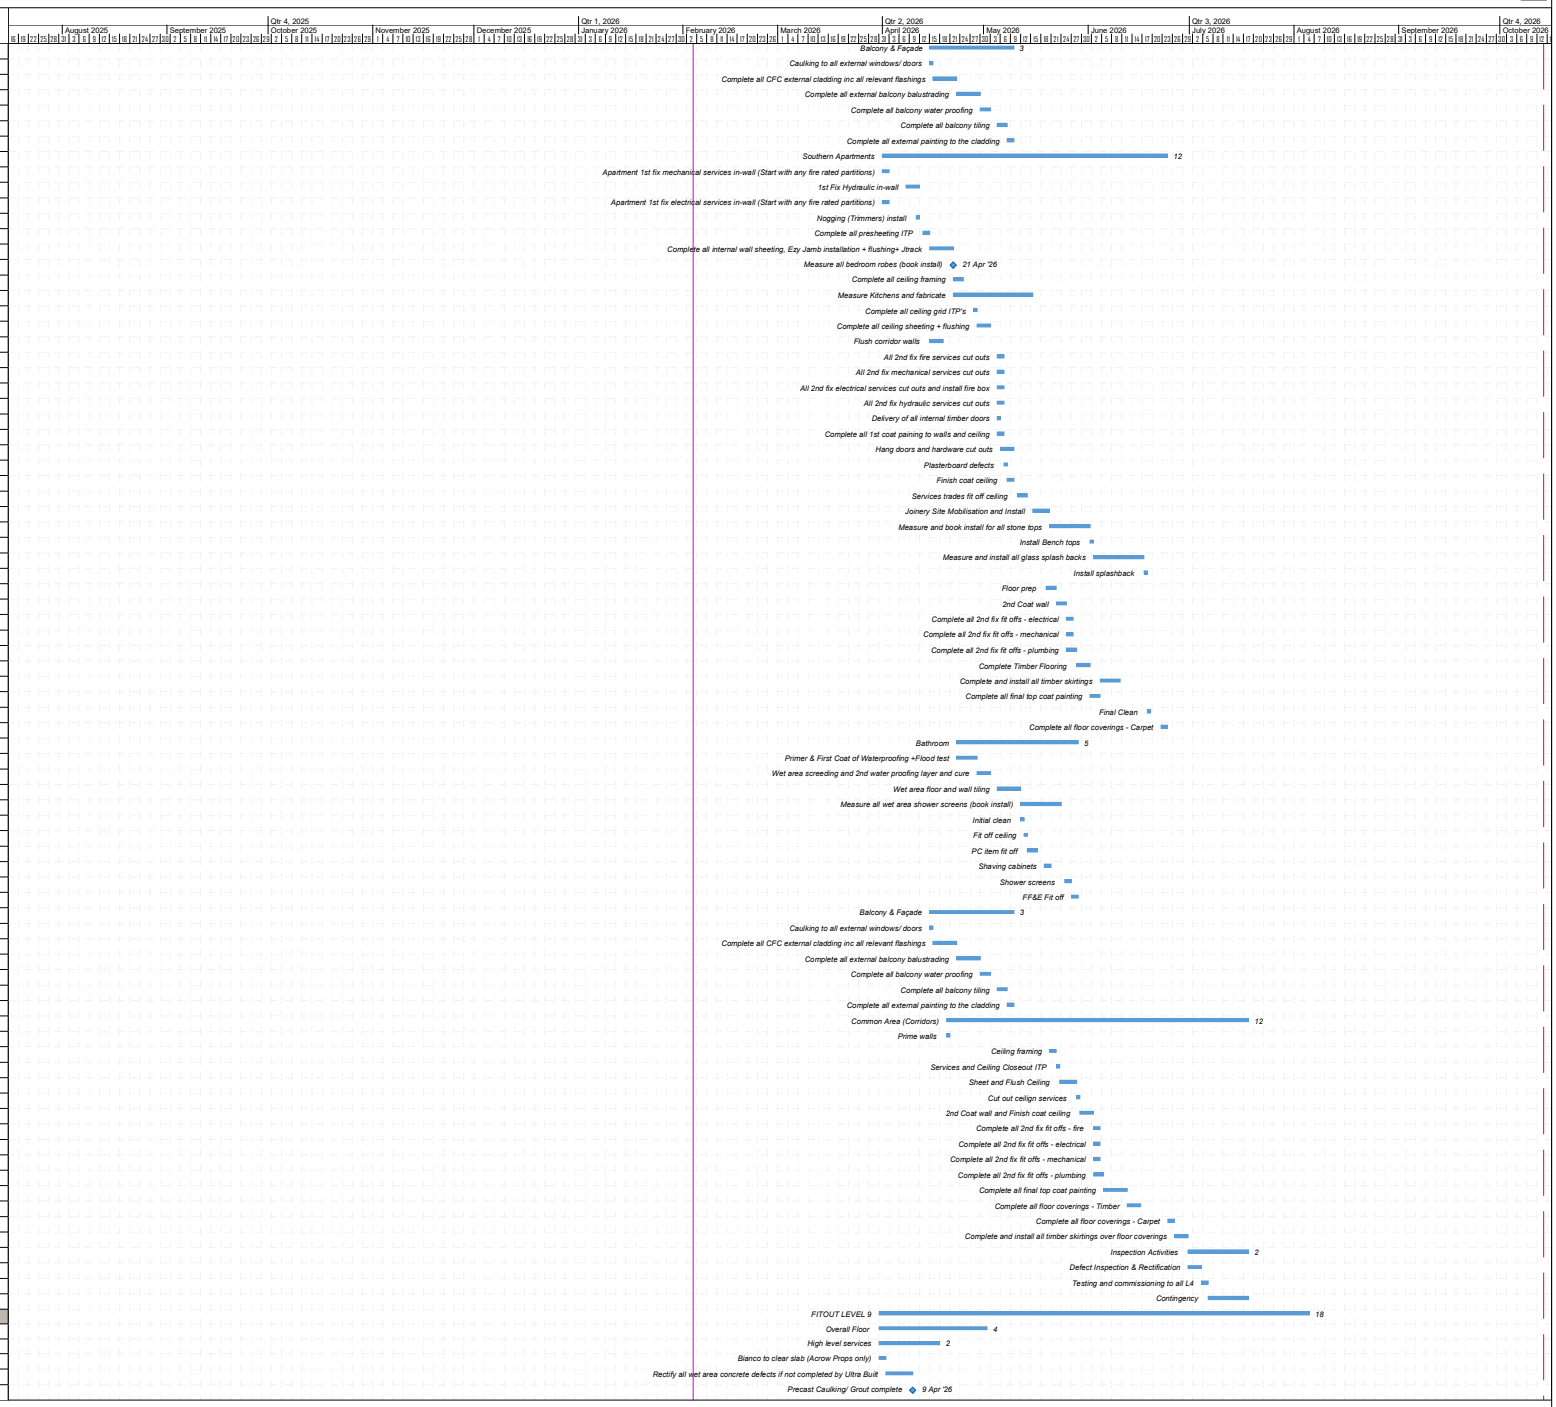

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
2942	Delivery of stud works + Entry door frames	0%	0 days	Thu 9/04/26	Thu 9/04/26
2943	Set out Wall frames	0%	4 days	Thu 9/04/26	Mon 13/04/26
2944	Delivery of all windows	0%	0 days	Fri 10/04/26	Fri 10/04/26
2945	Apartment 1st fix fire services high level	0%	4 days	Thu 9/04/26	Mon 13/04/26
2946	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Sat 11/04/26	Wed 15/04/26
2947	Apartment 1st fix mechanical services high level	0%	4 days	Tue 14/04/26	Fri 17/04/26
2948	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Sat 11/04/26**	**Fri 1/05/26**
2949	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Sat 11/04/26	Tue 14/04/26
2950	Intello wrap install	0%	1 day	Wed 15/04/26	Wed 15/04/26
2951	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Wed 15/04/26	Fri 17/04/26
2952	Install F channel for Balustrade	0%	4 days	Sat 18/04/26	Wed 22/04/26
2953	Delivery of plasterboard	0%	0 days	Thu 16/04/26	Thu 16/04/26
2954	Delivery of Door frame ready on site	0%	0 days	Wed 15/04/26	Wed 15/04/26
2955	Install window subframes (start with precast)	0%	4 days	Sat 18/04/26	Wed 22/04/26
2956	Subframe flood test sign off	0%	1 day	Thu 23/04/26	Thu 23/04/26
2957	Install window panels	0%	2 days	Fri 24/04/26	Tue 28/04/26
2958	Install Subsill/head for Sliding doors	0%	2 days	Tue 21/04/26	Wed 22/04/26
2959	Subsil flood test sign off	0%	1 day	Thu 23/04/26	Thu 23/04/26
2960	Install sliding door panels	0%	2 days	Wed 29/04/26	Thu 30/04/26
2961	All relevant ITP's for window	0%	1 day	Fri 1/05/26	Fri 1/05/26
2962	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side full	0%	4 days	Wed 15/04/26	Sat 18/04/26
2963	**Northern Apartments**	**0%**	**61.5 days**	**Mon 20/04/26**	**Thu 9/07/26**
2964	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 20/04/26	Tue 21/04/26
2965	1st Fix Hydraulic in-wall	0%	4 days	Mon 20/04/26	Thu 23/04/26
2966	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 20/04/26	Tue 21/04/26
2967	Nogging (Trimmers) install	0%	1 day	Thu 23/04/26	Thu 23/04/26
2968	Complete all presheeting ITP	0%	2 days	Fri 24/04/26	Tue 28/04/26
2969	Complete all internal wall sheeting, Ezy Jamb installation + flushing +J track	0%	6 days	Wed 29/04/26	Wed 6/05/26
2970	Measure all bedroom robes (book install)	0%	0 days	Wed 6/05/26	Wed 6/05/26
2971	Complete all ceiling framing	0%	3 days	Thu 7/05/26	Sat 9/05/26
2972	Measure Kitchens and fabricate	0%	3.5 wks	Thu 7/05/26	Thu 28/05/26
2973	Complete all ceiling grid ITP's	0%	1 day	Mon 11/05/26	Mon 11/05/26
2974	Complete all ceiling sheeting + flushing	0%	4 days	Tue 12/05/26	Fri 15/05/26
2975	Flush corridor walls	0%	4 days	Wed 29/04/26	Sat 2/05/26
2976	All 2nd fix fire services cut outs	0%	2 days	Sat 16/05/26	Tue 19/05/26
2977	All 2nd fix mechanical services cut outs	0%	2 days	Sat 16/05/26	Tue 19/05/26
2978	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Sat 16/05/26	Tue 19/05/26
2979	All 2nd fix hydraulic services cut outs	0%	2 days	Sat 16/05/26	Tue 19/05/26
2980	Delivery of all internal timber doors	0%	1 day	Sat 16/05/26	Sat 16/05/26
2981	Complete all 1st coat paining to walls and ceiling	0%	2 days	Sat 16/05/26	Tue 19/05/26
2982	Hang doors and hardware cut outs	0%	4 days	Tue 19/05/26	Fri 22/05/26
2983	Plasterboard defects	0%	1 day	Wed 20/05/26	Wed 20/05/26
2984	Finish coat ceiling	0%	2 days	Thu 21/05/26	Fri 22/05/26
2985	Services trades fit off ceiling	0%	3 days	Sat 23/05/26	Tue 26/05/26
2986	Joinery Site Mobilisation and Install	0%	3 days	Thu 28/05/26	Mon 1/06/26
2987	Measure and book install for all stone tops	0%	2 wks	Mon 1/06/26	Tue 16/06/26
2988	Install Bench tops	0%	1 day	Tue 16/06/26	Wed 17/06/26
2989	Measure and install all glass splash backs	0%	2 wks	Wed 17/06/26	Tue 30/06/26
2990	Install splashback	0%	1 day	Tue 30/06/26	Wed 1/07/26
2991	Floor prep	0%	3 days	Sat 30/05/26	Wed 3/06/26
2992	2nd Coat wall	0%	2 days	Wed 3/06/26	Fri 5/06/26
2993	Complete all 2nd fix fit offs - electrical	0%	2 days	Fri 5/06/26	Thu 11/06/26
2994	Complete all 2nd fix fit offs - mechanical	0%	2 days	Fri 5/06/26	Thu 11/06/26
2995	Complete all 2nd fix fit offs - plumbing	0%	3 days	Fri 5/06/26	Fri 12/06/26
2996	Complete timber floor	0%	3 days	Fri 12/06/26	Tue 16/06/26
2997	Complete and install all timber skirtings	0%	2 days	Fri 3/07/26	Mon 6/07/26
2998	Complete all final top coat painting	0%	3 days	Tue 30/06/26	Fri 3/07/26
2999	Final Clean	0%	1 day	Mon 6/07/26	Tue 7/07/26
3000	Complete all floor coverings - Carpet	0%	2 days	Tue 7/07/26	Thu 9/07/26
3001	**Bathroom**	**0%**	**27 days**	**Fri 8/05/26**	**Fri 12/06/26**
3002	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Fri 8/05/26	Mon 11/05/26
3003	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Tue 12/05/26	Fri 15/05/26
3004	Wet area floor and wall tiling	0%	6 days	Sat 16/05/26	Sat 23/05/26
3005	Measure all wet area shower screens (book install)	0%	10 days	Mon 25/05/26	Thu 4/06/26
3006	Initial clean	0%	1 day	Mon 25/05/26	Mon 25/05/26
3007	Fit off ceiling	0%	1 day	Tue 26/05/26	Tue 26/05/26
3008	PC item fit off	0%	3 days	Wed 27/05/26	Fri 29/05/26
3009	Shaving cabinets	0%	2 days	Sat 30/05/26	Mon 1/06/26
3010	Shower screens	0%	2 days	Fri 5/06/26	Wed 10/06/26
3011	FF&E Fit off	0%	2 days	Thu 11/06/26	Fri 12/06/26
3012	**Balcony & Façade**	**0%**	**19 days**	**Fri 1/05/26**	**Mon 25/05/26**
3013	Caulking to all external windows/ doors	0%	1 day	Fri 1/05/26	Fri 1/05/26
3014	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Sat 2/05/26	Sat 9/05/26
3015	Complete all external balcony balustrading	0%	4 days	Mon 11/05/26	Thu 14/05/26
3016	Complete all balcony water proofing	0%	3 days	Fri 15/05/26	Tue 19/05/26
3017	Complete all balcony tiling	0%	3 days	Wed 20/05/26	Fri 22/05/26
3018	Complete all external painting to the cladding	0%	2 days	Sat 23/05/26	Mon 25/05/26
3019	**Southern Apartments**	**0%**	**61.5 days**	**Wed 22/04/26**	**Sat 11/07/26**
3020	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 22/04/26	Thu 23/04/26
3021	1st Fix Hydraulic in-wall	0%	4 days	Fri 24/04/26	Thu 30/04/26
3022	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Wed 22/04/26	Thu 23/04/26
3023	Nogging (Trimmers) install	0%	1 day	Thu 30/04/26	Thu 30/04/26
3024	Complete all presheeting ITP	0%	2 days	Fri 1/05/26	Sat 2/05/26
3025	Complete all internal wall sheeting, Ezy Jamb installation + flushing +Jtrack	0%	6 days	Tue 5/05/26	Mon 11/05/26
3026	Measure all bedroom robes (book install)	0%	0 days	Mon 11/05/26	Mon 11/05/26
3027	Complete all ceiling framing	0%	3 days	Tue 12/05/26	Thu 14/05/26
3028	Measure Kitchens and fabricate	0%	3.5 wks	Tue 12/05/26	Tue 2/06/26
3029	Complete all ceiling grid ITP's	0%	1 day	Fri 15/05/26	Fri 15/05/26

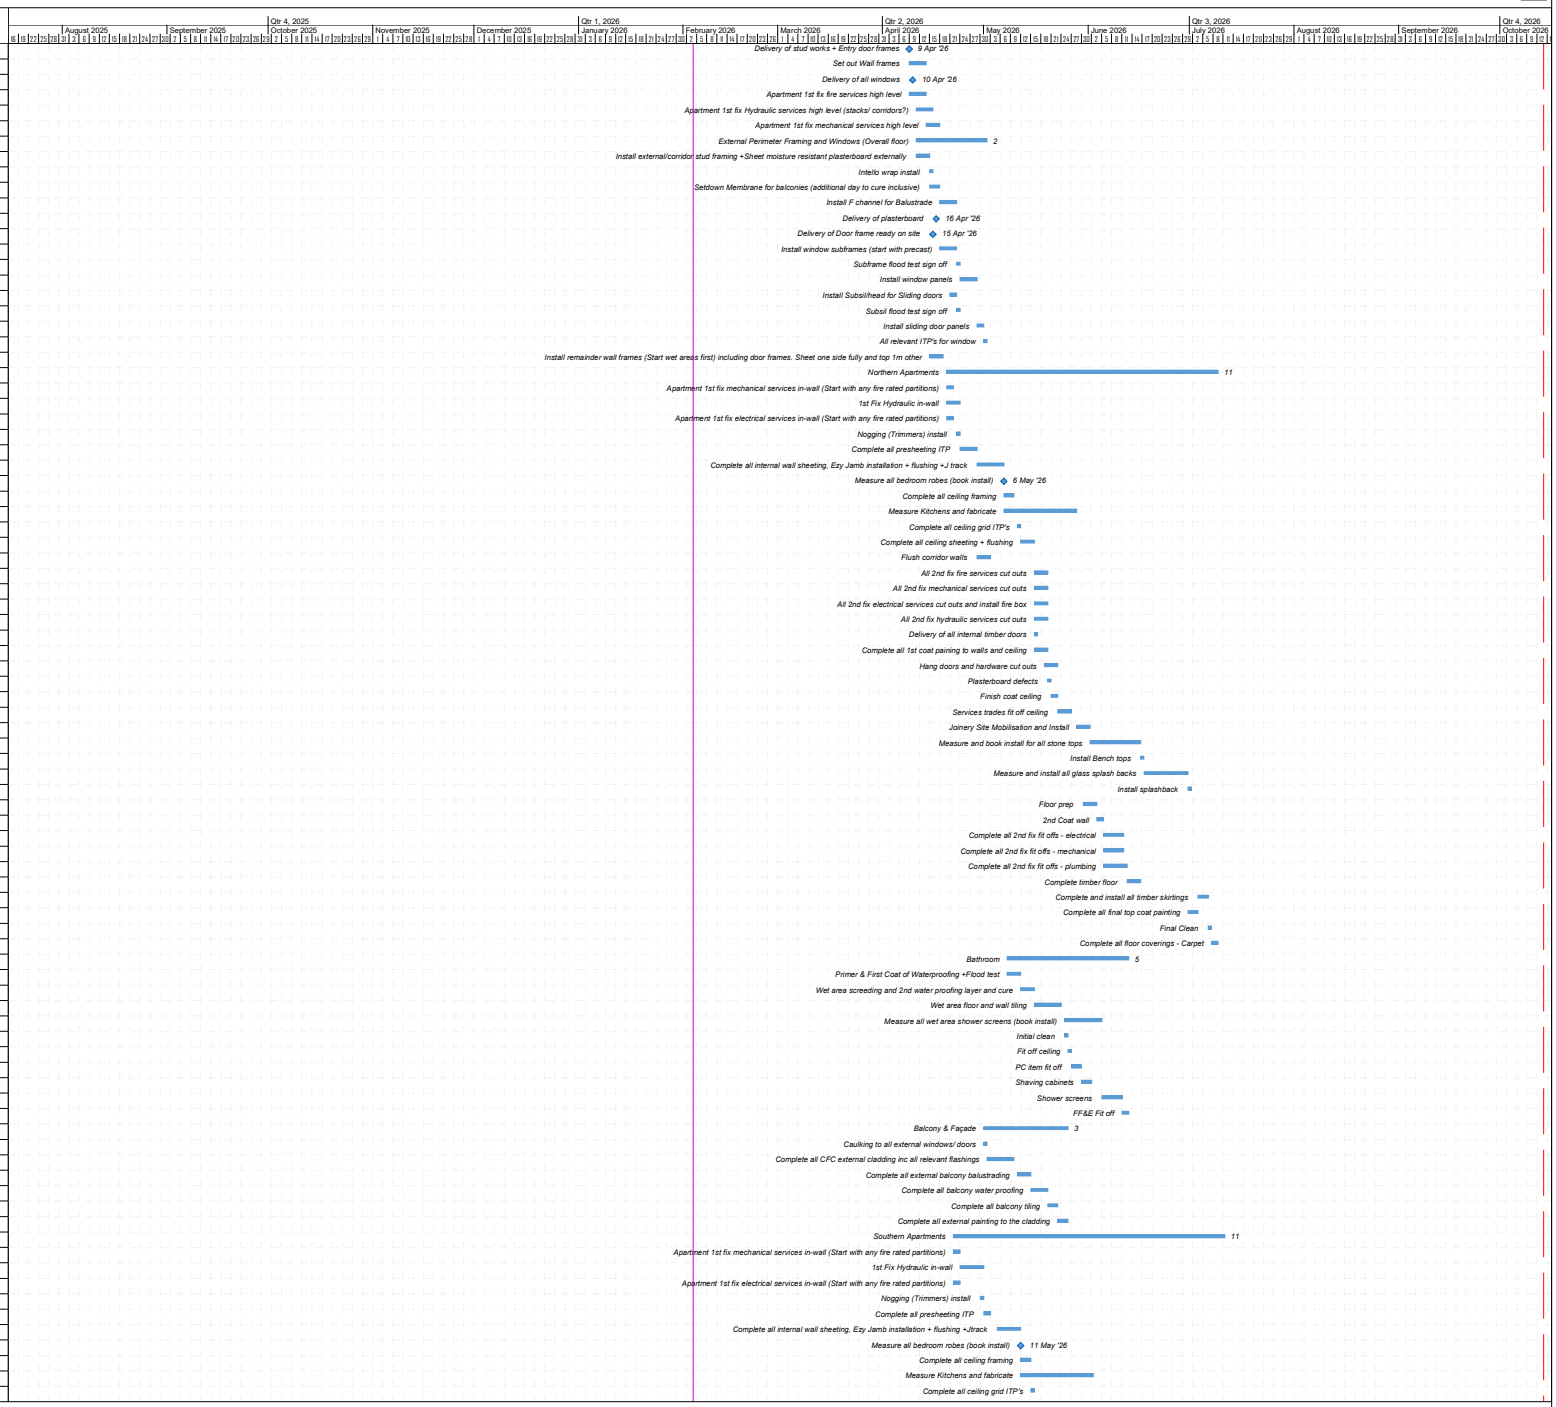

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
3030	Complete all ceiling sheeting + flushing	0%	4 days	Sat 16/05/26	Thu 21/05/26
3031	Flush corridor walls	0%	4 days	Tue 5/05/26	Fri 8/05/26
3032	All 2nd fix fire services cut outs	0%	2 days	Fri 22/05/26	Sat 23/05/26
3033	All 2nd fix mechanical services cut outs	0%	2 days	Fri 22/05/26	Sat 23/05/26
3034	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Fri 22/05/26	Sat 23/05/26
3035	All 2nd fix hydraulic services cut outs	0%	2 days	Fri 22/05/26	Sat 23/05/26
3036	Delivery of all internal timber doors	0%	1 day	Fri 22/05/26	Fri 22/05/26
3037	Complete all 1st coat paining to walls and ceiling	0%	2 days	Fri 22/05/26	Sat 23/05/26
3038	Hang doors and hardware cut outs	0%	4 days	Sat 23/05/26	Wed 27/05/26
3039	Plasterboard defects	0%	1 day	Mon 25/05/26	Mon 25/05/26
3040	Finish coat ceiling	0%	2 days	Tue 26/05/26	Wed 27/05/26
3041	Services trades fit off ceiling	0%	3 days	Thu 28/05/26	Sat 30/05/26
3042	Joinery Site Mobilisation and Install	0%	3 days	Tue 2/06/26	Fri 5/06/26
3043	Measure and book install for all stone tops	0%	2 wks	Fri 5/06/26	Sat 20/06/26
3044	Install Bench tops	0%	1 day	Sat 20/06/26	Mon 22/06/26
3045	Measure and install all glass splash backs	0%	2 wks	Mon 22/06/26	Sat 4/07/26
3046	Install splashback	0%	1 day	Sat 4/07/26	Mon 6/07/26
3047	Floor prep	0%	3 days	Thu 4/06/26	Thu 11/06/26
3048	2nd Coat wall	0%	2 days	Thu 11/06/26	Sat 13/06/26
3049	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 13/06/26	Tue 16/06/26
3050	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 13/06/26	Tue 16/06/26
3051	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 13/06/26	Wed 17/06/26
3052	Complete Timber Flooring	0%	3 days	Wed 17/06/26	Sat 20/06/26
3053	Complete and install all timber skirtings	0%	2 days	Wed 24/06/26	Fri 26/06/26
3054	Complete all final top coat painting	0%	3 days	Sat 20/06/26	Wed 24/06/26
3055	Final Clean	0%	1 day	Mon 6/07/26	Tue 7/07/26
3056	Complete all floor coverings - Carpet	0%	2 days	Thu 9/07/26	Sat 11/07/26
3057	**Bathroom**	**0%**	**27 days**	**Wed 13/05/26**	**Wed 17/06/26**
3058	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Wed 13/05/26	Fri 15/05/26
3059	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Sat 16/05/26	Thu 21/05/26
3060	Wet area floor and wall tiling	0%	6 days	Fri 22/05/26	Thu 28/05/26
3061	Measure all wet area shower screens (book install)	0%	2 wks	Fri 29/05/26	Fri 12/06/26
3062	Initial clean	0%	1 day	Fri 29/05/26	Fri 29/05/26
3063	Fit off ceiling	0%	1 day	Sat 30/05/26	Sat 30/05/26
3064	PC item fit off	0%	3 days	Mon 1/06/26	Wed 3/06/26
3065	Shaving cabinets	0%	2 days	Thu 4/06/26	Fri 5/06/26
3066	Shower screens	0%	2 days	Sat 13/06/26	Mon 15/06/26
3067	FF&E Fit off	0%	2 days	Tue 16/06/26	Wed 17/06/26
3068	**Balcony & Façade**	**0%**	**19 days**	**Fri 1/05/26**	**Mon 25/05/26**
3069	Caulking to all external windows/ doors	0%	1 day	Fri 1/05/26	Fri 1/05/26
3070	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Sat 2/05/26	Sat 9/05/26
3071	Complete all external balcony balustrading	0%	4 days	Mon 11/05/26	Thu 14/05/26
3072	Complete all balcony water proofing	0%	3 days	Fri 15/05/26	Tue 19/05/26
3073	Complete all balcony tiling	0%	3 days	Wed 20/05/26	Fri 22/05/26
3074	Complete all external painting to the cladding	0%	2 days	Sat 23/05/26	Mon 25/05/26
3075	**Common Area (Corridors)**	**0%**	**68.5 days**	**Sat 9/05/26**	**Wed 5/08/26**
3076	Prime walls	0%	1 day	Sat 9/05/26	Sat 9/05/26
3077	Ceiling framing	0%	2 days	Fri 5/06/26	Thu 11/06/26
3078	Services and Ceiling Closeout ITP	0%	1 day	Thu 11/06/26	Fri 12/06/26
3079	Sheet and Flush Ceiling	0%	4 days	Fri 12/06/26	Wed 17/06/26
3080	Cut out ceilign services	0%	1 day	Wed 17/06/26	Thu 18/06/26
3081	2nd Coat wall and Finish coat ceiling	0%	3 days	Thu 18/06/26	Mon 22/06/26
3082	Complete all 2nd fix fit offs - fire	0%	2 days	Mon 22/06/26	Wed 24/06/26
3083	Complete all 2nd fix fit offs - electrical	0%	2 days	Mon 22/06/26	Wed 24/06/26
3084	Complete all 2nd fix fit offs - mechanical	0%	2 days	Mon 22/06/26	Wed 24/06/26
3085	Complete all 2nd fix fit offs - plumbing	0%	3 days	Mon 22/06/26	Thu 25/06/26
3086	Complete all final top coat painting	0%	3 days	Thu 25/06/26	Tue 30/06/26
3087	Complete all floor coverings - Timber	0%	3 days	Tue 30/06/26	Fri 3/07/26
3088	Complete all floor coverings - Carpet	0%	2 days	Sat 11/07/26	Wed 15/07/26
3089	Complete and install all timber skirtings over floor coverings	0%	2 days	Wed 15/07/26	Fri 17/07/26
3090	**Inspection Activities**	**0%**	**15 days**	**Fri 17/07/26**	**Wed 5/08/26**
3091	Defect Inspection & Rectification	0%	4 days	Fri 17/07/26	Wed 22/07/26
3092	Testing and commissioning to all L4	0%	1 day	Wed 22/07/26	Thu 23/07/26
3093	Contingency	0%	10 days	Thu 23/07/26	Wed 5/08/26
3094	FITOUT LEVEL 10	0%	94.5 days	Fri 17/04/26	Tue 18/08/26
3095	**Overall Floor**	**0%**	**21 days**	**Fri 17/04/26**	**Thu 14/05/26**
3096	**High level services**	**0%**	**11 days**	**Fri 17/04/26**	**Fri 1/05/26**
3097	Bianco to clear slab (Acrow Props only)	0%	2 days	Fri 17/04/26	Sat 18/04/26
3098	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Mon 20/04/26	Wed 22/04/26
3099	Precast Caulking/ Grout complete	0%	0 days	Wed 22/04/26	Wed 22/04/26
3100	Delivery of stud works + Entry door frames	0%	0 days	Tue 21/04/26	Tue 21/04/26
3101	Set out Wall frames +Top track	0%	4 days	Tue 21/04/26	Fri 24/04/26
3102	Delivery of all windows	0%	0 days	Wed 22/04/26	Wed 22/04/26
3103	Apartment 1st fix fire services high level	0%	4 days	Tue 21/04/26	Fri 24/04/26
3104	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Thu 23/04/26	Wed 29/04/26
3105	Apartment 1st fix mechanical services high level	0%	4 days	Tue 28/04/26	Fri 1/05/26
3106	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Thu 23/04/26**	**Thu 14/05/26**
3107	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Thu 23/04/26	Tue 28/04/26
3108	Intello wrap install	0%	1 day	Wed 29/04/26	Wed 29/04/26
3109	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Wed 29/04/26	Fri 1/05/26
3110	Install F channel for Balustrade	0%	4 days	Sat 2/05/26	Thu 7/05/26
3111	Delivery of plasterboard	0%	0 days	Thu 30/04/26	Thu 30/04/26
3112	Delivery of Door frame ready on site	0%	0 days	Wed 29/04/26	Wed 29/04/26
3113	Install window subframes (start with precast)	0%	4 days	Sat 2/05/26	Thu 7/05/26
3114	Subframe flood test sign off	0%	1 day	Fri 8/05/26	Fri 8/05/26
3115	Install window panels	0%	2 days	Sat 9/05/26	Mon 11/05/26
3116	Install Subsill/head for Sliding doors	0%	2 days	Wed 6/05/26	Thu 7/05/26
3117	Subsil flood test sign off	0%	1 day	Fri 8/05/26	Fri 8/05/26

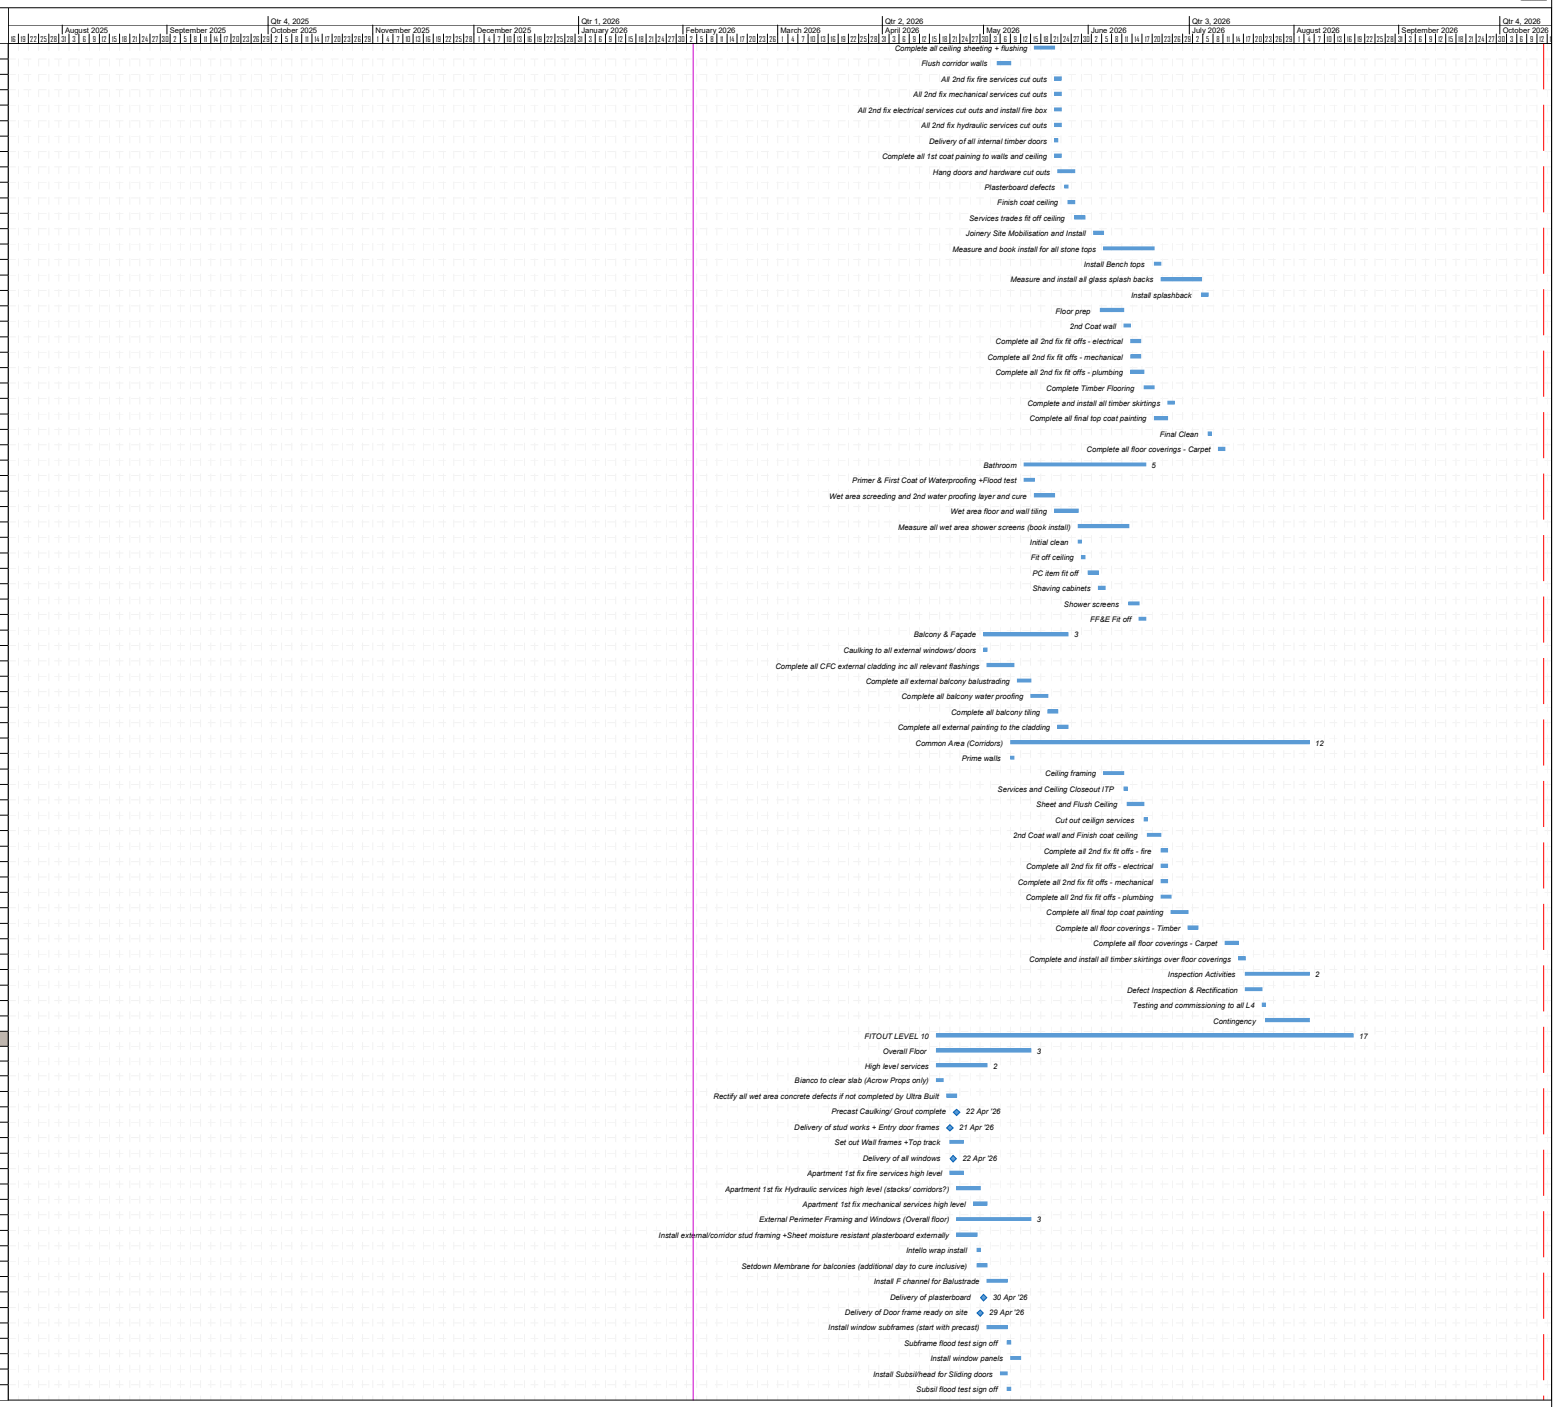

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
3118	Install sliding door panels	0%	2 days	Tue 12/05/26	Wed 13/05/26
3119	All relevant ITP's for window	0%	1 day	Thu 14/05/26	Thu 14/05/26
3120	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side full	0%	4 days	Wed 29/04/26	Sat 2/05/26
3121	**Northern Apartments**	**0%**	**61.5 days**	**Tue 5/05/26**	**Wed 22/07/26**
3122	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 5/05/26	Wed 6/05/26
3123	1st Fix Hydraulic in-wall	0%	4 days	Tue 5/05/26	Fri 8/05/26
3124	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 5/05/26	Wed 6/05/26
3125	Nogging (Trimmers) install	0%	1 day	Fri 8/05/26	Fri 8/05/26
3126	Complete all presheeting ITP	0%	2 days	Sat 9/05/26	Mon 11/05/26
3127	Complete all internal wall sheeting, Ezy Jamb installation + flushing + Jtrack	0%	6 days	Tue 12/05/26	Tue 19/05/26
3128	Measure all bedroom robes (book install)	0%	0 days	Tue 19/05/26	Tue 19/05/26
3129	Complete all ceiling framing	0%	3 days	Wed 20/05/26	Fri 22/05/26
3130	Measure Kitchens and fabricate	0%	3.5 wks	Wed 20/05/26	Fri 12/06/26
3131	Complete all ceiling grid ITP's	0%	1 day	Sat 23/05/26	Sat 23/05/26
3132	Complete all ceiling sheeting + flushing	0%	4 days	Mon 25/05/26	Thu 28/05/26
3133	Flush corridor walls	0%	4 days	Tue 12/05/26	Fri 15/05/26
3134	All 2nd fix fire services cut outs	0%	2 days	Fri 29/05/26	Sat 30/05/26
3135	All 2nd fix mechanical services cut outs	0%	2 days	Fri 29/05/26	Sat 30/05/26
3136	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Fri 29/05/26	Sat 30/05/26
3137	All 2nd fix hydraulic services cut outs	0%	2 days	Fri 29/05/26	Sat 30/05/26
3138	Delivery of all internal timber doors	0%	1 day	Fri 29/05/26	Fri 29/05/26
3139	Complete all 1st coat paining to walls and ceiling	0%	2 days	Fri 29/05/26	Sat 30/05/26
3140	Hang doors and hardware cut outs	0%	4 days	Sat 30/05/26	Wed 3/06/26
3141	Plasterboard defects	0%	1 day	Mon 1/06/26	Mon 1/06/26
3142	Finish coat ceiling	0%	2 days	Tue 2/06/26	Wed 3/06/26
3143	Services trades fit off ceiling	0%	3 days	Thu 4/06/26	Wed 10/06/26
3144	Joinery Site Mobilisation and Install	0%	3 days	Fri 12/06/26	Tue 16/06/26
3145	Measure and book install for all stone tops	0%	2 wks	Tue 16/06/26	Sat 27/06/26
3146	Install Bench tops	0%	1 day	Sat 27/06/26	Tue 30/06/26
3147	Measure and install all glass splash backs	0%	2 wks	Tue 30/06/26	Sat 11/07/26
3148	Install splashback	0%	1 day	Sat 11/07/26	Tue 14/07/26
3149	Floor prep	0%	3 days	Mon 15/06/26	Thu 18/06/26
3150	2nd Coat wall	0%	2 days	Thu 18/06/26	Sat 20/06/26
3151	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 20/06/26	Tue 23/06/26
3152	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 20/06/26	Tue 23/06/26
3153	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 20/06/26	Wed 24/06/26
3154	Complete timber floor	0%	3 days	Wed 24/06/26	Sat 27/06/26
3155	Complete and install all timber skirtings	0%	2 days	Thu 16/07/26	Sat 18/07/26
3156	Complete all final top coat painting	0%	3 days	Sat 11/07/26	Thu 16/07/26
3157	Final Clean	0%	1 day	Sat 18/07/26	Mon 20/07/26
3158	Complete all floor coverings - Carpet	0%	2 days	Mon 20/07/26	Wed 22/07/26
3159	**Bathroom**	**0%**	**27 days**	**Thu 21/05/26**	**Wed 24/06/26**
3160	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Thu 21/05/26	Sat 23/05/26
3161	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Mon 25/05/26	Thu 28/05/26
3162	Wet area floor and wall tiling	0%	6 days	Fri 29/05/26	Thu 4/06/26
3163	Measure all wet area shower screens (book install)	0%	10 days	Fri 5/06/26	Fri 19/06/26
3164	Initial clean	0%	1 day	Fri 5/06/26	Fri 5/06/26
3165	Fit off ceiling	0%	1 day	Wed 10/06/26	Wed 10/06/26
3166	PC item fit off	0%	3 days	Thu 11/06/26	Sat 13/06/26
3167	Shaving cabinets	0%	2 days	Mon 15/06/26	Tue 16/06/26
3168	Shower screens	0%	2 days	Sat 20/06/26	Mon 22/06/26
3169	FF&E Fit off	0%	2 days	Tue 23/06/26	Wed 24/06/26
3170	**Balcony & Façade**	**0%**	**19 days**	**Thu 14/05/26**	**Fri 5/06/26**
3171	Caulking to all external windows/ doors	0%	1 day	Thu 14/05/26	Thu 14/05/26
3172	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 15/05/26	Fri 22/05/26
3173	Complete all external balcony balustrading	0%	4 days	Sat 23/05/26	Wed 27/05/26
3174	Complete all balcony water proofing	0%	3 days	Thu 28/05/26	Sat 30/05/26
3175	Complete all balcony tiling	0%	3 days	Mon 1/06/26	Wed 3/06/26
3176	Complete all external painting to the cladding	0%	2 days	Thu 4/06/26	Fri 5/06/26
3177	**Southern Apartments**	**0%**	**61.5 days**	**Thu 7/05/26**	**Fri 24/07/26**
3178	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 7/05/26	Fri 8/05/26
3179	1st Fix Hydraulic in-wall	0%	4 days	Sat 9/05/26	Wed 13/05/26
3180	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 7/05/26	Fri 8/05/26
3181	Nogging (Trimmers) install	0%	1 day	Wed 13/05/26	Wed 13/05/26
3182	Complete all presheeting ITP	0%	2 days	Thu 14/05/26	Fri 15/05/26
3183	Complete all internal wall sheeting, Ezy Jamb installation + flushing +jtrack	0%	6 days	Sat 16/05/26	Sat 23/05/26
3184	Measure all bedroom robes (book install)	0%	0 days	Sat 23/05/26	Sat 23/05/26
3185	Complete all ceiling framing	0%	3 days	Mon 25/05/26	Wed 27/05/26
3186	Measure Kitchens and fabricate	0%	3.5 wks	Mon 25/05/26	Wed 17/06/26
3187	Complete all ceiling grid ITP's	0%	1 day	Thu 28/05/26	Thu 28/05/26
3188	Complete all ceiling sheeting + flushing	0%	4 days	Fri 29/05/26	Tue 2/06/26
3189	Flush corridor walls	0%	4 days	Sat 16/05/26	Thu 21/05/26
3190	All 2nd fix fire services cut outs	0%	2 days	Wed 3/06/26	Thu 4/06/26
3191	All 2nd fix mechanical services cut outs	0%	2 days	Wed 3/06/26	Thu 4/06/26
3192	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Wed 3/06/26	Thu 4/06/26
3193	All 2nd fix hydraulic services cut outs	0%	2 days	Wed 3/06/26	Thu 4/06/26
3194	Delivery of all internal timber doors	0%	1 day	Wed 3/06/26	Wed 3/06/26
3195	Complete all 1st coat paining to walls and ceiling	0%	2 days	Wed 3/06/26	Thu 4/06/26
3196	Hang doors and hardware cut outs	0%	4 days	Thu 4/06/26	Thu 11/06/26
3197	Plasterboard defects	0%	1 day	Fri 5/06/26	Fri 5/06/26
3198	Finish coat ceiling	0%	2 days	Wed 10/06/26	Thu 11/06/26
3199	Services trades fit off ceiling	0%	3 days	Fri 12/06/26	Mon 15/06/26
3200	Joinery Site Mobilisation and Install	0%	3 days	Wed 17/06/26	Sat 20/06/26
3201	Measure and book install for all stone tops	0%	2 wks	Sat 20/06/26	Fri 3/07/26
3202	Install Bench tops	0%	1 day	Fri 3/07/26	Sat 4/07/26
3203	Measure and install all glass splash backs	0%	2 wks	Sat 4/07/26	Fri 17/07/26
3204	Install splashback	0%	1 day	Fri 17/07/26	Sat 18/07/26
3205	Floor prep	0%	3 days	Fri 19/06/26	Tue 23/06/26

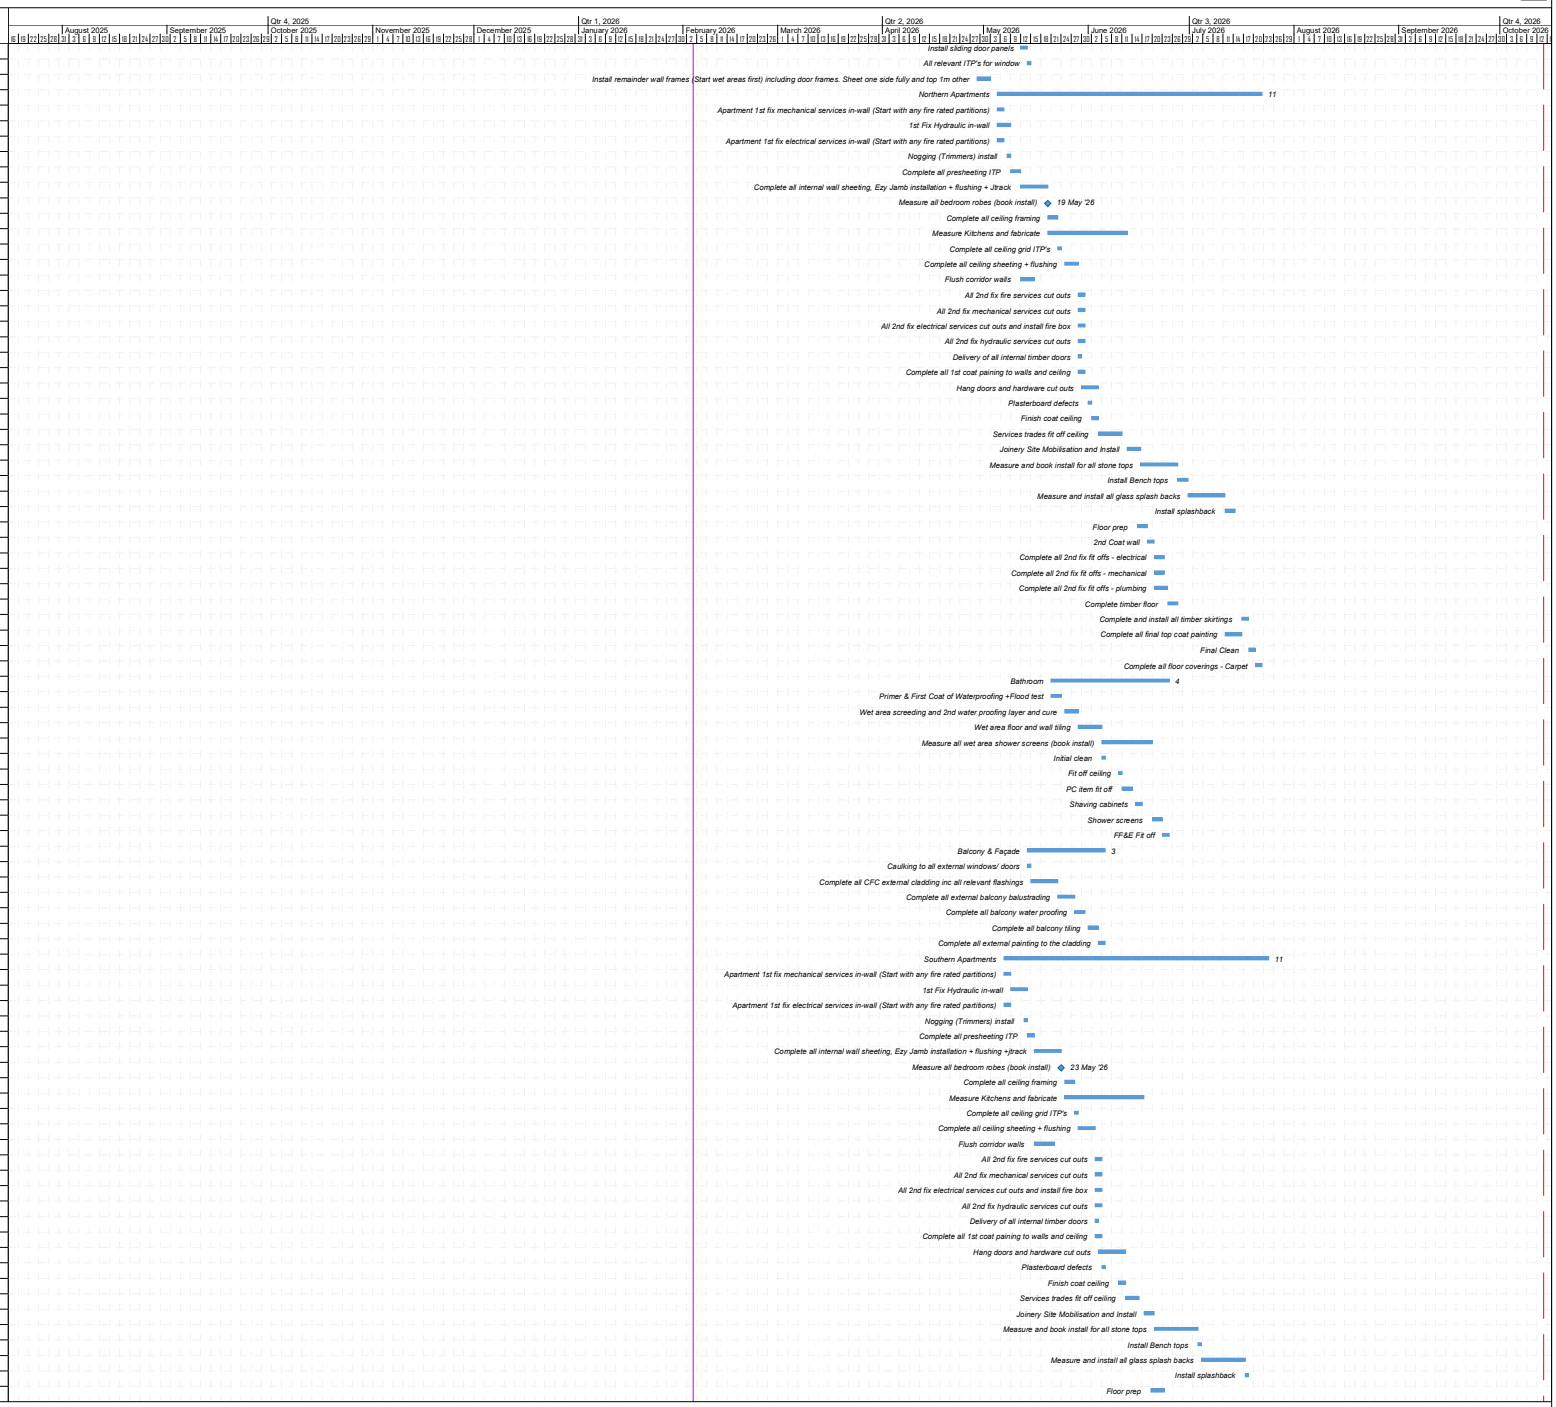

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

Planner: **Steve Church** Review: **Marcus Anderson**

ID	Name	% Complete	Duration	Start	Finish
3206	2nd Coat wall	0%	2 days	Tue 23/06/26	Thu 25/06/26
3207	Complete all 2nd fix fit offs - electrical	0%	2 days	Thu 25/06/26	Sat 27/06/26
3208	Complete all 2nd fix fit offs - mechanical	0%	2 days	Thu 25/06/26	Sat 27/06/26
3209	Complete all 2nd fix fit offs - plumbing	0%	3 days	Thu 25/06/26	Tue 30/06/26
3210	Complete Timber Flooring	0%	3 days	Tue 30/06/26	Fri 3/07/26
3211	Complete and install all timber skirtings	0%	2 days	Tue 7/07/26	Thu 9/07/26
3212	Complete all final top coat painting	0%	3 days	Fri 3/07/26	Tue 7/07/26
3213	Final Clean	0%	1 day	Sat 18/07/26	Mon 20/07/26
3214	Complete all floor coverings - Carpet	0%	2 days	Wed 22/07/26	Fri 24/07/26
3215	**Bathroom**	**0%**	**27 days**	**Tue 26/05/26**	**Tue 30/06/26**
3216	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Tue 26/05/26	Thu 28/05/26
3217	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Fri 29/05/26	Tue 2/06/26
3218	Wet area floor and wall tiling	0%	6 days	Wed 3/06/26	Fri 12/06/26
3219	Measure all wet area shower screens (book install)	0%	2 wks	Sat 13/06/26	Wed 24/06/26
3220	Initial clean	0%	1 day	Sat 13/06/26	Sat 13/06/26
3221	Fit off ceiling	0%	1 day	Mon 15/06/26	Mon 15/06/26
3222	PC item fit off	0%	3 days	Tue 16/06/26	Thu 18/06/26
3223	Shaving cabinets	0%	2 days	Fri 19/06/26	Sat 20/06/26
3224	Shower screens	0%	2 days	Thu 25/06/26	Fri 26/06/26
3225	FF&E Fit off	0%	2 days	Sat 27/06/26	Tue 30/06/26
3226	**Balcony & Façade**	**0%**	**19 days**	**Thu 14/05/26**	**Fri 5/06/26**
3227	Caulking to all external windows/ doors	0%	1 day	Thu 14/05/26	Thu 14/05/26
3228	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Fri 15/05/26	Fri 22/05/26
3229	Complete all external balcony balustrading	0%	4 days	Sat 23/05/26	Wed 27/05/26
3230	Complete all balcony water proofing	0%	3 days	Thu 28/05/26	Sat 30/05/26
3231	Complete all balcony tiling	0%	3 days	Mon 1/06/26	Wed 3/06/26
3232	Complete all external painting to the cladding	0%	2 days	Thu 4/06/26	Fri 5/06/26
3233	**Common Area (Corridors)**	**0%**	**68.5 days**	**Fri 22/05/26**	**Tue 18/08/26**
3234	Prime walls	0%	1 day	Fri 22/05/26	Fri 22/05/26
3235	Ceiling framing	0%	2 days	Sat 20/06/26	Tue 23/06/26
3236	Services and Ceiling Closeout ITP	0%	1 day	Tue 23/06/26	Wed 24/06/26
3237	Sheet and Flush Ceiling	0%	4 days	Wed 24/06/26	Tue 30/06/26
3238	Cut out ceilign services	0%	1 day	Tue 30/06/26	Wed 1/07/26
3239	2nd Coat wall and Finish coat ceiling	0%	3 days	Wed 1/07/26	Sat 4/07/26
3240	Complete all 2nd fix fit offs - fire	0%	2 days	Sat 4/07/26	Tue 7/07/26
3241	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 4/07/26	Tue 7/07/26
3242	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 4/07/26	Tue 7/07/26
3243	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 4/07/26	Wed 8/07/26
3244	Complete all final top coat painting	0%	3 days	Wed 8/07/26	Sat 11/07/26
3245	Complete all floor coverings - Timber	0%	3 days	Sat 11/07/26	Thu 16/07/26
3246	Complete all floor coverings - Carpet	0%	2 days	Fri 24/07/26	Tue 28/07/26
3247	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 28/07/26	Thu 30/07/26
3248	**Inspection Activities**	**0%**	**15 days**	**Thu 30/07/26**	**Tue 18/08/26**
3249	Defect Inspection & Rectification	0%	4 days	Thu 30/07/26	Tue 4/08/26
3250	Testing and commissioning to all L4	0%	1 day	Tue 4/08/26	Wed 5/08/26
3251	Contingency	0%	10 days	Wed 5/08/26	Tue 18/08/26
3252	**FITOUT PENTHOUSE**	**0%**	**92.5 days**	**Sat 18/04/26**	**Mon 17/08/26**
3253	**Overall Floor**	**0%**	**22 days**	**Sat 18/04/26**	**Sat 16/05/26**
3254	**High level services**	**0%**	**12 days**	**Sat 18/04/26**	**Tue 5/05/26**
3255	Bianco to clear slab (Acrow Props only)	0%	2 days	Sat 18/04/26	Mon 20/04/26
3256	Rectify all wet area concrete defects if not completed by Ultra Built	0%	3 days	Tue 21/04/26	Thu 23/04/26
3257	Precast Caulking/ Grout complete	0%	0 days	Thu 23/04/26	Thu 23/04/26
3258	Delivery of stud works + Entry door frames	0%	0 days	Thu 23/04/26	Thu 23/04/26
3259	Set out Wall frames	0%	4 days	Thu 23/04/26	Wed 29/04/26
3260	Delivery of all windows	0%	0 days	Fri 24/04/26	Fri 24/04/26
3261	Apartment 1st fix fire services high level	0%	4 days	Thu 23/04/26	Wed 29/04/26
3262	Apartment 1st fix Hydraulic services high level (stacks/ corridors?)	0%	4 days	Tue 28/04/26	Fri 1/05/26
3263	Apartment 1st fix mechanical services high level	0%	4 days	Thu 30/04/26	Tue 5/05/26
3264	**External Perimeter Framing and Windows (Overall floor)**	**0%**	**16 days**	**Tue 28/04/26**	**Sat 16/05/26**
3265	Install external/corridor stud framing +Sheet moisture resistant plasterboard externally	0%	3 days	Tue 28/04/26	Thu 30/04/26
3266	Intello wrap install	0%	1 day	Fri 1/05/26	Fri 1/05/26
3267	Setdown Membrane for balconies (additional day to cure inclusive)	0%	3 days	Fri 1/05/26	Tue 5/05/26
3268	Install F channel for Balustrade	0%	4 days	Wed 6/05/26	Sat 9/05/26
3269	Delivery of plasterboard	0%	0 days	Sat 2/05/26	Sat 2/05/26
3270	Delivery of Door frame ready on site	0%	0 days	Fri 1/05/26	Fri 1/05/26
3271	Install window subframes (start with precast)	0%	4 days	Wed 6/05/26	Sat 9/05/26
3272	Subframe flood test sign off	0%	1 day	Mon 11/05/26	Mon 11/05/26
3273	Install window panels	0%	2 days	Tue 12/05/26	Wed 13/05/26
3274	Install Subsill/head for Sliding doors	0%	2 days	Fri 8/05/26	Sat 9/05/26
3275	Subsil flood test sign off	0%	1 day	Mon 11/05/26	Mon 11/05/26
3276	Install sliding door panels	0%	2 days	Thu 14/05/26	Fri 15/05/26
3277	All relevant ITP's for window	0%	1 day	Sat 16/05/26	Sat 16/05/26
3278	Install remainder wall frames (Start wet areas first) including door frames. Sheet one side ful	0%	4 days	Fri 1/05/26	Wed 6/05/26
3279	**Northern Apartments**	**0%**	**59 days**	**Thu 7/05/26**	**Tue 21/07/26**
3280	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 7/05/26	Fri 8/05/26
3281	1st Fix Hydraulic in-wall	0%	4 days	Thu 7/05/26	Mon 11/05/26
3282	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Thu 7/05/26	Fri 8/05/26
3283	Nogging (Trimmers) install	0%	1 day	Mon 11/05/26	Mon 11/05/26
3284	Complete all presheeting ITP	0%	2 days	Tue 12/05/26	Wed 13/05/26
3285	Complete all internal wall sheeting, Ezy Jamb installation + flushing + jtrack	0%	6 days	Thu 14/05/26	Thu 21/05/26
3286	Measure all bedroom robes (book install)	0%	0 days	Thu 21/05/26	Thu 21/05/26
3287	Complete all ceiling framing	0%	3 days	Fri 22/05/26	Mon 25/05/26
3288	Measure Kitchens and fabricate	0%	17 days	Fri 22/05/26	Sat 13/06/26
3289	Complete all ceiling grid ITP's	0%	1 day	Tue 26/05/26	Tue 26/05/26
3290	Complete all ceiling sheeting + flushing	0%	4 days	Wed 27/05/26	Sat 30/05/26
3291	Flush corridor walls	0%	4 days	Thu 14/05/26	Tue 19/05/26
3292	All 2nd fix fire services cut outs	0%	2 days	Mon 1/06/26	Tue 2/06/26
3293	All 2nd fix mechanical services cut outs	0%	2 days	Mon 1/06/26	Tue 2/06/26

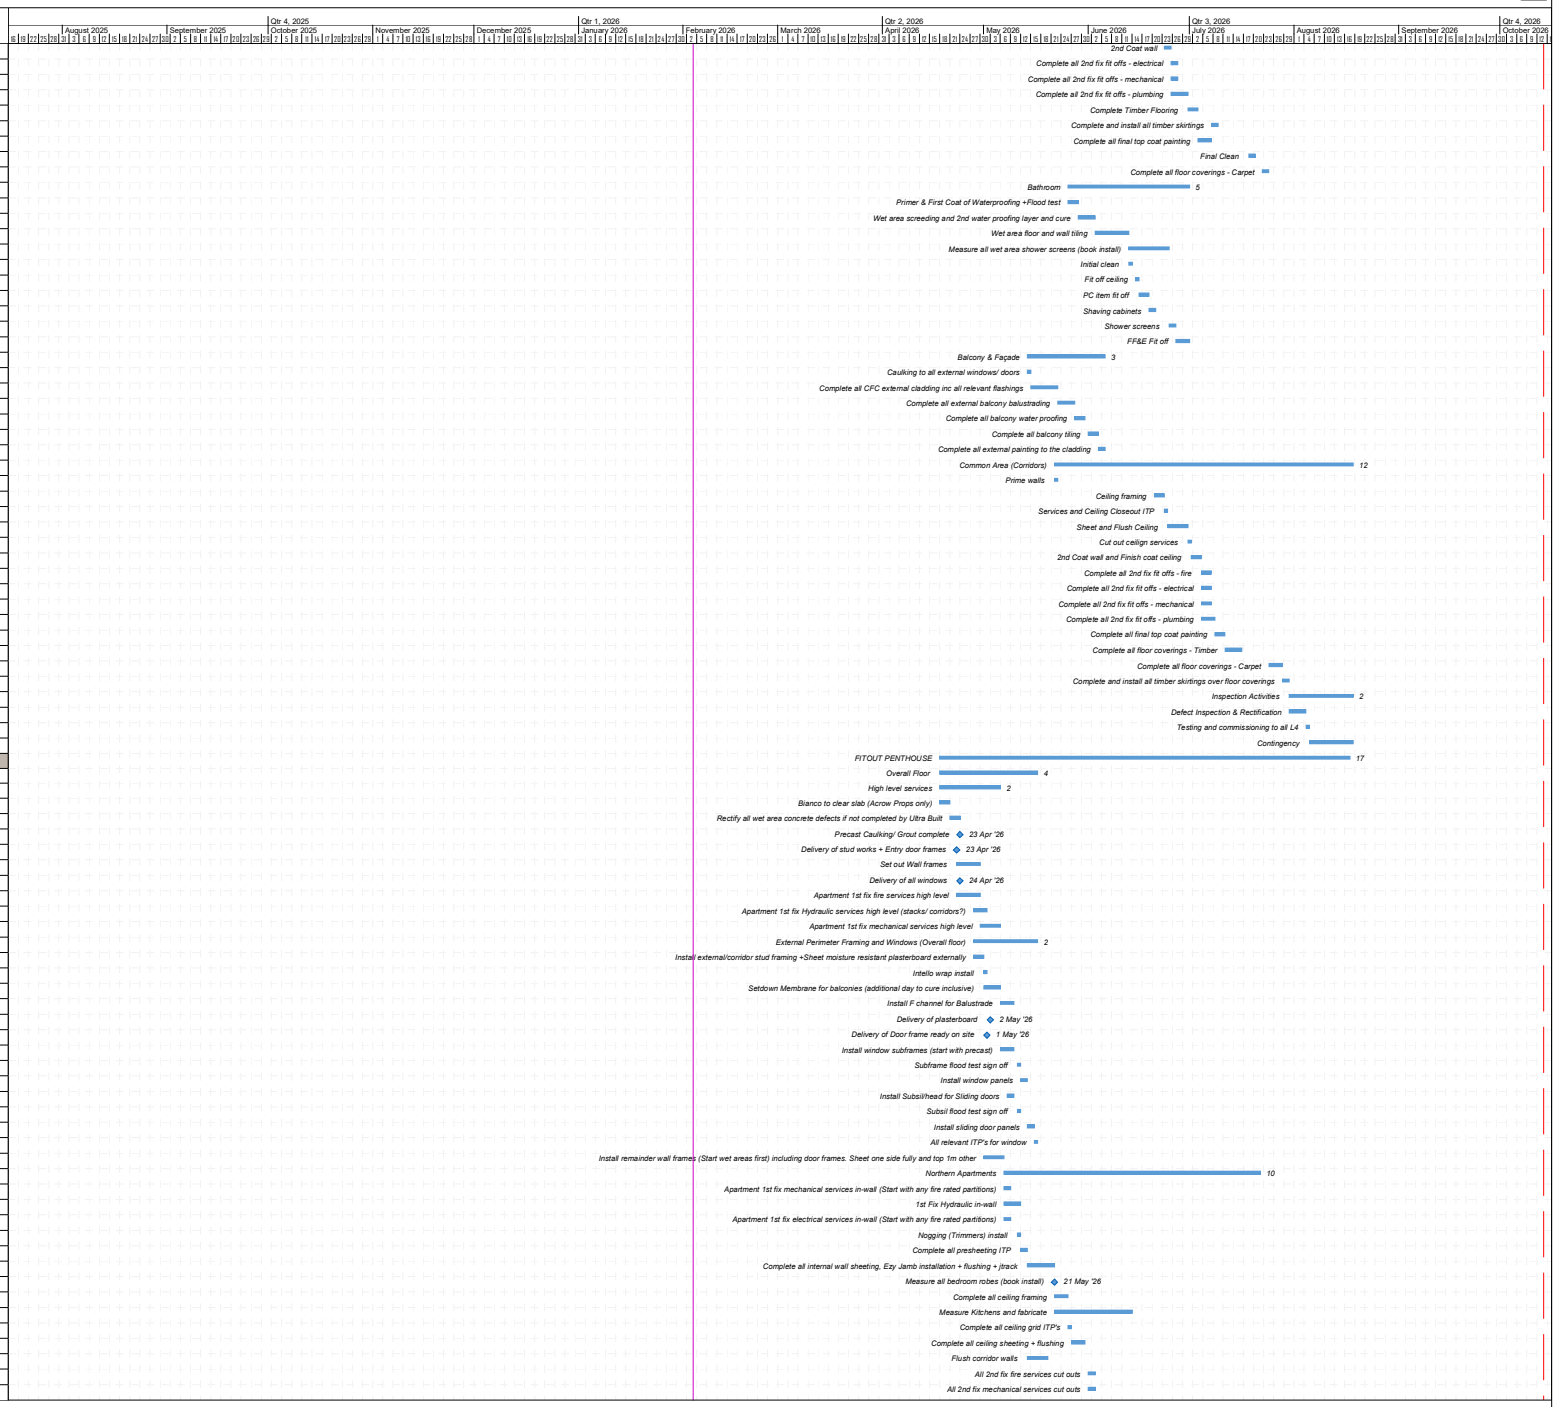

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
3294	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Mon 1/06/26	Tue 2/06/26
3295	All 2nd fix hydraulic services cut outs	0%	2 days	Mon 1/06/26	Tue 2/06/26
3296	Delivery of all internal timber doors	0%	1 day	Mon 1/06/26	Mon 1/06/26
3297	Complete all 1st coat paining to walls and ceiling	0%	2 days	Mon 1/06/26	Tue 2/06/26
3298	Hang doors and hardware cut outs	0%	4 days	Tue 2/06/26	Fri 5/06/26
3299	Plasterboard defects	0%	1 day	Wed 3/06/26	Wed 3/06/26
3300	Finish coat ceiling	0%	2 days	Thu 4/06/26	Fri 5/06/26
3301	Services trades fit off ceiling	0%	3 days	Wed 10/06/26	Fri 12/06/26
3302	Joinery Site Mobilisation and Install	0%	4 days	Mon 15/06/26	Thu 18/06/26
3303	Measure and book install for all stone tops	0%	10 days	Fri 19/06/26	Wed 1/07/26
3304	Install Bench tops	0%	1 day	Thu 2/07/26	Thu 2/07/26
3305	Measure and install all glass splash backs	0%	10 days	Fri 3/07/26	Wed 15/07/26
3306	Install splashback	0%	1 day	Thu 16/07/26	Thu 16/07/26
3307	Floor prep	0%	3 days	Thu 18/06/26	Sat 20/06/26
3308	2nd Coat wall	0%	2 days	Mon 22/06/26	Tue 23/06/26
3309	Complete all 2nd fix fit offs - electrical	0%	2 days	Wed 24/06/26	Thu 25/06/26
3310	Complete all 2nd fix fit offs - mechanical	0%	2 days	Wed 24/06/26	Thu 25/06/26
3311	Complete all 2nd fix fit offs - plumbing	0%	3 days	Wed 24/06/26	Fri 26/06/26
3312	Complete timber floor	0%	4 days	Sat 27/06/26	Thu 2/07/26
3313	Complete and install all timber skirtings	0%	2 days	Fri 3/07/26	Sat 4/07/26
3314	Complete all final top coat painting	0%	3 days	Thu 16/07/26	Sat 18/07/26
3315	Final Clean	0%	1 day	Fri 17/07/26	Fri 17/07/26
3316	Complete all floor coverings - Carpet	0%	3 days	Sat 18/07/26	Tue 21/07/26
3317	**Bathroom**	**0%**	**27 days**	**Sat 23/05/26**	**Fri 26/06/26**
3318	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Sat 23/05/26	Tue 26/05/26
3319	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Wed 27/05/26	Sat 30/05/26
3320	Wet area floor and wall tiling	0%	6 days	Mon 1/06/26	Wed 10/06/26
3321	Measure all wet area shower screens (book install)	0%	10 days	Thu 11/06/26	Mon 22/06/26
3322	Initial clean	0%	1 day	Thu 11/06/26	Thu 11/06/26
3323	Fit off ceiling	0%	1 day	Fri 12/06/26	Fri 12/06/26
3324	PC item fit off	0%	3 days	Sat 13/06/26	Tue 16/06/26
3325	Shaving cabinets	0%	2 days	Wed 17/06/26	Thu 18/06/26
3326	Shower screens	0%	2 days	Tue 23/06/26	Wed 24/06/26
3327	FF&E Fit off	0%	2 days	Thu 25/06/26	Fri 26/06/26
3328	**Balcony & Façade**	**0%**	**19 days**	**Sat 16/05/26**	**Thu 11/06/26**
3329	Caulking to all external windows/ doors	0%	1 day	Sat 16/05/26	Sat 16/05/26
3330	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Tue 19/05/26	Mon 25/05/26
3331	Complete all external balcony balustrading	0%	4 days	Tue 26/05/26	Fri 29/05/26
3332	Complete all balcony water proofing	0%	3 days	Sat 30/05/26	Tue 2/06/26
3333	Complete all balcony tiling	0%	3 days	Wed 3/06/26	Fri 5/06/26
3334	Complete all external painting to the cladding	0%	2 days	Wed 10/06/26	Thu 11/06/26
3335	**Southern Apartments**	**0%**	**59.5 days**	**Sat 9/05/26**	**Fri 24/07/26**
3336	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 9/05/26	Mon 11/05/26
3337	1st Fix Hydraulic in-wall	0%	4 days	Tue 12/05/26	Fri 15/05/26
3338	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Sat 9/05/26	Mon 11/05/26
3339	Nogging (Trimmers) install	0%	1 day	Fri 15/05/26	Fri 15/05/26
3340	Complete all presheeting ITP	0%	2 days	Sat 16/05/26	Tue 19/05/26
3341	Complete all internal wall sheeting, Ezy Jamb installation + flushing + J track	0%	6 days	Wed 20/05/26	Tue 26/05/26
3342	Measure all bedroom robes (book install)	0%	0 days	Tue 26/05/26	Tue 26/05/26
3343	Complete all ceiling framing	0%	3 days	Wed 27/05/26	Fri 29/05/26
3344	Measure Kitchens and fabricate	0%	3.5 wks	Wed 27/05/26	Fri 19/06/26
3345	Complete all ceiling grid ITP's	0%	1 day	Sat 30/05/26	Sat 30/05/26
3346	Complete all ceiling sheeting + flushing	0%	4 days	Mon 1/06/26	Thu 4/06/26
3347	Flush corridor walls	0%	4 days	Wed 20/05/26	Sat 23/05/26
3348	All 2nd fix fire services cut outs	0%	2 days	Fri 5/06/26	Wed 10/06/26
3349	All 2nd fix mechanical services cut outs	0%	2 days	Fri 5/06/26	Wed 10/06/26
3350	All 2nd fix electrical services cut outs and install fire box	0%	2 days	Fri 5/06/26	Wed 10/06/26
3351	All 2nd fix hydraulic services cut outs	0%	2 days	Fri 5/06/26	Wed 10/06/26
3352	Delivery of all internal timber doors	0%	1 day	Fri 5/06/26	Fri 5/06/26
3353	Complete all 1st coat paining to walls and ceiling	0%	2 days	Fri 5/06/26	Wed 10/06/26
3354	Hang doors and hardware cut outs	0%	4 days	Wed 10/06/26	Sat 13/06/26
3355	Plasterboard defects	0%	1 day	Thu 11/06/26	Thu 11/06/26
3356	Finish coat ceiling	0%	2 days	Fri 12/06/26	Sat 13/06/26
3357	Services trades fit off ceiling	0%	3 days	Mon 15/06/26	Wed 17/06/26
3358	Joinery Site Mobilisation and Install	0%	3 days	Fri 19/06/26	Tue 23/06/26
3359	Measure and book install for all stone tops	0%	2 wks	Tue 23/06/26	Mon 6/07/26
3360	Install Bench tops	0%	1 day	Mon 6/07/26	Tue 7/07/26
3361	Measure and install all glass splash backs	0%	2 wks	Tue 7/07/26	Mon 20/07/26
3362	Install splashback	0%	1 day	Mon 20/07/26	Tue 21/07/26
3363	Floor prep	0%	3 days	Mon 22/06/26	Thu 25/06/26
3364	2nd Coat wall	0%	2 days	Thu 25/06/26	Sat 27/06/26
3365	Complete all 2nd fix fit offs - electrical	0%	2 days	Sat 27/06/26	Wed 1/07/26
3366	Complete all 2nd fix fit offs - mechanical	0%	2 days	Sat 27/06/26	Wed 1/07/26
3367	Complete all 2nd fix fit offs - plumbing	0%	3 days	Sat 27/06/26	Thu 2/07/26
3368	Complete Timber Flooring	0%	3 days	Thu 2/07/26	Mon 6/07/26
3369	Complete and install all timber skirtings	0%	2 days	Thu 9/07/26	Sat 11/07/26
3370	Complete all final top coat painting	0%	3 days	Mon 6/07/26	Thu 9/07/26
3371	Final Clean	0%	1 day	Tue 21/07/26	Wed 22/07/26
3372	Complete all floor coverings - Carpet	0%	2 days	Wed 22/07/26	Fri 24/07/26
3373	**Bathroom**	**0%**	**27 days**	**Thu 28/05/26**	**Thu 2/07/26**
3374	Primer & First Coat of Waterproofing +Flood test	0%	3 days	Thu 28/05/26	Sat 30/05/26
3375	Wet area screeding and 2nd water proofing layer and cure	0%	4 days	Mon 1/06/26	Thu 4/06/26
3376	Wet area floor and wall tiling	0%	6 days	Fri 5/06/26	Mon 15/06/26
3377	Measure all wet area shower screens (book install)	0%	2 wks	Tue 16/06/26	Fri 26/06/26
3378	Initial clean	0%	1 day	Tue 16/06/26	Tue 16/06/26
3379	Fit off ceiling	0%	1 day	Wed 17/06/26	Wed 17/06/26
3380	PC item fit off	0%	3 days	Thu 18/06/26	Sat 20/06/26
3381	Shaving cabinets	0%	2 days	Mon 22/06/26	Tue 23/06/26

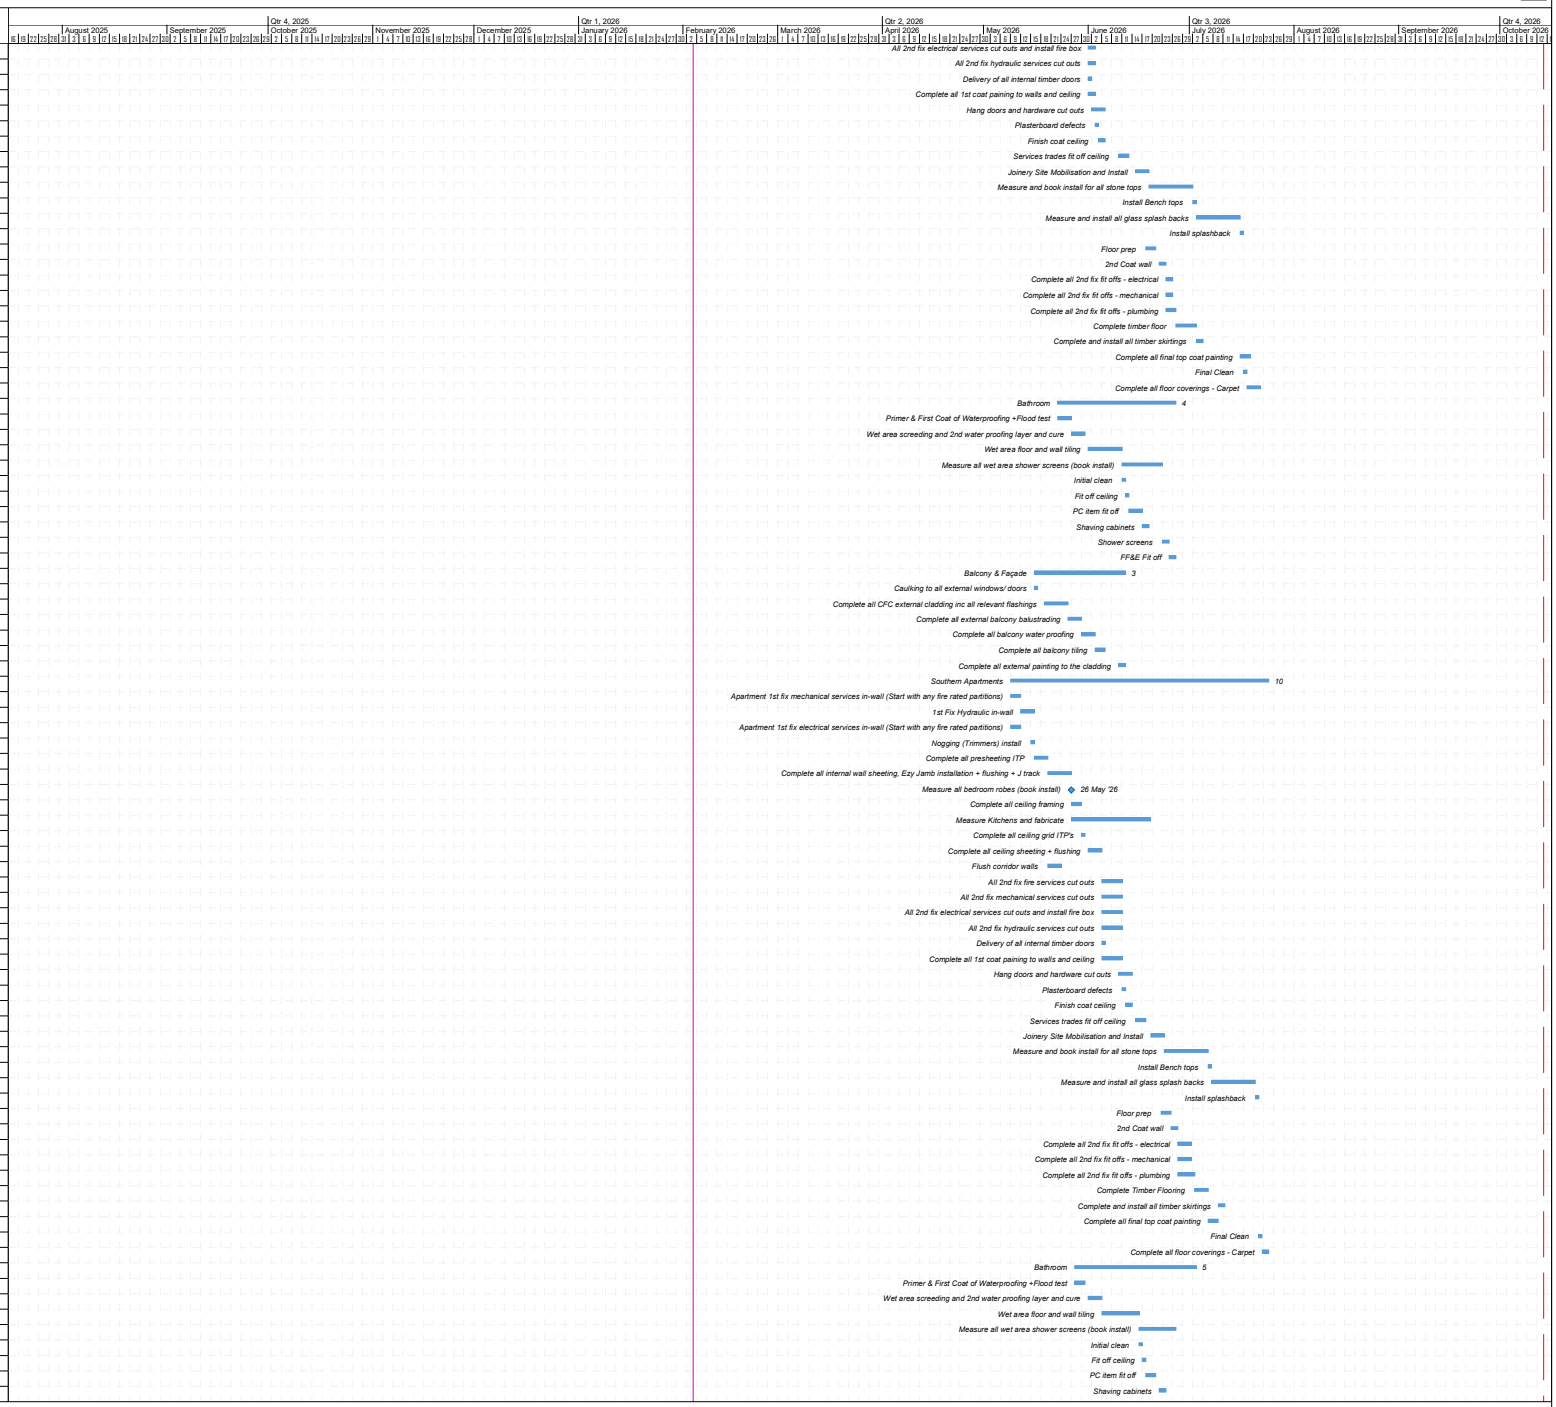

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones

ID	Name	% Complete	Duration	Start	Finish
3382	Shower screens	0%	2 days	Sat 27/06/26	Tue 30/06/26
3383	FF&E Fit off	0%	2 days	Wed 1/07/26	Thu 2/07/26
3384	**Balcony & Façade**	**0%**	**19 days**	**Sat 16/05/26**	**Thu 11/06/26**
3385	Caulking to all external windows/ doors	0%	1 day	Sat 16/05/26	Sat 16/05/26
3386	Complete all CFC external cladding inc all relevant flashings	0%	6 days	Tue 19/05/26	Mon 25/05/26
3387	Complete all external balcony balustrading	0%	4 days	Tue 26/05/26	Fri 29/05/26
3388	Complete all balcony water proofing	0%	3 days	Sat 30/05/26	Tue 2/06/26
3389	Complete all balcony tiling	0%	3 days	Wed 3/06/26	Fri 5/06/26
3390	Complete all external painting to the cladding	0%	2 days	Wed 10/06/26	Thu 11/06/26
3391	**Common Area (Corridors)**	**0%**	**65.5 days**	**Mon 25/05/26**	**Mon 17/08/26**
3392	Prime walls	0%	1 day	Mon 25/05/26	Mon 25/05/26
3393	Ceiling framing	0%	2 days	Tue 23/06/26	Thu 25/06/26
3394	Services and Ceiling Closeout ITP	0%	1 day	Thu 25/06/26	Fri 26/06/26
3395	Sheet and Flush Ceiling	0%	4 days	Fri 26/06/26	Thu 2/07/26
3396	Cut out ceilign services	0%	1 day	Thu 2/07/26	Fri 3/07/26
3397	2nd Coat wall and Finish coat ceiling	0%	3 days	Fri 3/07/26	Tue 7/07/26
3398	Complete all 2nd fix fit offs - fire	0%	2 days	Tue 7/07/26	Thu 9/07/26
3399	Complete all 2nd fix fit offs - electrical	0%	2 days	Tue 7/07/26	Thu 9/07/26
3400	Complete all 2nd fix fit offs - mechanical	0%	2 days	Tue 7/07/26	Thu 9/07/26
3401	Complete all 2nd fix fit offs - plumbing	0%	3 days	Tue 7/07/26	Fri 10/07/26
3402	Complete all final top coat painting	0%	3 days	Fri 10/07/26	Wed 15/07/26
3403	Complete all floor coverings - Timber	0%	3 days	Wed 15/07/26	Sat 18/07/26
3404	Complete all floor coverings - Carpet	0%	2 days	Fri 24/07/26	Tue 28/07/26
3405	Complete and install all timber skirtings over floor coverings	0%	2 days	Tue 28/07/26	Thu 30/07/26
3406	**Inspection Activities**	**0%**	**14 days**	**Thu 30/07/26**	**Mon 17/08/26**
3407	Defect Inspection & Rectification	0%	4 days	Thu 30/07/26	Tue 4/08/26
3408	Testing and commissioning to all L4	0%	1 day	Wed 5/08/26	Thu 6/08/26
3409	Contingency	0%	8 days	Thu 6/08/26	Mon 17/08/26
3410	HOIST APARTMENTS (LEVEL 3 TO 11)	0%	40 days	Thu 25/06/26	Fri 14/08/26
3411	**Apartments**	**0%**	**40 days**	**Thu 25/06/26**	**Fri 14/08/26**
3412	**High level services**	**0%**	**10 days**	**Thu 25/06/26**	**Tue 7/07/26**
3413	Install Stud Framing. Sheet 1 Side Fire Walls	0%	2 days	Thu 25/06/26	Fri 26/06/26
3414	Apartment 1st fix fire services high level	0%	2 days	Sat 27/06/26	Tue 30/06/26
3415	Apartment 1st fix Hydraulic services high level	0%	2 days	Wed 1/07/26	Thu 2/07/26
3416	Apartment 1st fix mechanical services high level	0%	2 days	Fri 3/07/26	Sat 4/07/26
3417	Apartment 1st fix electrical services high level	0%	2 days	Mon 6/07/26	Tue 7/07/26
3418	**General Area**	**0%**	**32 days**	**Mon 6/07/26**	**Fri 14/08/26**
3419	Apartment 1st fix mechanical services in-wall (Start with any fire rated partitions)	0%	2 days	Mon 6/07/26	Tue 7/07/26
3420	1st Fix Hydraulic in-wall	0%	4 days	Wed 8/07/26	Sat 11/07/26
3421	Apartment 1st fix electrical services in-wall (Start with any fire rated partitions)	0%	2 days	Tue 14/07/26	Wed 15/07/26
3422	Complete all services ITP's - high level & In-wall	0%	1 day	Thu 16/07/26	Thu 16/07/26
3423	Install Intello Vapour Barrier to external precast partitions and sarking to lightweight external	0%	1 day	Fri 17/07/26	Fri 17/07/26
3424	All relevant ITP's for window/ door install	0%	1 day	Sat 18/07/26	Sat 18/07/26
3425	Complete all services ITP's wall framing	0%	1 day	Mon 20/07/26	Mon 20/07/26
3426	Install all internal steel door frames	0%	2 days	Tue 21/07/26	Wed 22/07/26
3427	Complete all internal wall frame sheeting, Ezy Jamb installation + flushing	0%	4 days	Thu 23/07/26	Tue 28/07/26
3428	Complete all ceiling framing	0%	2 days	Tue 28/07/26	Wed 29/07/26
3429	Complete all ceiling sheeting + flushing	0%	3 days	Wed 29/07/26	Fri 31/07/26
3430	All 2nd fix fire services cut outs	0%	1 day	Sat 1/08/26	Sat 1/08/26
3431	All 2nd fix mechanical services cut outs	0%	1 day	Sat 1/08/26	Sat 1/08/26
3432	All 2nd fix electrical services cut outs	0%	1 day	Sat 1/08/26	Sat 1/08/26
3433	All 2nd fix hydraulic services cut outs	0%	1 day	Sat 1/08/26	Sat 1/08/26
3434	Measure all bedroom robes (book install)	0%	1 day	Mon 3/08/26	Mon 3/08/26
3435	Delivery of all internal timber doors	0%	1 day	Mon 3/08/26	Mon 3/08/26
3436	Complete all 1st coat paining to walls and complete all ceiling paint	0%	1 day	Tue 4/08/26	Tue 4/08/26
3437	Complete all 2nd fix carpentry inc doors and hardware cut outs	0%	2 days	Tue 4/08/26	Wed 5/08/26
3438	Joinery Site Mobilisation and Install	0%	2 days	Tue 4/08/26	Wed 5/08/26
3439	Measure and book install for all stone tops	0%	1 day	Thu 6/08/26	Thu 6/08/26
3440	Measure and install all glass splash backs	0%	1 day	Fri 7/08/26	Fri 7/08/26
3441	Complete all floor coverings - Timber	0%	1 day	Sat 8/08/26	Sat 8/08/26
3442	Complete all floor coverings - Carpet	0%	1 day	Tue 11/08/26	Tue 11/08/26
3443	Complete and install all timber skirtings over floor coverings	0%	1 day	Wed 12/08/26	Wed 12/08/26
3444	Complete all 2nd fix fit offs - electrical	0%	1 day	Thu 13/08/26	Thu 13/08/26
3445	Complete all 2nd fix fit offs - mechanical	0%	1 day	Thu 13/08/26	Thu 13/08/26
3446	Complete all 2nd fix fit offs - plumbing	0%	1 day	Thu 13/08/26	Thu 13/08/26
3447	Complete all final top coat painting	0%	2 days	Thu 13/08/26	Fri 14/08/26
3448	**Bathroom**	**0%**	**9 days**	**Tue 4/08/26**	**Fri 14/08/26**
3449	Primer & First Coat of Waterproofing	0%	1 day	Tue 4/08/26	Tue 4/08/26
3450	Wet area screeding and 2nd water proofing layer + flood tests	0%	2 days	Thu 6/08/26	Fri 7/08/26
3451	Wet area floor and wall tiling	0%	4 days	Sat 8/08/26	Thu 13/08/26
3452	Measure all wet area shower screens (book install)	0%	1 day	Fri 14/08/26	Fri 14/08/26
3453	**Balcony & Façade**	**0%**	**20 days**	**Thu 25/06/26**	**Mon 20/07/26**
3454	Waterproofing to all external balconies before window subs are installed	0%	2 days	Thu 25/06/26	Fri 26/06/26
3455	Installation of sarking to balcony walls, returning into the jamb	0%	1 day	Sat 27/06/26	Sat 27/06/26
3456	Delivery and installation of all aluminium sub framing	0%	2 days	Tue 30/06/26	Wed 1/07/26
3457	Caulking to all external windows/ doors	0%	1 day	Thu 2/07/26	Thu 2/07/26
3458	Deliver and install of aluminium window panels	0%	1 day	Fri 3/07/26	Fri 3/07/26
3459	Complete all CFC external cladding inc all relevant flashings	0%	4 days	Sat 4/07/26	Wed 8/07/26
3460	Complete all external balcony balustrading	0%	3 days	Thu 9/07/26	Sat 11/07/26
3461	Complete all balcony water proofing	0%	2 days	Tue 14/07/26	Wed 15/07/26
3462	Complete all balcony tiling	0%	2 days	Thu 16/07/26	Fri 17/07/26
3463	Complete all external painting to the cladding	0%	2 days	Sat 18/07/26	Mon 20/07/26
3464	VERTICAL TRANSPORTATION	0%	105 days	Mon 30/03/26	Mon 17/08/26
3465	Lift WORKS GF - Level 11	0%	105 days	Mon 30/03/26	Mon 17/08/26
3466	Lift Shaft complete	0%	0 days	Mon 30/03/26	Mon 30/03/26
3467	Clean / Builder's Works to Lift Shaft @ 1d/Level	0%	10 days	Tue 31/03/26	Wed 15/04/26
3468	Install Builder's Lift @ 4d/ level	0%	48 days	Thu 16/04/26	Thu 18/06/26
3469	Permanent Power Available	0%	0 days	Thu 18/06/26	Thu 18/06/26
3470	Test & Commission @ .5d/Level	0%	5 days	Fri 19/06/26	Wed 24/06/26
3471	Builders Lift Ready	0%	0 days	Wed 24/06/26	Wed 24/06/26
3472	Lift Complete and Operational As Builders Lift	0%	33 days	Thu 25/06/26	Wed 5/08/26

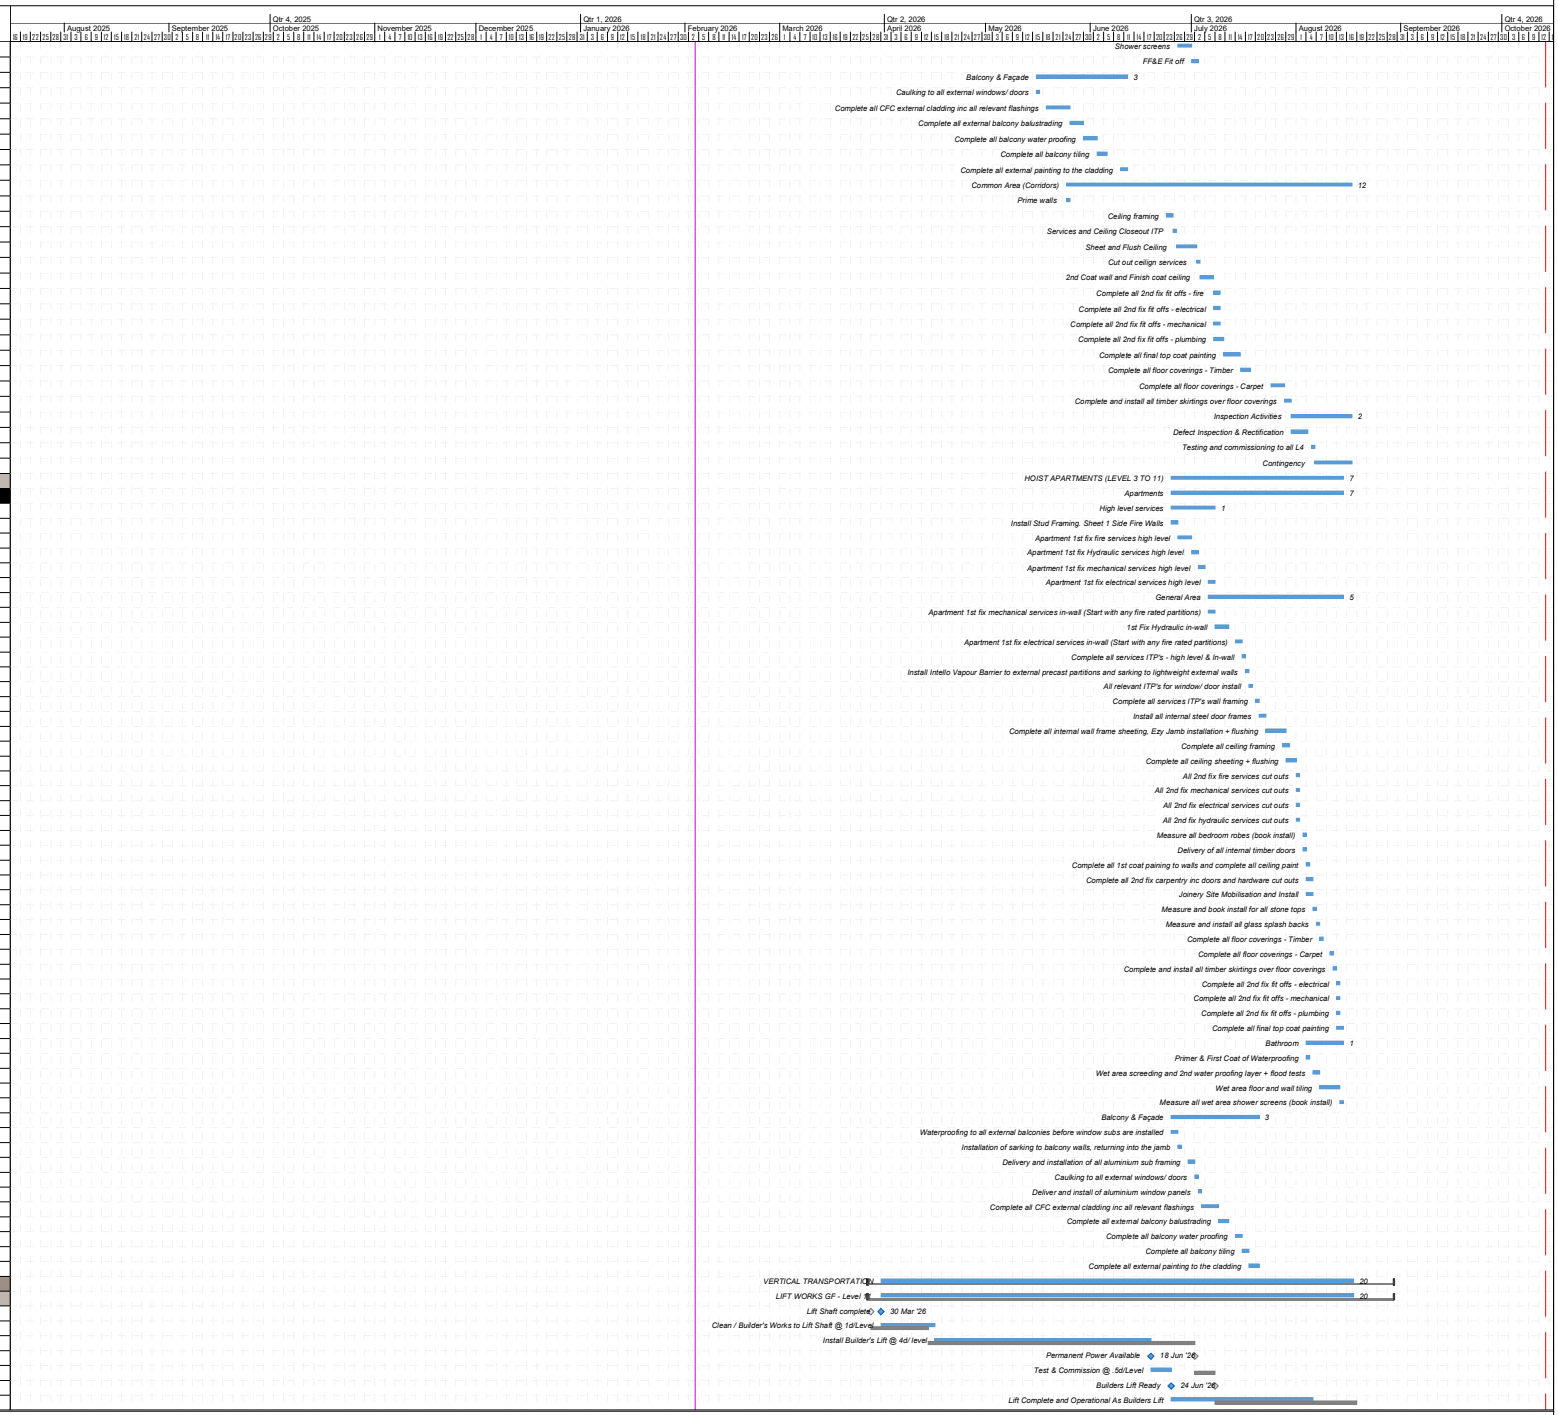

ARC BOWDEN 6D/W

Bowden Lot 33 and 34

FITOUT PROGRAM - All Tasks

HINDMARSH 45 YEARS

ID	Name	% Complete	Duration	Start	Finish
3473	Recommission Lift 1	0%	5 days	Thu 6/08/26	Wed 12/08/26
3474	Recommission Lift 2	0%	4 days	Thu 13/08/26	Mon 17/08/26
3475	PODIUM SLAB INFILL	0%	13 days	Wed 24/06/26	Fri 10/07/26
3476	Hoist off site following Builders Lift Ready	0%	0 days	Wed 24/06/26	Wed 24/06/26
3477	FRP GF infill	0%	2 days	Sat 27/06/26	Tue 30/06/26
3478	FRP Level 1	0%	3 days	Wed 1/07/26	Fri 3/07/26
3479	FRP Level 2	0%	3 days	Sat 4/07/26	Tue 7/07/26
3480	FRP Level 3	0%	3 days	Wed 8/07/26	Fri 10/07/26
3481	Infill works complete	0%	0 days	Fri 10/07/26	Fri 10/07/26
3482	EXTERNAL WORKS	0%	73 days	Sat 16/05/26	Wed 19/08/26
3483	PUBLIC DOMAIN	0%	73 days	Sat 16/05/26	Wed 19/08/26
3484	**Perimeter External Canopies**	**0%**	**22 days**	**Fri 29/05/26**	**Fri 26/06/26**
3485	**Park Terrace Canopy**	**0%**	**10 days**	**Sat 30/05/26**	**Sat 13/06/26**
3486	Survey and install the wall connections	0%	1 day	Sat 30/05/26	Sat 30/05/26
3487	Install steel canopy with the use of small crane	0%	1 day	Mon 1/06/26	Mon 1/06/26
3488	Install roof sheeting to steel canopy	0%	1 day	Tue 2/06/26	Tue 2/06/26
3489	Install services to steel canopy	0%	1 day	Wed 3/06/26	Wed 3/06/26
3490	Install soffit to canopy	0%	2 days	Thu 4/06/26	Fri 5/06/26
3491	Second fix services to canopy soffit	0%	1 day	Wed 10/06/26	Wed 10/06/26
3492	Paint canopy soffit	0%	3 days	Thu 11/06/26	Sat 13/06/26
3493	Complete	0%	0 days	Sat 13/06/26	Sat 13/06/26
3494	**Fourth Street Canopy**	**0%**	**12 days**	**Mon 1/06/26**	**Wed 17/06/26**
3495	Survey and install the wall connections	0%	1 day	Mon 1/06/26	Mon 1/06/26
3496	Install steel canopy with the use of small crane	0%	2 days	Tue 2/06/26	Wed 3/06/26
3497	Install roof sheeting to steel canopy	0%	1 day	Wed 3/06/26	Wed 3/06/26
3498	Install services to steel canopy	0%	1 day	Thu 4/06/26	Thu 4/06/26
3499	Install soffit to canopy	0%	2 days	Wed 10/06/26	Thu 11/06/26
3500	Second fix services to canopy soffit	0%	1 day	Thu 11/06/26	Thu 11/06/26
3501	Paint canopy soffit	0%	3 days	Mon 15/06/26	Wed 17/06/26
3502	Complete	0%	0 days	Wed 17/06/26	Wed 17/06/26
3503	**Fifth Street Canopy**	**0%**	**22 days**	**Fri 29/05/26**	**Fri 26/06/26**
3504	Prep civil levels	0%	3 days	Sat 30/05/26	Tue 2/06/26
3505	Dig footings / piles for steel canopy columns/ posts	0%	2 days	Fri 29/05/26	Sat 30/05/26
3506	Survey and install the wall connections	0%	1 day	Tue 2/06/26	Tue 2/06/26
3507	Install steel canopy with the use of small crane	0%	4 days	Thu 4/06/26	Thu 11/06/26
3508	Install roof sheeting to steel canopy	0%	3 days	Fri 12/06/26	Mon 15/06/26
3509	Install services to steel canopy	0%	2 days	Tue 16/06/26	Wed 17/06/26
3510	Install soffit to canopy	0%	3 days	Thu 18/06/26	Sat 20/06/26
3511	Second fix services to canopy soffit	0%	1 day	Mon 22/06/26	Mon 22/06/26
3512	Paint canopy soffit	0%	3 days	Tue 23/06/26	Thu 25/06/26
3513	Install roof safety access ladder bracket	0%	1 day	Fri 26/06/26	Fri 26/06/26
3514	Complete	0%	0 days	Fri 26/06/26	Fri 26/06/26
3515	**Landscaping**	**0%**	**73 days**	**Sat 16/05/26**	**Wed 19/08/26**
3516	Start Public Domain Works after Scaffold Down to Podium L3	0%	0 days	Sat 16/05/26	Sat 16/05/26
3517	FRP Retaining Walls / External Steps / Paths / Stairs Etc	0%	25 days	Tue 19/05/26	Fri 19/06/26
3518	Hard Landscaping / Fencing & Gates	0%	30 days	Fri 26/06/26	Mon 3/08/26
3519	Soft Landscaping / Planting	0%	18 days	Thu 16/07/26	Thu 6/08/26
3520	Signage / External FF & E / Make Good	0%	12 days	Wed 29/07/26	Wed 12/08/26
3521	Defect Inspections & Rectification	0%	6 days	Thu 13/08/26	Wed 19/08/26
3522	Public Domain Works complete	0%	0 days	Wed 19/08/26	Wed 19/08/26
3523	L3 OUTDOOR COMMUNAL SPACE	0%	39 days	Fri 26/06/26	Fri 14/08/26
3524	Start External Works after Podium Infill complete after Scaffold Down	0%	0 days	Fri 26/06/26	Fri 26/06/26
3525	**Perimeter External Canopies**	**0%**	**13 days**	**Fri 26/06/26**	**Sat 11/07/26**
3526	**Fifth Street Canopy**	**0%**	**13 days**	**Fri 26/06/26**	**Sat 11/07/26**
3527	Set out canopy steel	0%	1 day	Fri 26/06/26	Fri 26/06/26
3528	Install canopy steel with use of TC	0%	2 days	Sat 27/06/26	Tue 30/06/26
3529	Install roof sheeting to canopy	0%	1 day	Wed 1/07/26	Wed 1/07/26
3530	Water proofing to canopy posts	0%	2 days	Thu 2/07/26	Fri 3/07/26
3531	Install cladding to canopy	0%	3 days	Sat 4/07/26	Tue 7/07/26
3532	Install services to canopy	0%	1 day	Wed 8/07/26	Wed 8/07/26
3533	Painting to canopy (if required)	0%	3 days	Thu 9/07/26	Sat 11/07/26
3534	Complete	0%	0 days	Sat 11/07/26	Sat 11/07/26
3535	FRP Retaining Walls / Bench to Required Levels	0%	16 days	Fri 26/06/26	Thu 16/07/26
3536	Hard Landscaping / Fencing & Gates	0%	15 days	Thu 9/07/26	Tue 28/07/26
3537	Soft Landscaping / Planting	0%	10 days	Wed 29/07/26	Sat 8/08/26
3538	Signage / External FF & E / Make Good	0%	5 days	Tue 4/08/26	Sat 8/08/26
3539	Defect Inspections & Rectification	0%	4 days	Tue 11/08/26	Fri 14/08/26
3540	L3 OUTDOOR COMMUNAL SPACE complete	0%	0 days	Fri 14/08/26	Fri 14/08/26
3541	External Works complete	0%	0 days	Wed 19/08/26	Wed 19/08/26
3542	COMMISSIONING & HANDOVER	0%	35 days	Sat 18/07/26	Mon 31/08/26
3543	Start Overall Completion after Fitout & External Works complete	0%	0 days	Wed 19/08/26	Wed 19/08/26
3544	Overall Testing & Commissioning / Defect Rectification Works	0%	12 days	Tue 11/08/26	Tue 25/08/26
3545	Handover Manuals / As-Built Documentation / Certificates / Keys	0%	30 days	Sat 18/07/26	Tue 25/08/26
3546	Inspections & Obtain Certificate of Occupancy	0%	24 days	Sat 25/07/26	Tue 25/08/26
3547	Staff Training	0%	24 days	Sat 25/07/26	Tue 25/08/26
3548	Dismantle Site Hoarding / Temp. Services Etc.	0%	18 days	Mon 3/08/26	Tue 25/08/26
3549	Strata Survey	0%	6 days	Tue 18/08/26	Tue 25/08/26
3550	Commissioning & Handover	0%	5 days	Wed 26/08/26	Mon 31/08/26
3551	**COMPLETION**	**0%**	**0 days**	**Mon 31/08/26**	**Mon 31/08/26**
3552	NETT Target Completion	0%	0 days	Mon 31/08/26	Mon 31/08/26

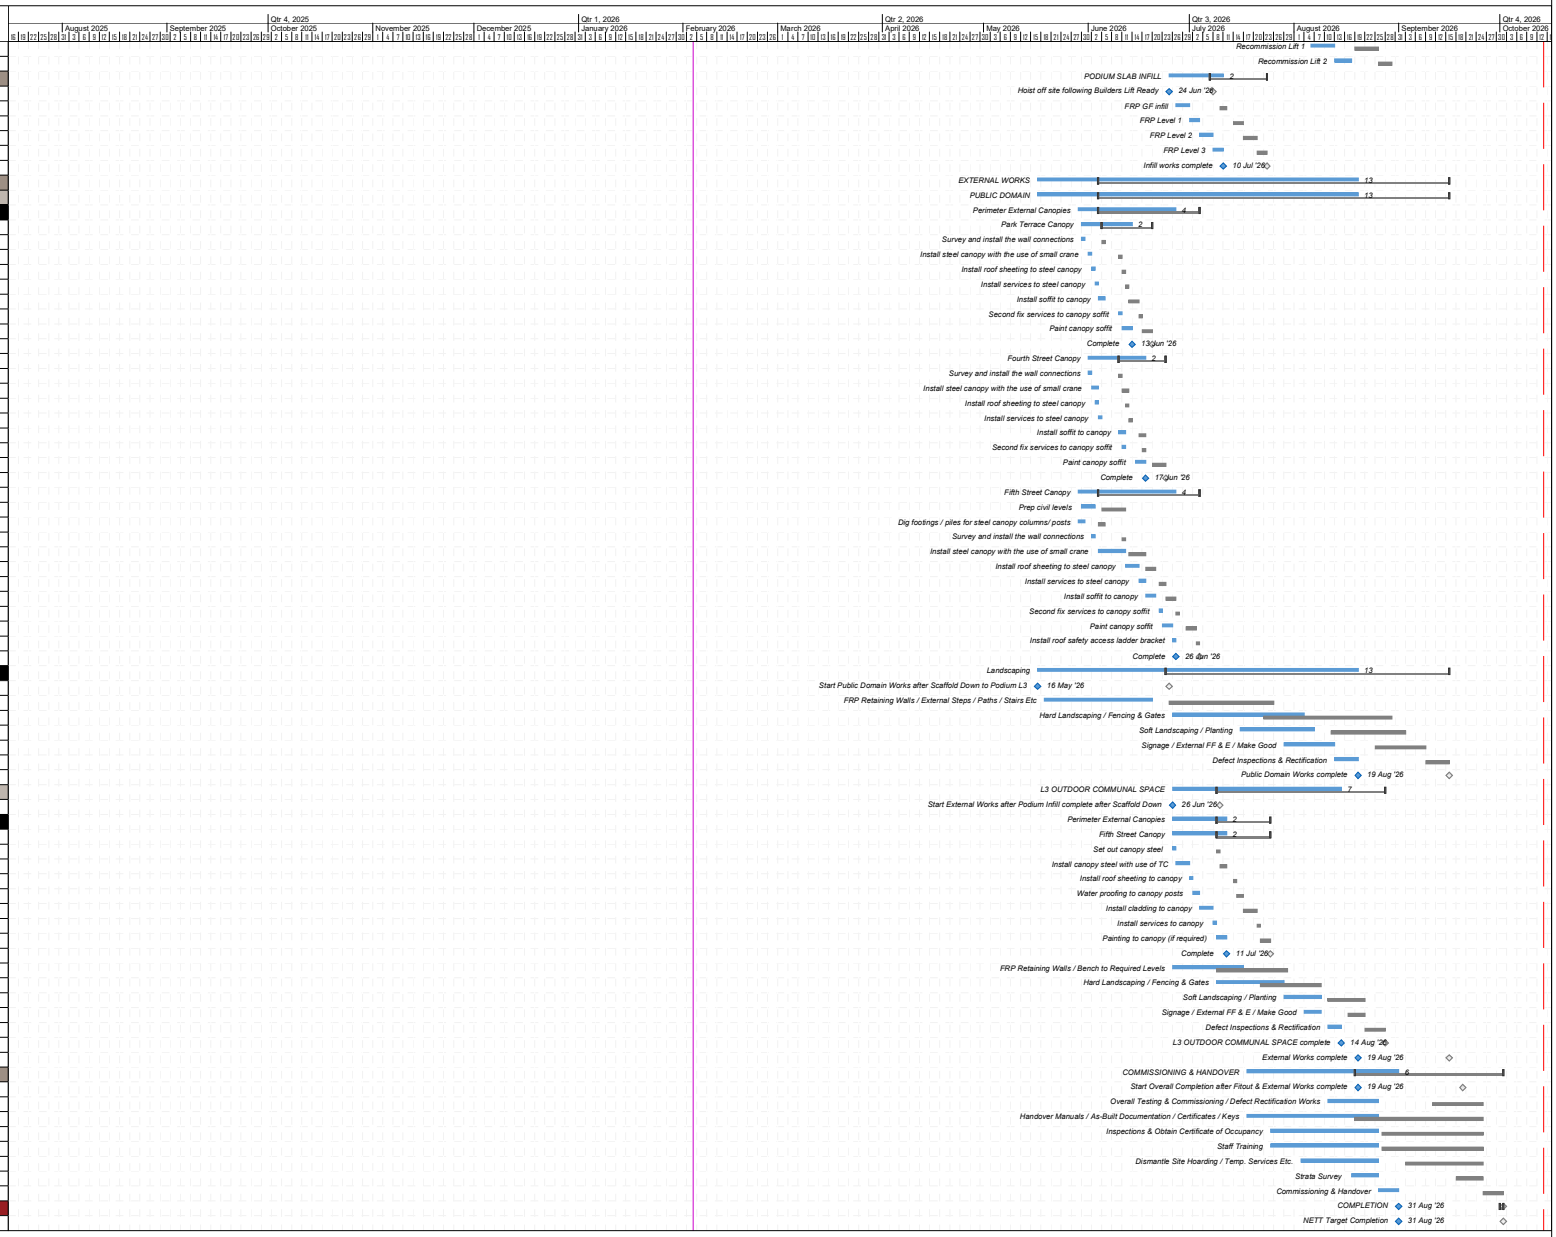

Revision : 20260130 - ARC Bowden- v36.1 - Revised Fitout Sequence
Print Date: Tue 3/02/26

Tasks | Summary | Critical Milestone | Client Milestones | Baseline Milestone | Progress
Milestone | Critical | Client Tasks | Baseline | Baseline Summary | Baseline Milestones
